



सत्यमेव जयते

भारत सरकार

Government Of India

विद्युत मंत्रालय

Ministry Of Power

पूर्वी क्षेत्रीय विद्युत समिति

Eastern Regional Power Committee

14 Golf Club Road, Tollygunje-70033 Website: www.erpc.gov.in

NO. ERPC/EE/OPERATION/2023/1280

DATE: 18.12.2023

To

As per list enclosed/ संलग्न सूची के अनुसार

विषय: सुभाषग्राम (पीजी), जीरात (डब्ल्यूबीएसईटीसीएल) और राजारहाट (पीजी) एस/एस से संबंधित परिचालन मुद्दों पर वर्चुअल मोड के माध्यम से 12.12.2023 (मंगलवार) को आयोजित विशेष बैठक का कार्यवृत्त।

Sub: Minutes of special Meeting held on 12.12.2023 (Tuesday) via virtual mode on operational issues related to Subhasgram(PG) and Jeerat(WBSETCL) S/S- reg.

Sir/ महोदय,

कृपया अपनी जानकारी और आवश्यक कार्रवाई के लिए 12.12.2023 (मंगलवार) को वस्तुतः 16:30 बजे माइक्रोसॉफ्ट टीमस प्लेटफॉर्म पर आयोजित विशेष बैठक के संलग्न विवरण देखें। यह ईआरपीसी वेबसाइट (www.erpc.gov.in) पर भी उपलब्ध है।

Please find enclosed minutes of special meeting held on **12.12.2023 (Tuesday)** virtually on Microsoft Teams platform at 16:30 hrs for your kind information and necessary action. The same is also available at ERPC website (www.erpc.gov.in).

टिप्पणियाँ, यदि कोई हों, कृपया यथाशीघ्र इस कार्यालय को अग्रेषित करें।

Observations, if any, may please be forwarded to this office at the earliest.

इसे सदस्य सचिव के अनुमोदन से जारी किया जाता है।

This issues with the approval of Member Secretary.

Regards/ सम्मान,

Yours faithfully/ आपका विश्वासी,

(S.Kejriwal)

SE (Operation)

एसई (ऑपरेशन)

LIST OF ADDRESSES:

1. CHIEF ENGINEER, CPD, WBSETCL
2. CHIEF ENGINEER, SLDC, WEST BENGAL
3. EXECUTIVE DIRECTOR ,POWERGRID, ER-II, KOLKATA
4. EXECUTIVE DIRECTOR, ERLDC, GRID-INDIA, KOLKATA
5. ADDITIONAL CHIEF ENGINEER, WBSEDCL
6. SENIOR MANAGER (SYSTEM OPERATION), CESC

ERPC:: KOLKATA

MoM OF THE 2nd WEEKLY MONITORING MEETING HELD ON 12.12.2023 AT 16:30 HRS VIA VIRTUAL MODE UNDER THE CHAIRMANSHIP OF MEMBER SECRETARY, ERPC TO DISCUSS ONGOING OPERATIONAL ISSUES RELATED TO SUBHASGRAM(PG) AND JEERAT(WBSETCL) S/S

1. Update on installation of 7th (Interim) 500 MVA ICT at 400 Kv Subhasgram(PG):

Deliberation in meeting

The followings were deliberated in the meeting:

- Powergrid ER-II representative presented detailed project bar chart (Gantt Chart) (attached at **Annexure-I**) encompassing timelines of various activities to be carried out for 7th (Interim) 500 MVA ICT installation at Subhasgram(PG).
- It was updated that all blanking plates/bushing end cover have been made ready after availing shutdown of bus reactor w.e.f 06.12.2023 while demolishing of foundation work shall tentatively commence from 14.12.2023.
- Powergrid ER-II representative delivered a concise presentation highlighting description of various activities including Transformer oil draining, reactor accessories dismantling and bushing de-erection, that were carried out as per schedule of project bar chart (Gantt Chart) at Subhasgram(PG) in the last week for 500 MVA(interim) ICT installation. Removal of reactor from plin and commencement of subsequent dismantling work by 15.12.2023 was also updated.
- It was reaffirmed that all works related to 500 MVA ICT installation Subhasgram(PG) have been awarded to concerned contractors except ICT transportation job, whose technical bid shall open on 15.12.2023 and LOA is expected by 25.12.2023 on completion of mandatory formalities.
- On enquiry from ERLDC representative, tentative participation of 3 prospective bidders in the ICT transportation tender was informed by Powergrid ER-II.
- Powergrid ER-II representative intimated of seeking administrative assistance from ERPC for smooth and fast transportation of 500 MVA ICT to Subhasgram(PG), if necessary and the same shall be confirmed in subsequent review meetings.
- ERPC representative requested Powergrid to submit detailed breakup of 40 days expected for ICT transportation job for easy monitoring on regular basis once the transportation process begins.
- Powergrid ER-II representative apprised of seeking administrative assistance in terms of bulky 500 MVA ICT transportation from Secretary(Power), Govt. of West Bengal in a meeting to be convened on 14.12.2023.
- A brief presentation on detailed route survey for 500 MVA ICT transportation from Maithon(PG) S/S was delivered by Powergrid ER-II outlining various constraints like

inappropriate height of advertisement display signages, roadside electrical poles etc. that shall pose hindrance in safe transportation of the bulky ICT. It was affirmed that similar route survey of ICT transportation around Kolaghat and onwards to Subhasgram(PG) shall also be presented by Powergrid ER-II in the next monitoring meeting. Seeking assistance from WBSEDCL in dismantling electrical poles and lines on the way of ICT transportation was also apprised .

- *No observation was received from CESC regarding cost escalation in multi-modal ICT transportation to Subhasgram(PG) as confirmed by Powergrid ER-II.*

Member secretary, ERPC complimented Powergrid ER-II for significant progress on 500 MVA ICT installation activities at Subhasgram(PG) over last week and also advised Powergrid ER-II to focus diligently on executing the ICT transportation process as per submitted timelines.

2. Update on replacement of one 315MVA, 400/220KV ICT from Regional Pool for replacement of one no of defective 315 MVA ICT (4th) at Jeerat 400 KV S/S(WB):

Deliberation in meeting


Powergrid ER-II representative apprised the following:

- *Bushings have already been dismantled for 315 MVA ICT and packing of the same is under process.*
- *Blanking plates shall be provided by Powergrid ER-II while gasket change to be carried out by WBSETCL.*
- *Sufficient quantity of transformer oil possessing good breakdown voltage characteristics shall be handed over by Powergrid ER-II to WBSETCL along with the ICT.*
- *Complete unpacking and packing of 315 MVA ICT from Malda(PG) S/S shall take minimum 10 days, thus the same needs to be commenced by WBSETCL hired contractors at the earliest.*
- *It was apprised that prior to handing over Powergrid asset to WBSETCL , an MOU needs to be signed between Powergrid ER-II and WBSETCL underlining relevant terms and conditions. The MOU is presently under vetting of Law department of Powergrid, which shall be thereafter shared with WBSETCL positively by 14.12.2023 for due consent and authorized signatory.*
- *The MOU, however, shall not pose any immediate hindrance in lifting of the 315 MVA ICT by WBSETCL but at the same time this MOU needs to be signed on behalf of WBSETCL at the earliest as per asset transfer norms of Powergrid.*

WBSETCL representative affirmed the following:

- *MOU regarding 315 MVA ICT from Regional pool to Jeerat(WBSETCL) shall be submitted with authorized signatory on behalf of WBSETCL at the earliest, once it is received from Powergrid ER-II.*
- *WBSETCL hired contractors shall reach Malda(PG) S/S on 13.12.2023 for carrying out necessary activities for shifting of the 315 MVA ICT from Malda(PG) to 400 kV Jeerat(WBSETCL) S/S .*

Annexure-I

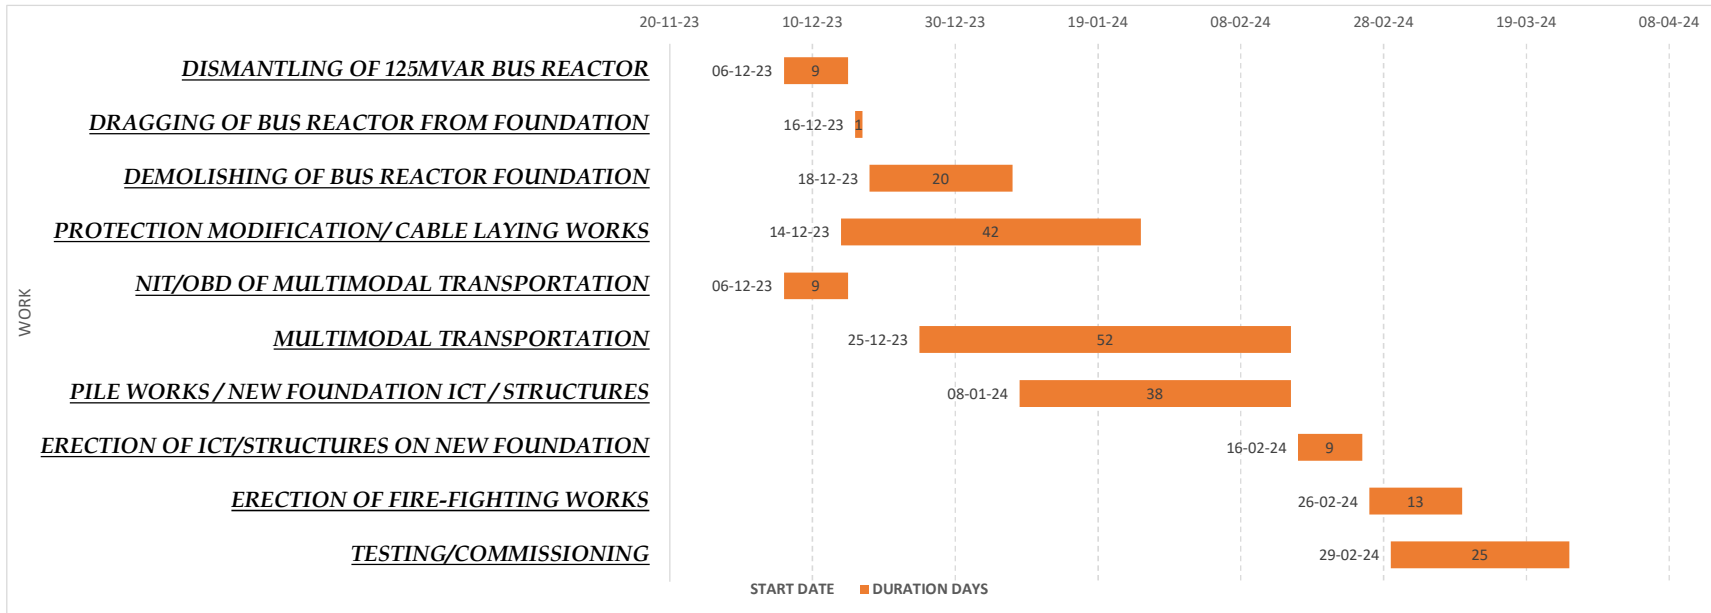

Annexure-II**LIST OF PARTICIPANTS**

Name	First Join	Last Leave	In-Meeting Duration	Email	Role
ERPC Kolkata	12/12/23, 4:24:41 PM	12/12/23, 5:07:41 PM	43m	ERPC@KolkataMST.onmicrosoft.com	Organizer
N S MONDAL (Guest)	12/12/23, 4:24:46 PM	12/12/23, 5:07:38 PM	42m 51s		Presenter
Debarshi De (CESC) (Guest)	12/12/23, 4:26:39 PM	12/12/23, 5:07:35 PM	40m 56s		Presenter
shouvik banerjee	12/12/23, 4:26:40 PM	12/12/23, 5:07:34 PM	40m 53s		Presenter
CE CPD WBSETCL	12/12/23, 4:27:20 PM	12/12/23, 5:07:47 PM	40m 27s		Presenter
Saurav Kr Sahay	12/12/23, 4:28:10 PM	12/12/23, 5:07:38 PM	39m 28s	saurav.sahay@erldc.onmicrosoft.com	Presenter
Partha Ghosh (पार्थ घोष)	12/12/23, 4:29:23 PM	12/12/23, 5:07:34 PM	38m 11s	partha.ghosh@powergrid.in	Presenter
S.KEJRIWAL	12/12/23, 4:30:07 PM	12/12/23, 5:07:40 PM	37m 33s		Presenter
Shouvik Banerjee	12/12/23, 4:32:16 PM	12/12/23, 4:32:56 PM	39s		Presenter
WB SLDC	12/12/23, 4:34:46 PM	12/12/23, 5:07:52 PM	33m 6s		Presenter
S Konar	12/12/23, 4:34:53 PM	12/12/23, 5:07:41 PM	32m 48s		Presenter
CE CPD WBSETCL	12/12/23, 4:37:26 PM	12/12/23, 5:07:50 PM	30m 23s		Presenter
Nitin K Shrivastava (एन.के. श्रीवास्तव)	12/12/23, 4:39:54 PM	12/12/23, 5:05:26 PM	25m 32s	nkshrivastava@powergrid.in	Presenter
Priyam Maity (प्रियम मैती)	12/12/23, 4:42:55 PM	12/12/23, 4:54:09 PM	11m 14s	pmaity@powergrid.in	Presenter
