

### भारत सरकार विद्युत मंत्रालय पूर्वी क्षेत्रीय विद्युत समिति



### **GOVERNMENT OF INDIA** MINISTRY OF POWER

### EASTERN REGIONAL POWER COMMITTEE

No. ERPC/TCC&Committee/14/2017/ 2385 - 2454 Date: 28<sup>th</sup> March 2017

To:

- 1. Members of Eastern Regional Power Committee.
- 2. Members of TCC.

Subject: Minutes of 35th ERPC & TCC Meetings.

Sir.

The minutes of the 35th TCC & ERPC meetings held on 24th & 25th February 2017 respectively at Ranchi have been issued and uploaded on www.erpc.gov.in. As per the decision of ERPC distribution of hard copies of the Minutes of Meeting has been discontinued as a Go Green initiative.

Yours faithfully,

(A.K. Bandyopadhyay) Member Secretary

Encl. As above.

### Distribution: ERPC Members

- Chairperson, ERPC & Chairman-cum- Managing Director, Bihar State Power Holding Company Ltd., Vidyut Bhavan, Bailey Road, Patna-800021.
- Managing Director, Bihar State Power Transmission Company Limited, Vidyut Bhavan, Bailey Road, Patna-800021.
- Managing Director, South Bihar Power Distribution Company Limited, Vidyut Bhavan, Bailey Road, Patna-800021.
- Chairman & Managing Director, West Bengal State Electricity Distribution Company Ltd., Vidyut Bhavan, 7<sup>th</sup> Floor, Block-DJ, Sector-II, Bidhannagar, Kolkata-700091.
- Managing Director, West Bengal State Electricity Transmission Company Ltd., Vidyut Bhavan, 8th Floor, Block-DJ, Sector-II, Bidhannagar, Kolkata-700091.
- Chairman & Managing Director, West Bengal Power Development Corporation Ltd., Bidyut Unnayan Bhavan, 3/C, Block LA, Sector-III, Bidhannagar, Kolkata-700098.
- Managing Director, Durgapur Projects Ltd., Administrative Building, Durgapur-713201, West Bengal.
- Principal Chief Engineer-cum-Secretary, Energy & Power Department, Govt. of Sikkim, Kazi Road, Gangtok – 737101, Sikkim.
- Chairman-cum-Managing Director, Odisha Power Transmission Corporation Ltd., Janpath, Bhubaneswar - 751022.
- 10. Chairman-cum-Managing Director, GRIDCO Ltd., Janpath, Bhubaneshwar-751022.
- Chairman-cum-Managing Director, OHPC Ltd., Orissa State Police Housing & Welfare Corporation Bldg. Vanivihar, Janpath, Bhubaneswar- 751022.
- Managing Director, OPGC Ltd., Zone-A, 7<sup>th</sup> Floor, Fortune Towers, Chandrasekharpur, Bhubaneswar-751023.
- Chairman & Managing Director, Jharkhand Urja Vikas Nigam Limited, Engineering Building, HEC, Dhurwa, Ranchi-834004.
- Managing Director, Jharkhand Urja Sancharan Nigam Limited, Engineering Building, HEC, Dhurwa, Ranchi-834004.
- Managing Director, Jharkhand Bijli Vitaran Nigam Limited, Engineering Building, HEC, Dhurwa, Ranchi-834004.
- 16. Managing Director, Tenughat Vidyut Nigam Ltd., Hinoo, Doranda, Ranchi 834002
- 17. Chairman, Damodar Valley Corporation, DVC Towers, VIP Road, Kolkata -700054.
- 18. Member (GO&D), Central Electricity Authority, Sewa Bhawan . R.K. Puram, New Delhi-110066.
- 19. Director (Commercial), NTPC Ltd., Core-7, SCOPE Complex, Lodhi Road, New Delhi -110003.
- 20. Director (Finance), NHPC Ltd., NHPC Office Complex, Sector-33, Faridabad, Haryana-121003.
- Director (Operations), Power Grid Corporation of India Ltd., Saudamini, Plot No. 2, Sector-29, Gurgaon-122001.
- 22. General Manager, ERLDC, POSOCO, 14 Golf Club Road, Tollygunge, Kolkata 700033.
- Chief Executive Officer, POSOCO, National Load Dispatch Center, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi-110016.
- 24. Director (C&O), PTC India Ltd., 2<sup>nd</sup> floor, NBCC Tower,15 Bhikaji Cama Place, New Delhi-110066.
- Chief Executive Officer, NTPC Vidyut Vyapar Nigam Limited, SCOPE Complex, Core-3, 7<sup>th</sup> Floor, Lodhi Road, New Delhi-110003.
- Managing Director, Tata Power Trading Company Limited, B12/13, 2<sup>nd</sup> Floor, Shatabdi Bhavan, Sector-4, Noida-201301, Uttar Pradesh.
- 27. Managing Director, CESC Ltd., CESC House, I Chowringhee Square, Kolkata-700001.
- Chief Executive Officer, Maithon Power Ltd., MA-5, Gogna Colony, P.O.-Maithon Dam, Dist.-Dhanbad, Jharkhand-828207.
- Managing Director, Adhunik Power & Natural Resources Ltd., Lansdowne Towers, 5th Floor, 2/1A Sarat Bose Road, Kolkata-700020.
- 30. Chief Operating Officer, 4x600 MW IPP, Vedanta Ltd., Bhurkahamunda, P.O.-Sripura, Jharsiuguda, Odisha-768202.
- 31. Chief Operating Officer, GMR Kamalanga Energy Ltd., 29 Satyanagar, Bhubaneswar-751007.
- President & Director (Projects), Gati Infrastructure Private Limited, 14/19/2 Old Delhi Gurgaon Road, Opposite Heera Public School, Samalkha, New Delhi-110037.
- Chief Executive Officer, Jindal India Thermal Power Limited, Plot No-12, Sector-B1, Local Shopping Complex, Vasant Kunj, New Delhi-110070.
- 34. Chairman & Managing Director, Dans Energy Private Limited, 5<sup>th</sup> Floor, Building No.8, Tower-C, DLF Cyber City, Phase-II, Gurgaon-12202, Haryana.

### **Distribution: TCC Members**

- Chairperson, TCC & Director (Project), Bihar State Power Transmission Company Limited, Vidyut Bhavan, Bailey Road, Patna-800021.
- Chief Engineer (Commercial), Bihar State Power Holding Company Ltd., Vidyut Bhavan, Bailey Road, Patna-800021.
- Director (Project), South Bihar Power Distribution Company Limited, Vidyut Bhavan, Bailey Road, Patna-800021.
- Director (Operations), West Bengal State Electricity Transmission Company Ltd., Vidyut Bhavan, 8<sup>th</sup> Floor, Block-DJ, Sector-II, Bidhannagar, Kolkata-700091.
- Director (R&T), West Bengal State Electricity Distribution Company Ltd., Vidyut Bhavan, 7<sup>th</sup> Floor, Block-DJ, Sector-II, Bidhannagar, Kolkata-700091.
- Director (O&M), WBPDCL, Bidyut Unnayan Bhavan, 3C, Block-LA, Sector-III, Bidhannagar, Kolkata-700098.
- General Manager I/C (Corporate Technical), Durgapur Projects Ltd., Administrative Building, Durgapur-713201, West Bengal.
- Principal Chief Engineer (HQ), Energy & Power Dept., Govt. of Sikkim, Kazi Road, Gangtok-737101.
- Chief General Manager (O&M), Odisha Power Transmission Corporation Ltd., Janpath. Bhubaneswar - 751022.
- 10. Director (Commercial), GRIDCO Ltd., Janpath, Bhubaneswar-751022.
- Director (Operation), Orissa Power Generation Corporation Ltd, Zone-A, 7<sup>th</sup> floor, Fortune Towers, Chandrasekharpur, Bhubaneswar-751023.
- Director (Operation), Orissa Hydro Power Corporation Ltd, Orissa State Police Housing & Welfare Corporation Building, Vanivihar Chowk, Janpath, Bhubaneswar-751022.
- Chairman & Managing Director, Jharkhand Urja Vikas Nigam Limited, Engineering Building, HEC, Dhurwa, Ranchi-834004.
- Chief Engineer (Trans. O&M), Jharkhand Urja Sancharan Nigam Limited , Engineering Building, HEC, Dhurwa, Ranchi-834004.
- Managing Director, Jharkhand Bijli Vitaran Nigam Limited, Engineering Building, HEC, Dhurwa, Ranchi-834004.
- 16. General Manager, Tenughat TPS, Lalpania, Dist-Bokaro, Jharkhand-829149.
- Executive Director (Commercial), Damodar Valley Corporation, DVC Tower, VIP Road, Kolkata-700054
- 18. Chief Engineer (GM), CEA, Sewa Bhawan, R.K. Puram, New Delhi-110066.
- 19. Regional Executive Director (ER-I), NTPC Ltd., 2<sup>nd</sup> floor, Lok Nayak Jai Prakash Bhawan, Dak Bunglow Chowk, Patna-800001.
- Regional Executive Director (ER-II), NTPC Ltd., 3<sup>rd</sup> Floor, OLIC Building, Plot No.N-17/2, Nayapalli, Bhubaneswar-751012.
- Executive Director (O&M), NHPC Ltd., NHPC Office Complex, Sector-33, Faridabad-121003, Haryana.
- Executive Director (ER-I), Power Grid Corporation of India Ltd, Alankar Place, Boring Road, Patna-800001.
- 23. Executive Director (ER-II), Power Grid Corporation of India Ltd, CF-17, Action Area-I, Newtown, Rajarhat, Near Axis Mall, Kolkata-700091.
- 24. General Manager, ERLDC, POSOCO, 14 Golf Club Road, Kolkata -700 033.
- Chief Executive Officer, POSOCO, National Load Dispatch Center, B-9 Qutab Institutional Area, Katwaria Sarai, New Delhi-110016.
- Executive Director (Marketing), PTC India Ltd., NBCC Tower, 15 Bhikaji Cama Place, New Delhi-110066.
- General Manager (BD), NTPC Vidyut Vyapar Nigam Limited, SCOPE Complex, Core-3, 7<sup>th</sup> Floor, Lodhi Road, New Delhi-110003.
- 28. The Head (Marketing), Tata Power Trading Company Limited, B-12/13, 2<sup>nd</sup> Floor, Shatabdi Bhavan, Sector-4, Noida-201301, Uttar Pradesh.
- 29. Executive Director (CS & SO), CESC Ltd, CESC House, 1 Chowringhee Square, Kolkata-700001.
- Station Head & General Manager (O&M), Maithon Power Ltd., MA-5, Gogna Colony, P.O.-Maithon Dam, Dist.- Dhanbad, Jharkhand-828207.
- 31. Director, Adhunik Power & Natural Resources Ltd., Lansdowne Towers, 5<sup>th</sup> Floor, 2/1A Sarat Bose Road, Kolkata-700020.
- 32. Sr. Vice President (Power), 4x600 MW IPP, Vedanta Ltd., Bhurkahamunda, P.O.-Sripura, Jharsiuguda, Odisha-768202.
- AVP & Head (O&M), GMR Kamalanga Energy Ltd., 29 Satyanagar, Bhubaneswar-751007.
- 34. Head (O&M), Chuzachen HEP, Gati Infrastructure Private Limited, Lower Bering Karabari, Pakyong, East Sikkim-737106.
- 35. Chief Executive Officer, Jindal India Thermal Power Limited, Plot No-12, Sector-B1, Local Shopping Complex, Vasant Kunj, New Delhi-110070.
- 36. Chairman & Managing Director, Dans Energy Private Limited, 5<sup>th</sup> Floor, Building No.8, Tower-C, DLF Cyber City, Phase-II, Gurgaon-12202, Haryana.



# MINUTES OF 35th ERPC MEETING

Date: 25th February, 2017

Venue: Ranchi

# Index

Item No	Title of Agenda				
Item No. A1	Confirmation of the minutes of 34 <sup>th</sup> ERPC meeting				
	Part B :: ISSUES REFERRED BY TCC IN ITS 35th MEETING				
Item No. B1	Status of DPR for PSDF funding in respect of Sikkim & JUSNL	3			
Item No. B2	Status of construction of 400 kV Sterlite-Jharsuguda D/C sections	4			
Item No. B3	Redundancy of data at either of the control centres in case of failure of any one communication path/ICCP link/communication equipments	6			
Item No. B4	Consideration of STU lines as Non-ISTS lines carrying ISTS power	9			
Item No. B5	Time correction of SEMs in Eastern Region	10			
Item No. B6	Proposal for stepwise completion of Rajarhat – Purnea 400 KV D/C lineunder ERSS-V Scheme	12			
Item No. B7	Nomination of the Bid Evaluation Committees (BECs) for the tranmission projects being implemented through TBCB	14			
	Part C :: ITEMS FOR INFORMATION				
Item No. C1	STATUS OF PROTECTION DATABASE PROJECT OF ERPC	15			
Item No. C2	ERPC ESTABLISHMENT FUND FOR THE YEAR 2017-18	15			
Item No. C3	ERPC FUND FOR THE YEAR 2017-18	16			
Item No. C4	CONTRIBUTIONS OUTSTANDING FROM GATI INFRASTRUCTURE PRIVATE LIMITED	16			
Item No. C5	MEMBERSHIP OF TEESTA URJA LIMITED IN ERPC	16			
Item No. C6	MEMBERSHIP OF ERPC ON ANNUAL BASIS FOR THE YEAR 2017- 18	17			
Item No. C7	NOMINATION IN TECHNICAL COORDINATION SUBCOMMITTEE (TCC) MEMBERS	18			
Item No. C8	NOMINATION OF CHAIRPERSON, ERPC FOR THE YEAR 2017-18	19			
Item No. C9	NOMINATION OF CHAIRPERSON, TCC FOR THE YEAR 2017-18	19			
Item No. C10	FINALISATION OF DATES AND VENUE FOR THE NEXT ERPC & TCC MEETINGS	20			
	Part D :: ITEMS FOR INFORMATION				
Item No. D1	Revision of DPR for establishment of Reliable Communication (Bihar-Portion)	21			
Item No. D2	FSTPS Islanding Scheme, NTPC	22			
Item No. D3	Status of Bus Splitting schemes in Eastern Region	23			
Item No. D4	Status of construction of 400 kV Ind-Barath-Jharsuguda D/C line	24			

Item No. D5	Status of construction of Chuzachen bay at Rangpo S/s.	24
Item No. D6	Status of construction of dedicated transmission lines of IPPs which are connected through interim arrangement	25
Item No. D7	Outstanding issues towards charging of 220kV Biharsharif-Tenughat line at 400 kV level	26
Item No. D8	High voltage problem in 400KV Meramundali Grid S/S	28
Item No. D9	Status of PLCC system installed in Eastern Region	30
Item No. D10	Opening of LC by ER constituents for Deviation Charges Payments	31
Item No. D11	High amount of Deviation Charges payable by BSPHCL on account of m/s. TALA HEP	32
Item No. D12	Operationalization of LTA for BRBCL	33
Item No. D13	Very high loading of 220kV Muzaffarpur(PG)-Kanti D/C line	33
Item No. D14	Augmentation of 400/220kV ICT capacity at Maithon, Patna, Sasaram, Biharshariff	34
Item No. D15	Commissioning of 125 MVAR bus reactor at Jamshedpur	34
Item No. D16	Priority-based commissioning of bus reactor for control of high voltage during lean periods	35
Item No. D17	Status of Transmission projects approved in various meetings	35
Item No. D18	Status of Spare Transformers & Reactors approved in various meetings	40
Item No. D19	Persistent over drawl by Jharkhand	41
Item No. D20	Commissioning of Tie bay and main bay of BUS-I of 400 kV Ranchi-New Ranch-I & II circuit at Ranchi Substation	42
Item No. D21	Issues related to associated / downstream systems Powergrid	43
Item No. D22	Commercial issues related to NHPC Stations	44
Item No. D23	Reconciliation of Deviation Accounts	46

## EASTERN REGIONAL POWER COMMITTEE

# MINUTES OF THE 35<sup>TH</sup> MEETING OF EASTERN REGIONAL POWER COMMITTEE

Date: 25<sup>th</sup> February, 2017 Venue: Ranchi

List of participants is at Annexure-I.

Shri Ashok Sethi, COO & Executive Director, Tata Power Company Limited, welcomed Shri N.T. Bhutia, Secretary, Energy & Power Department-Govt. of Sikkim, Shri A.K. Bandyopadhyaya, Member Secretary-ERPC, other distinguished members on dais, guests from Bhutan and all other delegates to the 35<sup>th</sup> ERPC meeting. He said MPL, the generating company, is a joint venture company between Tata Power and DVC with Tata Power having 74% equity whereas TPTCL, the power trading company, is a wholly owned subsidiary company of Tata Power. He thanked ERPC for giving MPL and TPTCL an opportunity to host this important meeting. In his presentation based address he briefly highlighted the following features of Tata Power:

Tata Power is the largest integrated power company in India in private sector with international presence. The present installed capacity of the company is 10477 MW with presence in all segments of power sector. The portfolio of Tata Power includes thermal and hydro power, solar and wind power, coal mining and shipment, power trading, transmission, distribution, renewable etc. Tata Power strives to lead the reform process for sustainable power. By the year 2025 about 30 to 40% of the total generation of Tata Power will come from renewable source. Tata Power has undertaken various digitisation initiatives like mobile app based services for Mumbai Discom consumers, Use of GIS for engineering, tracking and maintenance, digitisation of O&M through RCM toolkit in SAP, mobile app for safety reporting, digitisation of coal/ash logistics, remote operation of hydro / transmission assets etc.

Shri A.K. Bandyopadhyaya, Member Secretary, ERPC, welcomed Shri N.T. Bhutia, Secretary, Energy & Power Department, Govt. of Sikkim, Shri Ashok Sethi, COO & Executive Director-Tata Power, Shri Sanjeev Mehra, Managing Director-TPTCL, Shri K. Chandeasekhar, CEO-MPL, Shri Sandip K.R. Pudakalkatti, Managing Director-BSPTCL, other distinguished members on dais, TCC members, guests from Bhutan and other participants from various constituents to the 35<sup>th</sup> ERPC meeting. He thanked MPL and TPTCL for hosting the meeting out of turn and doing it in excellent manner. He informed that Shri Pratyaya Amrit, the present Chairperson-ERPC and CMD-BSPHCL, could not attend today's meeting due to his preoccupation. He requested Shri N.T. Bhutia, Secretary, Energy & Power Department, Govt. of Sikkim who was past Chairperson-ERPC to chair the meeting as per CBR of ERPC. He said there was overwhelming response from the constituents for attending the TCC and ERPC meetings. The number of participants had crossed hundred. He requested members to judiciously nominate the participants in future. In conclusion, he requested members for their valued opinions on the agenda placed for discussion and wished the meeting all success.

**Shri N.T. Bhutia, Secretary, Energy & Power Department, Govt. of Sikkim,** welcomed Shri A,K. Bandyopadhyaya, Member Secretary-ERPC, Shri Ashok Sethi, COO & Executive Director-Tata Power, Shri Sanjeev Mehra, Managing Director-TPTCL, Shri K. Chandeasekhar, CEO-MPL, Shri Sandip K.R. Pudakalkatti, Managing Director-BSPTCL, other distinguished members on dais, TCC members, guests from Bhutan and all other participants to the 35<sup>th</sup> ERPC meeting. He drew attention of members on the following issues which were slated for discussion:

- Construction of dedicated transmission lines associated with IPPs vis-à-vis continuation of the LILO arrangements. Many IPPs are now connected to the grid through interim LILO arrangement. Hon'ble CERC vide its order dated 28<sup>th</sup> September 2016 has directed CTU to take up the existing cases with the RPC and disconnect all such LILO arrangements within a period of three months unless RPC grants extension for continuation of LILO arrangements.
- There was total failure of real time SCADA data to all control centres from 05:53 hrs. of 8<sup>th</sup> August 2016 to 03:19 hrs. of 10<sup>th</sup> August 2016. This was a major incident. The matter was extensively discussed in OCC and Special meetings. It emerged that old RTUs are required to be replaced and for redundancy of ICCP links between main and backup control in few paths the last mile redundant fibre connectivity is required to be implemented.
- Time Correction of Special Energy Meters is also an area for concern. About 210 meters are there where the time drift is more than 10 minutes. Time drifting is having commercial implications in calculations of deviation charges. ERLDC and Powergrid may suggest remedial reassures on the issue and members may decide the course of action.
- ➤ Persistent overdrawal by some constituent and not responding to the instruction and advise of ERLDC is required to be addressed. The concerned constituent should abide by instruction of ERLDC and look into the advice of ERLDC on drawing URS power and comply with grid discipline.
- ➤ PSDF is providing fund for upgradation of protection system. Some of the State Utilities have already this facility. States like Jharkhand and Sikkim may finalise the DPR for submitting it to the Nodal Agency for PSDF funding.

In conclusion he thanked MPL and TPTCL for hosting this 35<sup>th</sup> ERPC meeting in excellent manner and wished the meeting a grand success.

ITEM NO.A1:	CONFIRMATION OF THE MINUTES OF 34th ERPC MEETING
-------------	--

The minutes of the 34<sup>th</sup> ERPC meeting held on 19<sup>th</sup> November 2016 in Kolkata were issued and uploaded on ERPC website vide ref. no.ERPC/TCC&Committee/14/2016/H3436-H3505 dated 23<sup>rd</sup> December 2016.

No comments have been received from constituent members on the minutes of the meeting.

Members may confirm the minutes of 34<sup>th</sup> ERPC meeting.

### **Deliberation in the ERPC meeting**

Members confirmed the minutes of 34th ERPC meeting.

### PART B: ISSUES REFERRED BY TCC IN ITS 35th MEETING HELD YESTERDAY

ITEM NO. B1: Status of DPR for PSDF funding in respect of Sikkim & JUSNL

In 33<sup>rd</sup>TCC, JUSNL and Sikkim informed that they need funds for upgradation of protection system. TCC, therefore advised JUSNL and Sikkim to prepare DPR within a month for up gradation of protection system and send to NLDC for PSDF funding with intimation to ERPC Secretariat.

In 34<sup>th</sup> TCC Sikkim informed that they will submit the DPR by January, 2016

JUSNL informed that they are going to place the order to PRDC for preparation of DPR by the end of November, 2016 and they will submit the DPR to PSDF nodal agency by February, 2017.

Sikkim and JUSNL may update.

### **Deliberation in TCC meeting**

Sikkim informed that they need some help from ERPC secretariat and assured that DPR will be submitted by 15<sup>th</sup> April 2017. Secretariat assured to extend their help.

JUSNL informed that M/s PRDC, consultant is preparing the DPR and they will submit the DPR to PSDF nodal agency by 15<sup>th</sup> April, 2017.

It was informed that CE, CEA will give a presentation on PSDF in tomorrow's ERPC meeting.

CEA may give a presentation on PSDF.

### **Deliberation in the ERPC meeting**

CE-NPC, CEA explained the eligibility criterion, procedures and latest status of the approved schemes of PSDF with a detailed presentation. The presentation is enclosed at **Annexure-III**.

CE-NPC, CEA informed that grant has been allotted to Powergrid for installation of STATCOM but no update on the progress have been received from Powergrid.

Powergrid informed that project has already been awarded and they will submit the details to PSDF Nodal Agency and NPC.

Members enquired about placing DPR for renovation and upgradation of transmission network of below 220kV voltage level and distribution system.

CE-NPC, CEA clarified that in general renovation and upgradation of the transmission network is considered up to 220kV level. But depending upon the importance of the transmission line, 132kV level may also be considered on case to case basis. Renovation and upgradation of distribution system is also eligible for PSDF.

MD, JBVNL pointed that they are not able to draw power from DVC stations due to system constraints and advised DVC to place DPR to address the constraints.

GMR asked about the reason for not considering IPPs for granting of PSDF as IPPs are also contributing to the fund.

CE-NPC, CEA explained that present eligibility criterion and procedures had been framed and approved by MoP, GoI. Any deviation from the criterion/procedure needs approval from MoP, GoI.

ERPC advised all the states to avail the opportunity to get the PSDF grant for upgradation of their system whereever it is neccessary.

ERPC also advised JUSNL and Sikkim to submit the DPRs to PSDF nodal agency at the earliest.

ITEM NO. B2:	Status of construction of 400 kV Sterlite-Jharsuguda D/C sections
--------------	---

Several deliberations were held in this forum on the issue of construction of 400 kV Sterlite – Jharsuguda D/C dedicated line of Vedanta Ltd (formerly known as Sesa Sterlite Ltd).

The 34<sup>th</sup> ERPC board, noted the progress made by Vedanta and advised Vedanta to expedite the work and complete the work by February, 2017 as decided by TCC. In this regard Vedanta was further advised to submit a fresh affidavit by 30.11.2016

Further, on appeal of Vedanta, ERPC reiterated that the physical completion of the project should be done by end February 2017. The pending statutory clearances may be obtained post completion of the physical activities and the status may be reviewed in next TCC meeting/ March 2017.

Subsequently, Vedanta Ltd submitted a affidavit on 15<sup>th</sup> December, 2016 (Copy of the same is attached at **Annexure-B5**).

The latest status updated in 130<sup>th</sup> OCC is as given below:

Activities	Nos	Status as on 15-Nov-16 (as updated in 34 <sup>th</sup> TCC)	Status as on 17-Feb-17 (As updated in 130 <sup>th</sup> OCC)	Target completion as given in 34 <sup>th</sup> TCC Meeting	Remarks
Tower Foundation	undation 64 60 <b>62</b>		30-Dec-16		
Tower Erection 64 42		42	55	10-Feb-17	
Stringing /OPGW	20.5	One stretch	5.5 km	28-Feb-17	
Cabling & Testing	Km	completed	completed	20-17-00-17	
Sub station Bay	2	Equipment Erection, Cable Trench, Earthing Completed	-	31-Dec-16	

Vedanta may update.

### **Deliberation in TCC meeting**

*Vedanta updated the latest status as follows:* 

Activities	Nos	Status as on 15-Nov-16 (as updated in 34 <sup>th</sup> TCC)	Status as on 24-Feb-17 (As updated in 35 <sup>th</sup> TCC)	Remarks
Tower Foundation	64	60	64	Completed
Tower Erection	64	42	58	
Stringing /OPGW	20.5	One stretch	8 km	
Cabling & Testing	Km	completed	completed	
Sub station Bay	2	Equipment Erection, Cable Trench, Earthing Completed	Bay construction completed	Will be completed by 2 <sup>nd</sup> March, 2017.

Vedanta informed that the construction work was delayed due to non-availability of shutdown of 11kV lines during Panchayat election.

Vedanta added that physical construction of the line will be completed by the end of March, 2017 and the line will be commissioned by end of April 2017 after getting the statutory clearances. Vedanta requested TCC to extend the dead line for removal of LILO up to April 2017.

CTU opined that in line with CERC order, they are ready to open the LILO as per the direction of TCC/ERPC.

Gridco, Odisha informed that they could not give the shutdown of 11kV feeders due to Panchayat elections and one month extension up to March 2017 may be granted to Vedanta for completion of line.

TCC opined that Vedanta is not serious about the construction of the line and still asking for 2 months extension. TCC viewed that the line can be commissioned by end of March 2017 if they could take up the activities related to statutory clearances simultaneously.

Accepting OPTCL request TCC decided to extend the dead line to 31.3.17 for commissioning of line including on-load charging of the same. Accordingly advised Vedanta to place item wise schedule for commissioning of line, in 35<sup>th</sup> ERPC meeting on 25.2.17.

Referred to ERPC for further guidance.

ERPC may decide.

### **Deliberation in the ERPC meeting**

Vedanta informed that they will submit the item wise schedule for commissioning of line within a week.

Vedanta added that physical construction of the line will be completed by the end of March, 2017 and the line will be commissioned by end of April 2017 after getting the statutory clearances. Vedanta requested ERPC to extend the dead line for removal of LILO up to 30<sup>th</sup> April 2017.

Further, GRIDCO, Odisha informed that the dead line for removal of LILO may be extended up to 15<sup>th</sup> April 2017.

In view of above, ERPC decided to extend the dead line for removal of LILO up to 15.04.2017 and advised Vedanta to strictly adhere to the schedule for commissioning of the dedicated line in all aspects.

Further, ERPC authorised CTU to open the LILO on 16.04.2017.

CTU agreed.

ITEM NO. B3:

Redundancy of data at either of the control centres in case of failure of any one communication path/ICCP link/communication equipments

There was a total failure of real time SCADA data to all control centres from 05:53 Hrs of 08-August-16. As an interim arrangement, real time SCADA data was restored on 10-August-16 at 03:19Hrs. The root cause was yet to be arrived and fixed.

In 126<sup>th</sup> OCC, it was raised that in case of failure of ICCP link/other communication equipment, the data availability needs to be assured at Back-up control centres.

OCC advised Powergrid to submit in 34<sup>th</sup> TCC their detail plan for data redundancy in case of failure of any one communication system at either of the control centres (Main & Back-up).

34<sup>th</sup> TCC felt that in case of failure of ICCP link/other communication equipment, the data availability needs to be assured at Main as well as Back-up control centres.

Powergrid informed that the alternate communication path was not available for SLDCs and ERLDC. Powergrid added that backup equipment is available and alternate communication path can be planned.

TCC advised to convene a special SCADA meeting to discuss the issue and report back.

In Special PRM meeting was held on 14.02.2017 to deliberate the issue. The minutes of the meeting is available at ERPC website (http://www.erpc.gov.in/event-calendar/). In the meeting the following two major issues emerged which need to be addressed:

# 1) Replacement of old RTU in Eastern Region for reporting of RTU / SAS to back-up control centres-

In the meeting, POWERGRID informed that independent reporting of RTU/SAS to backup ERLDC control center may consume lots of bandwidth and independent reporting will be easier through VLAN in 104 protocols but the old RTU in Central sector is not having 104 protocols provision. POWERGRID further informed that provision of dual reporting of RTUs / SAS would be possible in 104 protocols only after replacement of old RTUs.

ERLDC informed that new SCADA system is designed for dual reporting considering VLAN in 104 protocols and unless until, the dual data reporting of each RTUs / SAS would be configured in 104 protocols, complete control centre backup will not be achieved. So, it is quite necessary to replace the old RTUs / SAS at the earliest.

GM, ERLDC informed that process of replacement of similar old RTUs has taken up at Western Region also after getting proper approval at RPC level. GM, ERLDC suggested that a committee may be constituted to begin with to assess the requirement of the replacement of the old RTUs.

All members agreed and referred to TCC for further guidance.

TCC may guide.

### **Deliberation in TCC meeting**

ERLDC informed that new SCADA system is designed for dual reporting. It is possible through LOOP PDH and SAS at main ERLDC control centre and extended directly to backup ERLDC control centre. But for Alcatel PDH it would not be possible. As these RTUs have already completed 15 years and need to be replaced by 2020, the replacement process may be initiated by the respective utilities.

Further ERLDC informed that as per the draft communication regulation the life of RTUs is fifteen years so the utilities should take care for their RTUs.

NTPC informed that the RTUs will be completing their life by 2020 and if any replacement is required before 2020 it may be considered after proper assessment.

After detailed discussion, TCC decided that a committee may be formed by ERLDC with Powergrid as nodal agency for assessment of old RTUs and further necessary action on replacement. Progress reports in this regard are to be placed before TCC on regular basis.


ERPC may guide.

### **Deliberation in the ERPC meeting**

ERPC advised ERLDC to convene a separate meeting and form a committee with CTU/Powergrid as nodal agency for assessment of old RTUs of central sector and further necessary action on replacement.

### 2) Redundancy of ICCP links between control centres:

ERLDC informed that ICCP links from ERLDC / backup ERLDC to all control centres should be available as mentioned in the diagram below:

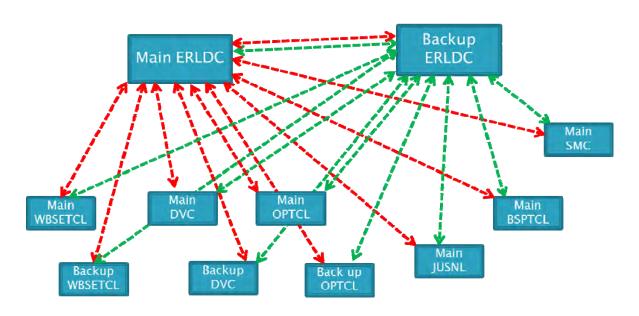

POWERGRID intimated that the ICCP connectivity of Backup ERLDC with all the control centers will be fully implemented after complete route redundancy of optical fiber. There are few paths (especially last mile) where there is no fiber redundancy. POWERGRID requested constituents to explore and implement the last mile redundant fiber connectivity. Such path having no redundancy has been identified for each sector and redundant route is shown in ICCP flow diagram in **Annexure** – **B12.2**. Following are the sections where fiber laying is to be done/under implementation:

### **Central Sector:**

<u>ERLDC</u> to Kasba-POWERGRID informed that one UGFO link between ERLDC to Kasba is under implementation by them. POWERGRID further informed that alternate FO link connectivity may be implemented after getting the fiber connectivity from CESC (Kasba S/S – Jadavpur S/S – ERLDC) for route diversity for redundancy. POWERGRID requested ERLDC to take up the matter with CESC so that the same fiber can be used between ERLDC to Kasba for route diversity for redundancy.

<u>Farakka to Jeerat</u> – POWERGRID informed that presently, FO link connectivity is available between Farakka to Jeerat through Behrampur which doesn't have route diversity. POWERGRID further informed that route diversity for redundancy would be available after commissioning of OPGW link from Farakka to Jeerat through Gokarna, Rajarhat & Subhashgram.

### WBSETCL Sector:

<u>Kasba</u> to Arambag – POWERGRID informed that presently, FO link connectivity is available between Kasba to Arambag through Jeerat, Behrampur, Farakka & Durgapur which doesn't have route diversity. POWERGRID further informed that route diversity for redundancy would be available after commissioning of OPGW link from Kasba to Arambag through Jeerat &Krishnanagar as mentioned in the ICCP flow diagram of WBSETCL. POWERGRID further informed that the same would be implemented by December 2017.

### **DVC Sector:**

Howrah SLDC to ERLDC– POWERGRID informed that presently, FO link connectivity between Howrah SLDC to ERLDC is available through leased line. POWERGRID further informed that route diversity for redundancy would be available after commissioning of OPGW link from Howrah SLDC to Maithon SLDC & Howrah SLDC to Waria as mentioned in the ICCP flow diagram of DVC. POWERGRID further informed that the same would be implemented by June 2017.

<u>Kalyaneshwari to Mathon SLDC</u> – POWERGRID informed that presently, FO link connectivity is available between Kalyaneshwari to Maithon SLDC through Maithon HPS which doesn't have route diversity. POWERGRID further informed that route diversity for redundancy would be available after commissioning of OPGW link from Maithon SLDC to Howrah SLDC as mentioned in the ICCP flow diagram of DVC. POWERGRID further informed that the same would be implemented by June 2017.

### **OPTCL Sector:**

<u>Rourkela to Bhubaneswar SLDC</u> – POWERGRID informed that presently, FO link connectivity between Rourkela to Bhubaneswar SLDCis available through TSTPS, Meeramundali& Mendhasal which doesn't have route diversity.

OPTCL informed that route diversity for redundancy would be available after commissioning of repeater station at Bhabanipatna between Jeypore – Bolangir line and FO link connectivity from Meeramundali to Bhubaneswar SLDC through Duburi New, Jagatsingpur & Cuttack as mentioned in the ICCP flow diagram of OPTCL. OPTCL further informed that the same would be implemented by March 2018.

### **BSPTCL Sector:**

<u>Biharsharif 400 kV (PG) to Patna SLDC</u> –POWERGRID informed that presently, FO link connectivity between Biharsharif 400 kV (PG) to Patna SLDC is available through Biharsharif 220,Fatwa &Jakkanpur which doesn't have route diversity.

BSPTCL informed that FO link connectivity between Biharsharif 220to Jakkanpur would be available through Bodhgaya, Chandwa, Jahanabad& Sipara. The same would be implemented by July 2017.

POWERGRID informed that route diversity for redundancy between Biharshariff 400 (PG) to Jakkanpur could not be achieved until unless FO connectivity from Patna to Sipara or/and Biharshariff 400 (PG) to Biharshariff 220 would be implemented. POWERGRID requested BSPTCL to get this FO link implemented. BSPTCL requested POWERGRID to include the same in the existing FO link implementation contract.

POWERGRID requested BSPTCL to explore the possibility of FO connectivity from Jakkanpur to Patna SLDC from their DISCOM for route diversity and redundancy between Jakkanpur to Patna SLDC. BSPTCL agreed for the same.

### JUSNL Sector:

Ranchi 400 kV (PG) to JUSNL SLDC (Kushai Colony) –POWERGRID informed that presently, FO link connectivity between Ranchi 400 kV (PG) to JUSNL SLDC is available through Hatia 220 kV which doesn't have route diversity.

POWERGRID further informed that route diversity for redundancy between Ranchi 400 kV (PG) to JUSNL SLDC (Kushai Colony) could not be achieved until unless OPGW connectivity from Chandil to JUSNL SLDC through Namkum (132 kV) i.e. 95 Km could be completed. POWERGRID further informed redundant fiber route is to be explored and implemented by JUSNL.

### Sikkim:

<u>Gangtok to Sikkim SLDC</u> –POWERGRID informed that presently, FO link connectivity between Gangtok to Sikkim SLDC is available which doesn't have route diversity.

POWERGRID further informed redundant fiber route is to be explored and implemented by Sikkim.

TCC may deliberate.

### **Deliberation in TCC meeting**

TCC advised all the respective constituents to explore for the last mile connectivity of fibre.

ERPC may guide.

### **Deliberation in the ERPC meeting**

ERPC endorsed.

ITEM NO. B4:	Consideration of STU lines as Non-ISTS lines carrying ISTS power
--------------	--

Subsequently, in line with 34<sup>th</sup> TCC decision, ERPC and ERLDC conducted the load flow study using WebNet software for first three quarters of validated data. Summary of the results for percentage utilization of the transmission line by STU to meet the own demand is given at **Annexure-B13.** 

Balance (100 - utilization of the transmission line by the STU) is the ISTS power flowing through the line.

128<sup>th</sup> OCC decided that ISTS power flowing through STU lines greater than 50% of the total power as per the WebNet software of the validated data for each quarter will be considered as ISTS line.

In 129<sup>th</sup> OCC, OPTCL pointed that the PoC charges for STU lines should be calculated based on the actual ISTS power flow through STU lines as per the WebNet software of the validated data for each quarter.

However, after detailed deliberation all the STUs including OPTCL agreed that STU lines carrying ISTS power greater than 50% of the total power as per the WebNet software of the validated data for each quarter will be considered as non-ISTS line carrying ISTS power.

Further, GM-ERLDC informed that in Western Region the same principle is being followed for STU lines.

OCC requested concerned utilities to file petition before CERC in this regard with this recommendation.

TCC may guide.

### **Deliberation in TCC meeting**

TCC advised all the respective states to file petition before CERC for consideration of non-ISTS lines under respective control areas as ISTS lines with OCC recommendation.

TCC also advised ERPC/ERLDC to continue study in this regard on each quarter.

ERPC may guide.

### **Deliberation in the ERPC meeting**

ERPC approved.

ITEM NO. B5:	Time correction of SEMs in Eastern Region
--------------	---

The drifting of meter time was important in commercial terms since the reading for a block for a time drifted meter might not be true and lead to erroneous calculation of Deviation Charge for that constituent. Further, it was decided to keep this as a standing agenda in Commercial Sub Committee meetings for monitoring. List of Time drifted (more than 5-6 min) meters in ER as on 30.01.17 is enclosed in **Annexure-B15.** 

It has been seen that constituents are not making any time correction in SEM. Further after AMR implementation due to non-use of the DCDs, many DCDs are not working in many places. Time correction from laptops is not possible. In Last CCM, It was decided that all the constituents would give a list of DCD with them and their status. Powergrid is requested to keep some spare DCD for the purpose of time correction of meters.

In the last CCM held on 06.02.2017, POWERGRID proposed purchase of about 10 to 15% new L & T meters and some DCDs so that time correction could be taken up urgently by replacing the

time drifted meters from highest drift first. Then the drifted meters could be sent to the works of M/s L&T for bulk time correction. It was further informed that the new Genus make meters are yet to be interfaced with AMR system so procurement of new L&T meters could help relieve the drift issue.

ERLDC observed that the integration of Genus meters with AMR system are already ongoing by TCS and may be successful in a few days. Therefore, it may be prudent to replace the L & T meters with Genus meters, which have bulk time correction facility on site. The replaced L & T meters may be sent to factory for bulk time correction.

Powergrid was requested to prepare a list of L& T meters which were faulty or have exhausted their specification so that the same may be taken up for replacement immediately by Genus meters (as and when interface with AMR was complete)

GRIDCO representative informed that smart meters may be considered in future so that online time simultaneous time correction could be incorporated. ERLDC informed that the revision of metering regulations was under process in CEA and smart features may be incorporated.

Powergrid may update regarding integration of new Genus make meter in ER AMR.

### **Deliberation in TCC meeting**

Constituents felt that the performance of the new Genus make meter should be confirmed before replacing all the SEMs.

Powergrid informed that new Genus meters were procured after conforming the specifications as per the CEA meter regulations and the bulk time drift in these meters can be corrected in one attempt through Laptop. The interfacing issues of Genus meters with AMR will be resolved by April 2017.

It was felt that the meters with severe drift greater than 10 min need to be replaced first and if replacement is done with Genus then readings are to be collected manually using Laptop till interfacing with AMR is completed.

TCC advised Powergrid to replace the 10% of the heavily drifted SEMs and monitor the performance of the new meters. Powergrid should present this performance before constituents and subsequently the decision on replacement of the other time drifted meters will be taken up.

ERPC may advise.

### **Deliberation in the ERPC meeting**

ERLDC informed that the integration of Genus meter with AMR is being taken up with Powergrid and TCS. ERLDC added that two Genus make meters have been installed at 400kV Arambag and PPSP S/s in December 2016 and their performance is satisfactory.

ERPC advised Powergrid to replace the 10% of the heavily drifted SEMs with new Genus make meters and monitor the performance of the Genus meters. Powergrid should present this performance before constituents and subsequently the decision on replacement of the other time drifted meters will be taken up.

ERPC also advised Powergrid to place the list of 10% of the heavily drifted SEMs to be replaced with Genus make meters in next OCC meeting.

ITEM NO. B6:	Proposal for stepwise completion of Rajarhat – Purnea 400 KV D/C line under ERSS-V Scheme
--------------	---

Investment approval for the following transmission project associated with Eastern Region Strengthening Scheme-V (ERSS-V) was accorded by the competent authority in 292<sup>nd</sup> Board meeting on 23<sup>rd</sup> Oct'2013.

- 1. Rajarhat Purna 400 KV D/C line (with triple snow bird conductor) with LILO of one circuit at Gokarna(WBSETCL) and other circuit at Farakka(NTPC).
- 2. LILO of Subhasgram Jeerat 400 KV S/C line at Rajarhat.
- 3. Establishment of 400/220 KV, 2X500 MVA Gas Insulated Sub-station at Rajarhat in west Bengal.

Keeping in view of the facts and priorities, the project element "Rajarhat – Purnea 400 KV D/C line (with triple snow bird conductor) with LILO of one circuit at Gokarna (WBSETCL) and other circuit at Farakka (NTPC)" associated with ERSS-V was proposed to be rearranged and commissioned stepwise as detailed below:

Sl.	Description of rearranged Element
No.	
1	Rajarhat - Farakka portion of Rajarhat - Purnea 400 KV D/C transmission line including LILO of one ckt. of Rajarhat - Purnea Line at Farakka
2	LILO of one Circuit of 400 KV D/c Rajarhat- Purnea Line at Gokarna Substation
3	Farakka – Purnea portion of Rajarhat - Purnea 400 KV D/C transmission line


34<sup>th</sup> TCC agreed for the above rearrangement.

In 129<sup>th</sup> OCC, Powergrid informed that the construction work of 400 KV GIS Sub-station and tower package of 400 KV D/C Rajarhat –Purnea Transmission line at Rajarhat end has completely brought to a standstill condition since last one month due to agitation of local villagers.

However, Farakka-Gokarna portion of the said line along with associated bays at Farakka may be completed within the FY 2016-17. Further, Sub-station work including ICT at Gokarna (under jurisdiction of WBSETCL) is ready for charging and 400 KV line bays including 80 MVAR B/R (under scope of POWERGRID) is also ready for commissioning. Accordingly, 400 KV D/C Farakka-Gokarna portion of Rajarhat-Purnea 400 KV D/C transmission line including LILO of one circuit at Farakka and other circuit at Gokarna can be commissioned within March, 2017. This is also to be noted that commissioning of Farakka-Gokarna portion of the Rajahat-Purnea transmission line can connect Gokarna S/s at 400 KV level which will improve the power situation in and around Berhampur area.

Keeping in view of the above facts and priorities the project element "Rajarhat-Purnea 400 KV D/C transmission line (with triple snow bird conductor) with LILO of one circuit at Gokarna (WBSETCL) and other circuit at Farakka (NTPC)" associated with ERSS-V is proposed to be rearranged and commissioned stepwise as detailed below:

SL	DESCRIPTION OF REARRANGED ELEMENT
NO	
1.	400 KV Farakka-Gokarna portion of Rajarhat-Purnea 400 KV D/C Transmission line including LILO of one circuit at Farakka & other circuit at Gokarna.
2.	Rajarhat-Gokarna portion of the 400 KV D/C Rajarhat-Purnea Line.
3.	Farakka – Purnea portion of Rajarhat - Purnea 400 KV D/C transmission line.

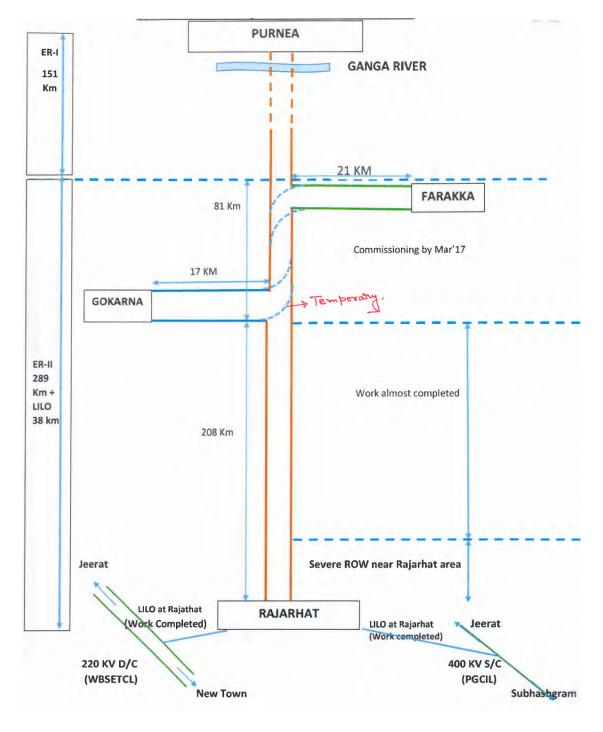

Rajarhat Purnea re-arrangement diagram

After commissioning of element at Sl. No. 1 the effective transmission line shall be 400 KV D/C Gokarna-Farakka TL with 1 No. 80 MVAR B/R at Gokarna end and 1 No. 80 MVAR line reactor at Farakka end.

OCC agreed and recommended for TCC approval.

TCC may deliberate.

### **Deliberation in TCC meeting**

TCC approved the changes and referred to ERPC for further concurrence.

TCC decided that the scheme will be referred to Standing Committee after approval of ERPC.

ERPC may approve.

### **Deliberation in the ERPC meeting**

Powergrid informed that with the above arrangement the line will function as 400kV Farakka-Gokarna D/c line and support WBSETCL system.

ERPC approved the scheme and advised to place before Standing Committee.

ITEM NO. B7:	Nomination	of the	Bid	Evaluation	Committees	(BECs)	for	the
	tranmission	project	being	g implemente	d through TB	CB		

CEA vide letter dated 30.11.16 & 16.02.17 informed that Ministry of Power had notified the below scheme vide Gazette Notification dated 31.10.2016.

As per the Tariff based Competitive Bidding Guidelines for Transmission Service notified by Govt. of India nomination of officers at Director level are sought for constituting the scheme specific Bid Evaluation Committee (BEC) which is as follows:

Sl. No.	Name of Transmission Scheme	Bid Process Coordinator	Nomination of officers (in no.)
1.	Eastern Region Strengthening-XXI(ERSS-XXI)  (i) Establishment of 400/220/132 kV, 2x500 MVA+2x200 MVA S/s at Sitamarhi(New)  (ii) Establishment of 400/220/132 kV, 3x500 MVA+3x200 MVA S/s at Chandauti(New)  iii) Establishment of 400/220/132 kV, 2x500 MVA+2x200 MVA S/s at Saharsa(New)  iv) Substation extension at Darbhanga S/s  v) Substation extension at Motihari S/s	REC Transmission Projects Co. Ltd.	2

It is requested that two no. of officers at Director level may be nominated for BEC for above ERSS-XXI projects.

TCC may nominate.

### **Deliberation in TCC meeting**

TCC advised Bihar and Jharkhand to nominate for BEC at the earliest.

ERPC may nominate.

### **Deliberation in the ERPC meeting**

Bihar and Jharkhand nominated the following members for BECs:

- 1) Director (Project), Bihar State Power Transmission Company Ltd.,
- 2) Chief Engineer (Trans.), Jharkhand Urja Sancharan Nigam Ltd,

### **PART C: ERPC MATTERS**

ITEM NO. C1: STATUS OF PROTECTION DATABASE PROJECT OF ERPC

PRDC may present the status of Protection Database project of ERPC being funded by PSDF.

### **Deliberation in the ERPC meeting**

PRDC has given a presentation on latest status of Implementation of Protection Database Project of ERPC. Presentation is enclosed at Annexure-IV. PRDC informed the following:

- Operational load flow study is completed
- Data collection, SLD preparation and relay data population in PDMS completed for pilot state Odisha
- Server has been installed at ERPC on 15<sup>th</sup> December 2016
- PDMS software has been installed on 20<sup>th</sup> December 2016
- Software acceptance trails of pilot state Odisha has been completed on 21st January 2017

PRDC added that data collection, SLD preparation and relay data population in PDMS is in progress for other states. Training program for different states is also in progress.

Further, PRDC informed that they will complete the project by April 2017.

ITEM NO. C2:	ERPC ESTABLISHMENT FUND FOR THE YEAR 2017-18
--------------	--

For the year 2016-17 contribution of Rs.15 Lakh per member was approved by ERPC. It is proposed to keep the contribution unchanged for the year 2017-18 i.e. Rs 15 Lakh per member. The fund is utilised for reimbursement of ERPC Secretariat expenditures to the Govt. of India and any other expenditures as per the approval of ERPC.

Members may approve contribution of Rs. 15 Lakh per member for the year 2017-18.

### **Deliberation in the ERPC meeting**

ERPC approved contribution of Rs. 15 Lakh per member for the year 2017-18.

ITEM NO. C3: ERPC FUND FOR THE YEAR 2017-18

For the year 2016-17 contribution of Rs.1 Lakh per member was approved by ERPC. It is proposed to keep the contribution unchanged for the year 2017-18 i.e. Rs. 1 Lakh per member. The fund is utilised for holding various meetings, workshops, seminars etc. at the Secretariat and any other expenditures as per the approval of ERPC.

Members may approve contribution of Rs. 1 Lakh per member for the year 2017-18.

### **Deliberation in the ERPC meeting**

ERPC approved contribution of Rs. 1 Lakh per member for the year 2017-18.

ITEM NO. C4:	CONTRIBUTIONS	OUTSTANDING	FROM	<b>GATI</b>
11 EWI NO. C4:	INFRASTRUCTURE 1	PRIVATE LIMITED		

The following payments are outstanding from Gati Infrastructure Private Limited (GIPL) as a member of ERPC:

ERPC Establishment Fund: Rs. 30 lakh for the year 2015-16 and 2016-17 ERPC Fund: Rs. 2 lakh for the year 2015-16 and 2016-17.

GIPL vide letters dated 28.10.2016 and 25.01.2017 proposed to relinquish the membership of ERPC w.e.f. FY 2016-17 citing financial constraints to contribute in ERPC Establishment Fund and ERPC Fund.

In response ERPC Secretariat vide letter dated 03.01.2017 and 15.02.2017 has conveyed to GIPL that as per the decision taken by ERPC in its 34<sup>th</sup> meeting held on 19.11.2016 the membership GIPL would continue upto 31<sup>st</sup> March 2017. GIPL is required pay its contributions upto 2016-17.

Members may discuss and decide on the matter.

### **Deliberation in the ERPC meeting**

Gati Infrastructure Private Limited (GIPL) agreed to pay the contributions upto 2016-17 shortly.

ITEM NO. C5:	MEMBERSHIP OF TEESTA URJA LIMITED IN ERPC
--------------	---

As per GoI Resolution on ERPC State Generating Companies are members of ERPC. Teesta Urja Limited (TUL) is a State owned generating company, Govt. of Sikkim having more than 51% equity holding. Teesta-III HEP will have 1200 MW installed capacity (6X200 MW). Five units Teesta-III have already been commissioned. As a member of ERPC Teesta Urja Limited will be required to contribute in ERPC Funds at par with other ERPC members.

ERPC may ratify the membership of Teesta Urja Limited.

### **Deliberation in the ERPC meeting**

ERPC approved the membership of Teesta Urja Limited (TUL) and welcomed them as a new member of ERPC. Representatives of TUL acknowledged.

ITEM NO. C6:	MEMBERSHIP OF ERPC ON ANNUAL BASIS FOR THE YEAR
	2017-18

**C6.1 Membership of Private Distribution Company:** As per GoI Resolution on ERPC one distribution company by alphabetical rotation out of the private distribution companies functioning in the region is eligible to become new member on yearly basis. The private distribution companies functioning in the region are IPCL in West Bengal, NESCO, SOUTHCO & WESCO in Odisha and JUSCO in Jharkhand. The names of the private distribution companies in alphabetical order are IPCL (formerly DPSC), JUSCO, NESCO, SOUTHCO & WESCO. In the past none of the private distribution companies showed interest to become member of ERPC and agree to contribute in ERPC Funds at par with other members. The last such offer for ERPC membership was made to JUSCO but they did not respond. Now it is the turn of NESCO in Odisha to become member of ERPC for the year 2017-18.

Accordingly, it is proposed to empower the Secretariat to approve the membership of North Eastern Electricity Supply Company of Odisha Limited (NESCO) for the year 2017-18 subject to NESCO filing an application for membership together with its contribution in ERPC Funds. ERPC Secretariat will suggest NESCO to apply.

Members may approve the above proposal.

### **Deliberation in the ERPC meeting**

Members noted in the past none of Discoms had shown any interest to become member of ERPC in this category. After brief deliberation on the matter it was decided the Secretariat would write to all Discoms in alphabetical order starting from NESCO. The Discom which accepts the offer in the same alphabetical order would be inducted as a member of ERPC for the year 2017-18 subject to their willingness to contribute in funds at par with other members.

**C6.2 Membership of Private Generating Company (I.C.1000 MW & less):** As per GoI Resolution on ERPC one generating company having installed capacity 1000 MW & less out of the GENCOs functioning in the region (other than central & state generating companies and IPPs having installed capacity more than 1000 MW) is eligible by alphabetical rotation to become member on yearly basis.

In the above category the following IPPs are operating in the region:

- i) Dans Energy Private Limited (Jorthang Loop HEP, 2X48 MW)
- ii) Gati Infrastructure Private Limited (Chuzachen HEP, 2X55MW)
- iii) Ind-Bharath Energy (Utkal) Limited (2X350MW)
- iv) Tata Power Haldia Limited (2X45 MW)
- v) Vedanta Limited (1X600 MW)

Dans Energy Private Limited is the member for the year 2016-17. Gati Infrastructure Private Limited has already expressed to relinquish ERPC membership due to financial constraints. Now it is the turn of Ind-Bharath Energy (Utkal) Limited to become member of ERPC for the year 2017-18.

It is proposed to empower the Secretariat to approve the membership of Ind-Bharath Energy (Utkal) Limited (IBEUL) for the year 2017-18 subject to IBEUL filing an application for membership together with its contribution in ERPC Funds. ERPC Secretariat will suggest IBUEL to apply.

Members may approve the above proposal.

### **Deliberation in the ERPC meeting**

Members decided that the Secretariat would write to IBEUL and other IPPs in alphabetical order except Gati Infrastructure Private Limited (GIPL). The IPP which accepts the offer in the same alphabetical order would be inducted as a member of ERPC for the year 2017-18 subject to their willingness to contribute in funds at par with other members. GIPL would be excluded from the list since they wanted to relinquish membership of ERPC.

**C6.3 Membership of Electricity Trader:** As per GoI Resolution on ERPC one electricity trader is eligible to become member of ERPC representing electricity traders in the region on yearly basis. As per existing practice, CEA recommends the name of the trader. Recommendation from CEA is awaited. On receipt of the recommendation from CEA the nominated trader will be asked to apply for membership together with its contributions in ERPC Funds.

Members may approve the above proposal.

### **Deliberation in the ERPC meeting**

Members authorised Member Secretary, ERPC to communicate to the concerned trader on receipt of nomination from CEA.

ITEM NO. C7:	NOMINATION	IN	<b>TECHNICAL</b>	COORDINATION	SUB-
	COMMITTEE (T	CC)	MEMBERS		

Nomination of members in TCC is pending from the following organisations:

- 1. Jharkhand Urja Vikas Nigam Limited (JUVNL)
- 2. Jharkhand Bizli Vitaran Nigam Limited (JBVNL)
- 3. Jindal India Thermal Power Limited (JITPL)

Members of ERPC from the above organisations are requested to nominate TCC members from their organisations.

Members may kindly note the following provision of Conduct of Business Rules of ERPC while nominating representatives:

Technical Coordination Sub-Committee (TCC): The representation shall be at the level of Member/Director in State Utilities, and Executive Director/General Manager in CPSUs, Technical Head of Distribution Company/Traders/IPPs, Heads of NLDC & ERLDC and Chief Engineer of CEA.

### **Deliberation in the ERPC meeting**

Representatives from JUVNL and JBVNL agreed to nominate their TCC members and communicate to ERPC Secretariat. In absence of any representative from JITPL it was decided that the Secretariat would write to JITPL seeking nomination of TCC member.

ITEM NO. C8:	NOMINATION OF CHAIRPERSON, ERPC FOR THE YEAR 2017- 18
--------------	--

The incumbent Chairperson, ERPC i.e. Chairman-cum-Managing Director, BSPHCL, will complete his term on 31<sup>st</sup> March 2017.

As per GoI Resolution "Chairperson of ERPC would represent the States of the region by rotation in alphabetical order. Members of ERPC from the particular State would nominate the Chairperson of ERPC from amongst themselves. Term of Chairperson would be for a period of one year."

The names of the States in alphabetical order are Bihar, Jharkhand, Odisha, Sikkim & West Bengal. Now it is the turn of Jharkhand. The following designated officers are the member of ERPC from Jharkhand:

- 1. Chairman & Managing Director, Jharkhand Urja Vikas Nigam Limited
- 2. Managing Director, Jharkhand Urja Sancharan Nigam Limited
- 3. Managing Director, Jharkhand Bizli Vitran Nigam Limited
- 4. Managing Director, Tenughat Vidyut Nigam Limited

Therefore, the members of ERPC from Jharkhand are requested to nominate the Chairperson, ERPC for the year 2017-18.

### **Deliberation in the ERPC meeting**

Members from Jharkhand nominated Chairman & Managing Director, Jharkhand Urja Vikas Nigam Limited (CMD, JUVNL) as the Chairperson, ERPC for the year 2017-18.

ITEM NO. C9:	NOMINATION OF CHAIRPERSON, TCC FOR THE YEAR 2017-18
--------------	---

The incumbent Chairperson, TCC i.e. Director (Project), BSPTCL, will complete his term on 31<sup>st</sup> March 2017.

As per TCC regulations, Chairperson, ERPC shall nominate the Chairperson, TCC from the TCC members from the same State for a period of one year.

Accordingly, the new Chairperson, ERPC, nominated for the year 2017-18 as above, may nominate the Chairperson, TCC for the year 2017-18.

### **Deliberation in the ERPC meeting**

It was decided that CMD, JUVNL nominated as Chairperson, ERPC for the year 2017-18, would be requested to nominate Chairperson, TCC for the year 2017-18 amongst the TCC members from Jharkhand.

ITEM NO. C10:	Finalisation of dates and venue for the next ERPC & TCC meetings
---------------	--

The roster for hosting of ERPC meetings is given below:

Sl.	Host Organisation
No.	
1.	WEST BENGAL
	- hosted 26 <sup>th</sup> ERPC Mtg. on 18.01.2014
2.	DVC
	- hosted 22 <sup>nd</sup> ERPC Mtg. on 25.08.2012
3.	NHPC
4.	POWERGRID
5.	SIKKIM
6.	PTC
7.	ODISHA
8.	JHARKHAND
9.	BIHAR
10.	NTPC
11.	CESC
12.	APNRL
13.	MPL— hosting 35 <sup>th</sup> Meeting jointly
14.	GMRKEL
15.	NVVN
16.	TPTCL— hosting 35 <sup>th</sup> Meeting jointly
17.	JITPL

Now, it is the turn of APNRL to host the next meeting. Members may decide about the dates and the venue for the next TCC & ERPC meetings.

### **Deliberation in the ERPC meeting**

Representatives from APNRL submitted that due to financial constraints and few other related issues they would prefer to host the meeting at a later date jointly with any other member organisation.

On the request of members, GMRKEL agreed to host the next ERPC and TCC meetings. It was decided that the next (36<sup>th</sup>) TCC and ERPC meetings would be held in the month of September 2017. GMRKEL would finalise the dates and venue in consultation with ERPC Secretariat.

### PART D: ITEMS FOR INFORMATION

### **ERPC** members noted the following items:

ITEM NO. D1:	Revision of DPR for establishment of Reliable Communication (Bihar-
HEMINO.DI:	Portion)

In 34<sup>th</sup> TCC, it was informed that MoP agreed to fund 30% of the OPGW project through PSDF and rest 70% from states. Chairperson advised that TCC members may explore possibilities of enhancement of the PSDF portion on funding for OPGW project.

Powergrid updated that DPR for installation of OPGW for transmission lines of 132kV and above voltage level for both central and state sectors has been prepared for submission to the PSDF appraisal committee but now as per the decision of MoP the central sector is to be implemented by Powergrid on tariff based scheme and States sectors have to implement their portion on their own or may apply for PSDF funding on grant & investment ratio @30:70.

TCC advised all the States to place the DPR to PSDF appraisal committee for OPGW project with their proposed PSDF funding requirement.

BSPTCL vide letter dated 07.01.17 intimated that the that power sector in Bihar is growing many folds. Since the submission of transmission details and its connectivity diagram to PGCIL, many new transmission lines and sub-station has been commissioned and many of these elements are going to be commissioned shortly. Further, in view of achieving redundancy, some transmission lines have been taken into consideration for laying OPGW under ULDC revised scheme. This scheme is under implementation with PGCIL. So, the DPR need to be revised based on the update information of Sub-stations which is enclosed at **Annexure-B2**.

In Special PRM held on 14.02.2017, Powergrid informed that the State portion has to be implemented by the respective States. Powergrid will only implement for the Central Sector portion.

States may update respective status. TCC may guide.

### **Deliberation in TCC meeting**

Chairman, TCC informed that states were not attending the higher level meetings being held at CEA and advised all the state representatives to attend.

He added that PSDF grant & investment ratio @30:70 was arrived based the marketing of the OPGW network by the states. However it is not possible for Eastern Region states.

He suggested that all the constituents should approach MoP, GoI for PSDF grant & investment ratio @90:10.

CE, NPC informed that such schemes will be considered for PSDF funding but for changeing the grant & investment ratio to 90:10 the approval needs to be taken from Ministry of power, GOI.

TCC decided that all the states should prepare DPR and send it to PSDF appraisal committee by 5<sup>th</sup> March, 2017 with a request to CE, NPC to take up the matter with ministry for considering the PSDF grant & investment ratio @90:10 for the projects of state sectors.

JUSNL informed that their DPR is ready and will be submitted by next week. Further, JUSNL pointed that the ownership of ties of JUSNL and BSPTCL lines was not yet decided and a procedure should be formulated for installation of OPGW in those lines.

TCC viewed that ownership issues are bilateral and these issues should be resolved by mutual interaction.

ITEM NO. D2: FSTPS Islanding Scheme, NTPC

In 118th OCC, NTPC informed that their part is ready for implementation.

Powergrid informed that the battery charger has been delivered and expected to complete the work by March, 2016.

In 128<sup>th</sup> OCC meeting it was informed that progress of the islanding scheme is being monitored at Ministry level and ERPC Secretariat has already communicated the completion schedule as December, 2016.

OCC took serious note of extending the completion schedule of the islanding scheme in the last moment.

OCC felt that NTPC is not serious about implementation of the islanding scheme advised NTPC to submit their complete action plan to ERPC and ERLDC.

Subsequently NTPC submitted that

### **QUOTE**

Regarding Farakka Islanding scheme, Cabling work has been done up to unit control room but final hooking with C&I system is pending. After evaluating every aspect, NTPC Farakka is of the view that the connection to C&I system is to be done during unit overhaul only so that proper checking of control system response can be done by simulation. Due to this, there has been a revision of the plan at our end. Our overhauling plan as of now, has been informed through our earlier mail yesterday. We shall hook units one by one during these overhauls.

**UNQUOTE** 

OCC advised NTPC to explore final hooking up with C& I system at an opportune S/D time of the unit.

In 129<sup>th</sup> OCC, NTPC explained that after final hooking up with C&I of units they have to conduct dry simulation for checking the successful operation of the scheme which can only be carried out during overhauling.

Further, they informed that the maintenance programme of U#1 is scheduled from 10<sup>th</sup> March, 2017. So the hooking up with unit-I will be completed by March,2017 and the Islanding scheme will be operational. Unit#2 and Unit #3 will be hooked in April, 2017 and June/July, 2017 respectively during their overhauling.

OCC advised NTPC to strictly maintain the schedule so that the FSTPS islanding scheme can be put into service w.e.f. March, 2017.

In 130<sup>th</sup> OCC, NTPC assured to complete the islanding scheme with U#1 of FSTPS and they have requisitioned for shutdown of U#1 w.e.f. 10<sup>th</sup> March, 2017.

NTPC may update.

### **Deliberation in TCC meeting**

NTPC confirmed that the final hooking of U#1 will be completed during overhauling S/D of U-1 in the month of March-April, 2017. They assured FSTPP islanding scheme with U#1 of FSTPS will be operational positively by April 2017 without further delay. On specific queries NTPC informed that except hooking up with units all their assigned works for implementing FSTPS islanding are satisfactorily completed.

ITEM NO. D3:	Status of Bus Splitting schemes in Eastern Region
--------------	---

### A. Bus Splitting of Powergrid Sub-stations

As per decision of Standing Committee of ER CTU was entrusted to do Bus splitting at Maithon, Durgapur & Biharsariff S/Ss or ER. The latest status on the same are:

- 400 kV Maithon --- Completed
- 400 kV Durgapur--Completed
- 400 kV Biharshariff— In 129<sup>th</sup> OCC, Powergrid informed that bus splitting scheme will be completed by February, 2017.

In 130<sup>th</sup> OCC meeting, Powergrid informed that physical bus splitting at 400kV Biharshariff S/s has been completed. Protection part is yet to be completed.

Powergrid added that bus splitting at 400kV Biharshariff S/s will be commissioned by March 2017.

Powergrid may update.

### **Deliberation in TCC meeting**

Powergrid informed that bus splitting at 400kV Biharshariff S/s will be commissioned by March 2017.

### B. Bus Splitting of Kahalgaon STPS Stage I&II, NTPC

In 130<sup>th</sup> OCC, NTPC has given the present status as follows:

- ➤ 400/132kV Switchyard package bid opened on 14.03.16. Awarded on 04.05.2016.
- ➤ Site leveling *Site leveling work has been completed.*
- Transformer package and Shunt reactor—have been awarded.

In 34<sup>th</sup> TCC, NTPC informed that the bus splitting will be completed by December, 2018.

NTPC may update.

### **Deliberation in TCC meeting**

NTPC informed that the work is in progress as per the schedule and the bus splitting will be completed by December, 2018.

ITEM NO. D4:	Status of construction of 400 kV Ind-Barath-Jharsuguda D/C line.
--------------	--

CERC vide order dated 31.08.16 on petition No. 134/MP/2016 clarified the following:

### Quote:

"............The Commission allowed the petitioner to inject infirm power upto 31.7.2016 for the purpose of achieving COD of the unit. It is clarified that even infirm power shall not be allowed for injection after 31.7.2016, the petitioner is stated to have achieved COD on 19.7.2016. In our view, the petitioner should commission the dedicated transmission line at the earliest and inject commercial power through dedicated transmission line. From the point of view of grid security, we cannot allow the petitioner to inject firm power through LILO which was basically a temporary arrangement."

Unquote

In 130<sup>th</sup> OCC meeting, IBEUL informed that construction of the line has been completed and ready for commission. The line will be commissioned by 28<sup>th</sup> February, 2017.

OCC advised IBUEL to communicate the status to ERPC and ERLDC after commissioning of line for commencement of commercial transaction.

IBEUL may update.

### **Deliberation in TCC meeting**

It was informed that IBUEL vide mail has submitted the status of their dedicated line to ERPC and ERLDC on 23-02-2017. TCC advised ERPC secretariat to assess the position and do needful in line with CERC order, regulation and decisions taken in several meetings held on this issue.

ITEM NO. D5:	Status of construction of Chuzachen bay at Rangpo S/s.
--------------	--

Construction of bays at Rangpo S/s meant for evacuation of power from Chuzachen has been undertaken by Department of Power, Govt of Sikkim, under consultancy with Powergrid.

In 33<sup>rd</sup> ERPC, Sikkim placed the road map for construction of the bays as follows:

- Tender will be floated by July 2016
- Bid will be opened by August 2016
- Work will be awarded by September 2016
- Bay will be commissioned by December, 2017

In 34th TCC, Sikkim informed that they are going for retendering in November, 2016.

Sikkim assured that they will commission the bay within the target date i.e. December, 2017.

Sikkim may update. TCC may guide.

### **Deliberation in TCC meeting**

Sikkim informed that retendering work is in progress.

Sikkim assured that they will commission the bay within the target date i.e. December, 2017.

ITEM NO. D6:	Status of construction of dedicated transmission lines of IPPs which
	are connected through interim arrangement

The progress of dedicated transmission lines of IPPs in Eastern Region, which were connected through interim arrangement, was reviewed in 34<sup>th</sup> ERPC meeting held on 19<sup>th</sup> November 2016. Dikchu HEP of Sneha Kinetic Power Projects Pvt. Ltd. is expected to be shortly commissioned on interim arrangement. Therefore, it is proposed that status of dedicated transmission system of Dickhu HEP may also be monitored in ERPC forum. The status of the dedicated transmission lines as reported by IPPs in ER during the last ERPC meeting and Dikchu HEP is summarized below:

Gene	Generation Project in ER connected through temporary LILO arrangement					
Sl. No.	Generation Project	Installed Capacity (in MW)	Present Connectivity through LILO	Final Connectivity Arrangement (not commissioned)	Anticipated Completion Schedule	
1	Vedanta (Sterlite Energy Ltd.)	4x600	LILO of one circuit of Rourkela - Raigarh 400kV D/c line (granted in Sept'09)	Sterlite - Jharsuguda 400kV 2xD/c	Feb'17	
2	Ind Barath Energy (Utkal) Ltd.	2x350	LILO of one circuit of Jharsuguda - Raigarh 400kV D/c line (granted in Sept'09)	Ind Barath - Jharsuguda 400kV D/c	Completed but CEA clearance awaited	
3	Gati Infrastructure Ltd. (Chuzachen)	2X49.5	LILO of Rangpo - Melli 132kV S/c line (granted in Nov'07)	Chuzachen - Rangpo 132kV D/c (with Zebra conductor)	Dec'17	
4	Sneha Kinetic Power Projects Pvt. Ltd. (Dikchu)	2x48	(*) LILO of one circuit of Teesta-III – Rangpo 400kV D/c line (granted in Dec'14 by CERC)	Dikchu – Dikchu Pool 132kV D/c	(\$) To be informed by developer & Sikkim	

<sup>(\*)</sup> Under Implementation. Interim granted vide CERC order in Petition no. 157/MP/2014 dated 03<sup>rd</sup> Dec 2014.

( \$ ) Dikchu Pool S/s is being implemented under Sikkim Comprehensive scheme of Govt. of Sikkim (being implemented by POWERGRID on consultancy). The expected commissioning schedule of Dikchu Pool and dedicated transmission line to be informed by Sikkim and SKPPPL, respectively.

As per CERC order dated 28.09.2016 on Petition no. 30/MP/2014, "CTU shall take up all the existing cases of connectivity on interim LILO with the RPC of respective regions within a period of one month from the date of issue of this order for review and decision on disconnection of the interim arrangements through LILO. All such interim arrangements through LILO shall be disconnected within a period of three months of the issue of this order unless the RPC grants extension for continuation of LILO keeping in view of all relevant factors."

In view of the CERC order, further decision regarding the disconnection of the interim arrangements through LILO may be taken in the ERPC forum.

TCC may deliberate.

### **Deliberation in TCC meeting**

CTU opined that in line with CERC order, they are ready to open the LILOs as per the TCC/ERPC direction.

ITEM NO. D7:	Outstanding issues towards charging of 220kV Biharsharif-Tenughat
HEMINO.D7:	line at 400 kV level

Powergrid vide letter dated 18.01.2017 informed that the scope of POWERGRID for charging the 220kV Biharsharif-Tenughat line at 400 KV level is construction of (a) 01 no. bay and 0.8Km 400 KV transmission line for termination at Biharsarif S/s and (b) 5 nos. bays including Erection, Testing & Commissioning of OSM Equipments (i.e. 2 x 250 MVA ICTs, 50 MVAR L/R) at Tenughat end of TVNL. The detail scope of work with present status is enclosed at **Annexure-B9**.

In this regard, the following points are being put forward for consideration owing to which the balance work could not be completed till date:

### A) Biharsharif S/s End (Deposit work of JUSNL):- Cost Plus Basis.

- a. The balance work at Biharsharif S/s end could not be completed due to irregular and delayed payment in past form JUSNL despite repeated reminders for deposit of fund by POWERGRID. Forcing agencies to demobilized frequently for want of fund. *Still payment of Rs. 48.5 Lakh is pending from JUSNL*.
- b. The said T/L is charged at 220 KV level and BSPTCL is currently drawing power from the said line directly. After charging of the said T/L on 400 KV level, BSPTCL will be deprived of power from Tenughat directly. *This issue has been strongly raised by BSPTCL in ERPC forum*.
- c. Work related to 400 KV bays at Biharsarif is nearing completion and line diversion work will be completed by April-2017.

### B) Tenughat End (TVNL Consultancy project):- Cost Plus Basis.

- a. The balance work at Tenughat end could not be completed due to non-receipt of payment of Rs. 4.07 Crores approx from TVNL despite repeated reminders by POWERGRID. Part payment issues is not resolving.
- b. It is to inform that the agency (M/s Sterling Wilson) at Tenughat end has demobilized from site due to non-receipt of payment. The re-mobilization of agency for completion of balance work shall take approx. 01 month after receipt of pending fund from TVNL. Subsequent to mobilization of agency at site, approx. 03 months shall be required for completion of the balance work at Tenughat end. Other pending issues are enclosed in **Annexure-B9**.
- c. Completion target for above job (B) is by June-17.

34<sup>th</sup> ERPC advised JUSNL to settle the disputes in the bill and do the payment by end of November, 2016. JUSNL agreed.

In 34<sup>th</sup> TCC, Director (Projects), BSPTCL stated that the 4<sup>th</sup> ICT of 500 MVA at Biharshariff must be commissioned in close co-ordination with the up gradation of the subjected line.

Powergrid informed that this ICT may take at least two years as per the schedule.

ERPC requested Powergrid to explore the possibility of diversion of ICT from other projects/region. Director (O), Powergrid agreed to explore.

JUSNL/TVNL/Powergrid may update.

### **Deliberation in TCC meeting**

### A) Biharsharif S/s End (Deposit work of JUSNL):- Cost Plus Basis.

Powergrid informed that payment of Rs. 48.5 Lakh is still pending from JUSNL and they would complete the balance work at Biharsharif S/s end within 2 months from date of receipt of balance payment.

JUSNL has asked some clarifications on balanced payment.

TCC felt that the issue was pending from last two meetings and advised ERPC secretariat to convene a separate meeting at ERPC, Kolkata on 2<sup>nd</sup> March, 2017 at 12:00 hrs to resolve the issues.

TCC advised JUSNL and Powergrid to send their concerned officers at senior level for settlement of the problem.

### B) Tenughat End (TVNL Consultancy project):- Cost Plus Basis.

TVNL informed that yesterday they have paid Rs 2 cr to Powergrid and they will pay the balance amount by March 2017.

Powergrid informed that they need 6 months from date of receipt to complete the work.

TVNL requested Powergrid to complete the work as per the given schedule by June 2017. Further, TVNL pointed that linking at Tenughat switchyard needs some deliberation.

TCC advised TVNL also to attend the special meeting scheduled on 2<sup>nd</sup> March 2017 with higher level participation and with all the details for effective discussion.

ITEM NO. D8: High voltage problem in 400KV Meramundali Grid S/S

GRIDCO vide letter dated 07.01.17 intimated that presently Odisha is going through very high voltages at 400kV bus of Meramundali, Duburi and Mendhashal grid S/S. The situation is further worsened due to high reactive power flow from Meramundali to Angul pooling sub-station, from Duburi to Meramundali sub-station and from Kuchei to Duburi sub-station. It may be noted that, PGCIL has installed two nos. of 330 MVAr Bus reactors at Angul 765kV substation and two nos. of 125 MVAR Bus reactors at Ancul 400kV substation, thus resulting high reactive power flow from Meramundali to Angul & Duburi to Meramundali grid S/S. In view of the above OPTCL suggests the following as short term and long term measures to mitigate the high voltage issue as well as to improve the high reactive power flow situation.

### **Short term measure**

- OPTCL will install 80 MVAr reactor at Meramundali 400kV S/S.
- The Angul-Meramundali Double circuit tie to be opened at both ends.

### Long term measure

• The Meramundali-Angul Double circuit will be terminated at Meramundali (B). A letter regarding the above change has already been forwarded to CEA and will be placed in the next Standing Committee meeting of CEA. Meremundali(B) will be a new 400kV substation of OPTCL, approved by CEA and the work order to be issued shortly.

In view of the above and as the high voltage situation is menacing, it is requested to grant permission for the short term measures, mentioned above, to get relief from the high voltage issue and high reactive power flow. The system in the above condition will remain stable.

In 129<sup>th</sup> OCC, OPTCL informed that they are incurring substantial financial loss on account of reactive charges due to this overvoltage problem at 400 KV Meramundali substation and requested to explore the high voltage scenario by opening of 400 kV Angul-Meramundali D/C tie on trial basis.

ERLDC informed that the same may be granted as per real time grid conditions.

Further, OPTCL requested OCC to take up the issue of opening of LILOs of 400 kV Talcher-Meramundali & Bolangir –Meramundali lines at 765/400 kV Angul S/s which was already decided in 17<sup>th</sup> SCM meeting.

In 17<sup>th</sup> SCM it was pointed that the 400 kV LILO lines are feeding the load centres of Orissa at Meramundali and Mendasal. It is proposed that the above LILOs at Angul pooling station may not be disconnected. Instead, switching arrangements may be made at Angul substation such that above 400 kV LILOs may be operated either by-passing Angul substation or terminating at Angul

substation as and when required, depending upon the power flow condition. Members agreed to the proposal as a part of Easter Region strengthening scheme-17 (ERSS-17)

The issue was also discussed in the special meeting on High voltage issues of ER, the minutes of the meeting is enclosed at Annexure-B10. In the meeting it was decided that OPTCL would ensure absorption of maximum possible reactive power (as per capability curve) by the units of JSPL, Vedanta and GMR(Odisha). Also, OPTCL should endeavor to restore the 50MVAR line reactor at Meramundali end of Vedanta-Meramundali-I at the earliest.

The issue was placed in 129<sup>th</sup> OCC and OCC viewed that as it is the matter related to Standing Committee of ER the same may be taken up with CEA/CTU.

Subsequently, MS took up the issue with CTU and it was agreed that ERLDC will carry out study for Reactive power flow in OPTCL system.

In 130<sup>th</sup> OCC, ERLDC has presented the study results and informed the following:

- The voltage at Meramundali is increasing during winter season due low demand at Meramundali, Dubri and Mendhasal and insufficient reactive power support.
- In the present scenario the 765/400 kV Angul S/s is acting like sink of Reactive power for OPTCL system in around 400kV Meramundali S/s.
- With opening 400kV Angul-Meramundali line the export of reactive power to the ISTS network is reduced drastically but the voltage at 400kV Meramundali S/s is increasing by 4 kV which may affect the sub-station equipment.
- Further due to outage of one ckt of 400 kV Meramundali- Mendhasal the voltage at Meramundali is on higher side. This line may be restored at the earliest.

*OPTCL* informed that 400 kV Meramundali- Mendhasal line will be restored within a week and 315 MVA, 400/220kV ICT will be restored by 15<sup>th</sup> March, 2017.

OCC advised OPTCL to plan for adequate reactive power compensation at 400kV Meramundali, New Dubri and Mendhasal S/s as a long term a measure.

ERLDC may elaborate. TCC may guide.

### **Deliberation in TCC meeting**

ERLDC informed that VAR is being generated at OPTCL system and the 765/400 kV Angul S/s is acting like sink of Reactive power for OPTCL system in around 400kV Meramundali S/s. The opening of 400kV Angul-Meramundali line will not the solution. Further due to outage of one ckt of 400 kV Meramundali- Mendhasal the voltage at Meramundali is on higher side. This line may be restored at the earliest.

*OPTCL* informed that 400 kV Meramundali- Mendhasal line will be charged on tomorrow and 315 MVA, 400/220kV ICT will be restored by 15<sup>th</sup> March, 2017.

Powergrid informed that the flexible LILO scheme as approved in 18<sup>th</sup> SCM was approved in their Board and it is in final stage and the scheme will be implemented by 2018.

TCC opined that the high voltage issue should be reviewed after restoration of 400 kV Meramundali- Mendhasal line and commissioning of 315 MVA, 400/220kV ICT at Meramundali in OCC meeting.

TCC advised all generators in around 400kV Meramundali S/s to absorb VAR up to maximum extend as per the capability curve. TCC also advised OPTCL to plan for proper reactive power compensation at 400kV Meramundali, New Dubri and Mendhasal S/s.

CE, CEA opined that reactive power compensation is part of grid security and it is eligible for PSDF grant. OPTCL may apply for PSDF.

ITEM NO. D9: Status of PLCC system installed in Eastern Region

### 1) Restoration of PLCC system of important lines of JUSNL

### I) 220 KV Chandil –Santaldih line

In 130th OCC meeting, JUSNL intimated that PLCC for 220 kV Chandil-Santaldih line has been tested and commissioned successfully on 25.01.17.

WBPDCL informed that the PLCC was activated but the auto-reclosure could not be put into service as the R-Ph pole of Circuit Breaker is not getting closed during auto-reclosure operation. The same is taken up with the OEM (i.e. ABB) and they will be rectifying the CB.

### II) 220 KV Ramchandrapur-Joda line

In 130th OCC meeting, OPTCL informed that PLCC panels at 220kV Joda end will be commissioned within a week. JUSNL informed that the Ramchandrapur end is ready in all respect for implementation of PLCC.

JUSNL/WBPDCL/OPTCL may update.

### **Deliberation in TCC meeting**

WBPDCL informed that overhauling of the R-ph pole of CB will be done by 15<sup>th</sup> March 2017. Subsequently, auto-reclosure feature will be enabled.

OPTCL informed that PLCC panels at 220kV Joda end will be commissioned by March 2017.

### 2) Restoration of PLCC system of important lines of OPTCL and BSPTCL

In 34<sup>th</sup> TCC, OPTCL updated the latest status as follow:

- 1. Jeypore(PG)-Jayanagar (Commn. in OPGW exists): SDH tendering is in progress
- 2. Rourkela(PG)-Tarkera (Commn. in OPGW exists): SDH received commissioning by January, 2017
- 3. Rengali(PG)-Rengali S/Y (Proposal for Commn. in OPGW is pending): tendering is in progress
- 4. Indravati(PG)-Indravati(PH) (Proposal for Commn. in OPGW pending): tendering is in progress
- 5. Baripada(PG)-Baripada (Tendering in Progress for OPGW): Contract awarded
- 6. Baripada(PG)-Rairangpur (Tendering in Progress for OPGW): Contract awarded

BSPTCL informed the latest status as follows:

- 1. 220kV Patna-Fatua S/C line---Will commission the PLCC system by 31st December, 2016
- 2. 220kV Patna-Khagul S/C line---Will commission the PLCC system by 31st December, 2016
- 3. 220kV Gaya-Dehri D/C line--- The line is under breakdown. After coming of line in service, the work will be completed within another one month.
- 4. 220kV Gaya-Bodhgaya D/C line--- There is T-connection in line after removal of T connection PLCC will be installed.

Further, in PCC meetings the need of PLCC system was felt for the following lines of BSPTCL:

- 1. 220kV Purnea (PG)-Madhepura line
- 2. 220 kV Biharshariff- Begusarai line
- 3. 220 kV Biharshariff- Bodhgaya line

UNDER JURISDICTION OF BSPTCL

OPTCL and BSPTCL may update.

#### **Deliberation in TCC meeting**

OPTCL informed that PLCC system for Rourkela(PG)-Tarkera (Commn. in OPGW exists) line will be commissioned by March, 2017.

BSPTCL updated the following.

- 1. 220kV Patna-Fatua S/C line---*PLCC system has been installed and relays were reconfigured. PLCC system will be commissioned by March, 2017*
- 2. 220kV Patna-Khagul S/C line--- *PLCC system has been installed and relays were reconfigured. PLCC system will be commissioned after completion of re-conductoring work*
- 3. 220kV Gaya-Dehri D/C line--- PLCC system has been installed and relays were reconfigured. PLCC system will be commissioned by March, 2017
- 4. 220kV Gaya-Bodhgaya D/C line--- *PLCC system has been installed and relays were reconfigured. PLCC system will be commissioned by March, 2017*
- 5. 220kV Purnea (PG)-Madhepura line
- 6. 220 kV Biharshariff- Begusarai line

Digital PLCC will be implemented.

7. 220 kV Biharshariff- Bodhgaya line

**ITEM NO. D10:** 

**Opening of LC by ER constituents for Deviation Charges Payments** 

Clause 10 (4) of CERC Deviation Settlement Mechanism and related matters Regulations, 2014 vide notification No. L-1/132/2013/CERC dated 6<sup>th</sup> January, 2014 to be implemented from 17.02.2014 is reproduced below:

#### Quote

All regional entities which had at any time during the previous financial year failed to make payment of Charges for Deviation including Additional Deviation Charges for Deviation within the time specified in this regulations shall be required to open a Letter of Credit (LC) equal to 110% of its average payable weekly liability for Deviations in the previous financial year, in favour of the concerned RLDC within a fortnight from the date these Regulations come into force.......

......Provided further that LC amount shall be increased to 110% of the payable weekly liability in any week during the year, if it exceeds the previous LC amount by more than 50%.

Unquote

As intimated by ERLDC, the details of LC amount required to be opened in 2016-17 by ER constituents is given in **Annexure – B14.** Letters to this effect has already been issued by ERLDC to the defaulting entities viz, BSPHCL, JUVNL, GATI, SIKKIM and Ind Barath. Rest of the constituents which were required to open/recoup the LC, they have opened/recoup the LC.

In the last CCM on 06.02.2017, BSHPCL informed that they would get the LC opened by the end of February, 2017. JUVNL informed that the matter had been taken with their bank and LC would be opened shortly. Sikkim representative was not present.

ERLDC may update.

#### **Deliberation in TCC meeting**

BSPHCL informed that they have renewed their LC. GATI informed that LC will be opened shortly. Sikkim informed that LC will be opened by March, 2017.

ITEM NO D11.	HIGH AMOUNT OF DEVIATION CHARGES PAYABLE BY BSEB
ITEM NO. D11:	ON ACCOUNT OF M/s. TALA HEP

SBPDCL vide letter dated 07.01.17 informed that the deviation charges incurred by M/s TALA HEP are to be borne by its beneficiaries, and BSEB being a major beneficiary, having a share of 25.5% has to bear a major portion of these deviation charges.

For the last 8 weeks, it has been observed, to their great concern that the deviation charges incurred by M/s TALA HEP have been continually high, amounting to as high as few crores per week. A summary report of the amount incurred by M/s TALA HEP as deviation charges, and consequently the amount to be borne by BSP(H)CL erstwhile BSEB was also submitted.

From the statistics in this table; & discussion with ERLDC, it was concluded that a major percentage of bill for UI & Deviation payable by BSP(H)CL erstwhile BSEB, is on account of huge deviation charges incurred by M/s TALA HEP.

As such, ERLDC should keep scheduled generation near to actual generation or devise a mechanism to make deviation zero or minimum. Beneficiaries should not be charged for the high declared capacity (DC) given by TALA or CHUKHA HEP, as they are not responsible for the high mismatch between scheduled generation and actual generation of Bhutan generating station.

So, it was requested that the future scheduling for power purchase on behalf of M/s TALA HEP and M/s CHUKHA HEP should be done keeping in mind the concerns of its beneficiaries.

In 129<sup>th</sup> OCC, MS- ERPC assured that the matter is under consideration and will be resolved at the earliest.

In 130<sup>th</sup> OCC, ERPC/ERLDC explained the adjustment of Tala, and Chukha power in DSM and Regional Energy Accounting of ERPC. It was informed that the there is no applicability of DSM for Tala/Chukha power. However, in DSM Account the deviation of Tala/Chukha is being adjusted at their respective rates not at frequency variable DSM rate.

BSPTCL may note.

#### **Deliberation in TCC meeting**

SBPDCL pointed that they need some more clarification on the issue.

TCC advised SBPDCL to interact with ERPC Secretariat and resolve the issue.

ITEM NO. D12:	Operationalization of LTA for BRBCL
---------------	-------------------------------------

In the special meeting on the issue of Scheduling of BRBCL station which was held on 25<sup>th</sup> January, 2017 at Kolkata, it was decided that CTU will notify Operationalization of LTA after detailed studies before ensuing 35<sup>th</sup> TCC/ ERPC meetings. LTA will be operationalized upto the state periphery with total available transfer capability from the station.

CTU may update.

#### **Deliberation in TCC meeting**

It was informed that BRBCL has filed a petition before CERC and the issue is pending with CERC. Therefore the agenda was dropped and no discussions were held.

ITEM NO. D13:	Very high loading of 220kV Muzaffarpur(PG)-Kanti D/C line
---------------	---

Due to heavy import by BSPHCL at Muzaffarpur, power flow through the said line generally remains above 150MW/ckt and even crosses 195 MW/ckt in the peak. Though the situation is likely to ease after commencement of generation at KBUNL Stg-2, for facilitating planned shutdown of the line, it is desirable to have additional 220kV circuits in parallel to the existing line. In the 34<sup>th</sup> TCC meeting it was informed that circuits 3 and 4 between Muzaffarpur(PG) and and Kanti (Extn) would be completed by November, 2016.

BSPTCL / PGCIL may kindly expedite commissioning of 220kV circuits 3 and 4 between Muzaffarpur(PG) and Kanti (Extn).

BSPTCL/Powergrid may update.

#### **Deliberation in TCC meeting**

Powergrid informed that 2 nos line bays will be commissioned at Muzaffarpur by March 2017 but the line construction is not in the scope of Powergrid.

BSPTCL informed that there is uncertainty in commissioning of line. However, BSPTCL is taking measures to relive the overloading of 220 kV Muzaffarpur-Kanti.

ITEM NO. D14:	Augmentation	of	$400/220 \mathrm{kV}$	<b>ICT</b>	capacity	at	Maithon,	Patna,
TIEM NO. D14:	Sasaram, Bihai	rsha	riff					

ICTs of (1X315+1X500) MVA capacity exists at Maithon, Patna and Sasaram. In the peak period, the total power catered by each of the sub-stations is high enough to cause tripping of the parallel 315MVA ICT, if the 500MVA ICT trips. Similarly, if one out of the 3X315 MVA ICTs at Biharshariff trips, the other two ICTs are also likely to trip on overload.

The 315 MVA ICTs at Patna and Sasaram are already planned to be replaced by 500MVA ICTs while a 500MVA ICT is scheduled to be added each at Maithon and at Biharshariff.

As the peak demands of Bihar and DVC systems are likely to rise sharply in the coming summer season, PGCIL may kindly expedite augmentation of 400/220kV ICT capacities at the above mentioned sub-stations

Powergrid may update.

#### **Deliberation in TCC meeting**

Powergrid informed that the augmentation 400/220kV ICTs at Maithon S/s will be completed by July, 2017.

Powergrid added that type test of 400/220kV ICT of Sasaram and Patna S/s has been failed and the design of the ICT is being reviewed by OEM. The augmentation of 400/220kV ICTs at Sasaram and Patna will take time.

Powergrid also informed that augmentation of 400/220kV ICTs at Biharshariff will take one and half year.

Bihar requested Powergrid to divert ICTs from any other sub-stations for early argumentation at Biharsariff, Sasaram and Patna S/s. Bihar added that immediate argumentation of ICTs at Biharsariff S/s is essential to meet increasing demand in Bihar.

Powergrid informed that diversion of ICT to Biharshariff S/s is not possible at this juncture. However Powergrid assured to explore further possibilities to expedite.

ITEM NO. D15: Commissioning of 125 MVAR bus reactor at Jamshedpur	
---	--

Voltage of 400kV Jamshedpur remains above 420kV (IEGC upper limit) for nearly 100% of the time.

In the Standing Committee Meeting of ER held on 05-01-2013, it was inter-alia agreed to install 2X125 MVAR bus reactors in parallel with the existing 2X50 MVAR reactors at Jamshedpur. The same decision was reiterated in the next Standing Committee Meeting of ER held on 02-05-2014. While 125 MVAR reactors for voltage control have been installed by PGCIL at Rourkella, Patna, Sasaram, Maithon, Durgapur etc. the reactors at Jamshedpur are yet to be commissioned. PGCIL

may be requested to kindly accord topmost priority in mitigating high voltage at Jamshedpur and expedite installation of the 125 MVAR reactors there.

In 130<sup>th</sup> OCC, ERLDC informed that severe high voltage is being observed at 400kV Jamshedpur S/s on continuous basis and advised Powergrid to commission 2X125 MVAR bus reactors at the earliest.

Powergrid informed that the reactor will be commissioned by April, 2017.

Powergrid may update.

#### **Deliberation in TCC meeting**

Powergrid informed that the reactor will be commissioned by May, 2017.

ITEM NO. D16:	Priority-based commissioning of bus reactor for control of high voltage during lean periods

*In 34<sup>th</sup> TCC, Powergrid updated the latest status as follows:* 

S.N.	Reactor	Status
1	125 MVAR reactor of Jeypore	Commissioned
2	125 MVAR Bus reactor of	
	Jamshedpur	Expected commissioning by Feb'17
3	125 MVAR Bus reactor of	(Jamshedpur) and Jan'17 (Biharshariff)
	Biharshariff	
4	Additional bus-reactor of 125	Will be made available for commissioning
	MVAR capacity at Beharampur	by Oct, 2017.
	on urgent basis.	
5	50 MVAR at Behrampur on	Reactor has reached Behrampur.
	urgent basis by diverting from	Commissioning by Nov'16 end.
	Rourkela which is kept as a spare	

Powergrid may update the latest status.

#### **Deliberation in TCC meeting**

OPTCL informed that the high voltage problem persists even after the commissioning of 125MVAR reactor at Jeypore.

TCC referred the issue to OCC for further deliberation.

ITEM NO. D17:	Status of Transmission projects approved in various meetings
---------------	--

The status as updated in 34<sup>th</sup> TCC/ERPC meeting on transmission projects approved to various meetings is given below:

Sl No.	Scheme	ERPC/SCM Meeting	Latest status
1	Modification of 132 kV Bus arrangement at 220/132 kV Birpara S/s of Powergrid from existing single main & transfer bus scheme to double mainscheme.	28 <sup>th</sup> ERPC Meeting	Powergrid informed that the work undr progress and expected commissioning by Aug'17.
2	Change in proposed the Associated 765 kV System Strengthening Scheme in ER	28 <sup>th</sup> ERPC Meeting	Under TBCB
3	Retrofitting of pilot wire protection of 132 kV Purnea (PG) – Purnea (BSPHCL) feeders	26 <sup>th</sup> ERPC Meeting	Powergrid informed that the scheme was covered in the scheme of modification of 132 kV Bus arrangement at 220/132 kV Purnea S/S of Powergrid under GIS package. The work has been awarded and expected to be completed by Jan'17.
4	Transmission System for immediate evacuation of power from North Karanpura STPP (3x660 MW) to Chandwa and Gaya Pooling stations of Powergrid	25 <sup>th</sup> ERPC Meeting	T/L is under TBCB, POWERGRID informed that Chandwa bay awarded and for Gaya tendering activity under progress.
5	Procurement of two single phase spare ICT units (2x500 MW), 765/400 kV for Eastern Region - to be stationed at Angul&JharsugudaS/S).	25 <sup>th</sup> ERPC Meeting	Powergrid informed that work has been awarded on March, 2015 and expected to be completed by Mar'17.
6	Augmentation of transformation capacity at the existing 400/220 kV Jamshedpur (PG) &Sasaram (PG)S/S	25 <sup>th</sup> ERPC Meeting	Powergrid informed that for Sasaram-  1 <sup>st</sup> ICT commissioned, 2 <sup>nd</sup> ICT in supply, expected commissioning by Mar'17. For Jamshedpur, commissioning expected to be completed by November, 2016
7	Establishment of 220 kV MTPS (Extn.) – Muzaffarpur (PG) D/C line (3 <sup>rd</sup> & 4 <sup>th</sup> Circuits)	25 <sup>th</sup> ERPC Meeting	Bay construction at Muzaffarpurto be done by Powergrid under consultancy projected. Expected to be completed by Dec,2016.
8	Modification of 132 kV Bus arrangementat 220/132 kV Siliguri S/S(PG)	25 <sup>th</sup> ERPC Meeting	Powergrid informed that the work has been awarded and expected to be complete by November,2016.
9	Procurement of 110 MVAR, 765 kV Single Phase spare Reactor unit at Sasaram	25 <sup>th</sup> ERPC Meeting	Powergrid informed that the work has been awarded on March, 2015 and expected to be delivered by Mar' 2017.
10	Establishment of Gazol 220/132 kV S/S in Malda by LILO of Malda-Dalkhola 220 kV D/C line of Powergrid	25 <sup>th</sup> ERPC Meeting	Not pertaining to POWERGRID
11	Construction of down linking transmission network for drawal of power from Kishanganj 400/220 kV S/S ofPowergrid	25 <sup>th</sup> ERPC Meeting	Powergrid informed that four numbersof 220 kV bays at 440 kV Kishanganj (PG) for 2xD/C 220 kV Kishanganj (PG)-Kishanganj (BSPHCL) will be under regional scheme as informed by CEA. Powergrid bays ready, 2 bays charged and another 2 no. bays expected in Dec'16.

12	Modification of 132 kV Bus arrangementat 220/132 kV Purnea S/S ofPowergrid	25 <sup>th</sup> ERPC Meeting	Powergrid informed that the scheme will be implemented by Jan'17.
13	Single phase spare converter transformer units of 1x234MVA for pole 1 and 1x201.2 MVA for pole 2 at 2x500 MW HVDC Back-to-Back station at Gazuwaka (one for eachpole)	25 <sup>th</sup> ERPC Meeting	NIT completed. OBD scheduled by end Nov'16
14	GIS bays for 400 kV, 125 MVAR Bus Reactor atBaripada	24th ERPC Meeting	Powergrid informed that the work has been awarded and expected to be completed by 3 <sup>rd</sup> qtr of 2017-18.
15	Eastern Region Strengthening Scheme- XV; Construction of Farakka—Baharampur 400kV D/C (HTLS) line and Subsequent modification of LILOs	17th SCM & 30th ERPC	Linked with Bangladesh, Work awarded and construction of line under progress, expected completion by 2 <sup>nd</sup> Qtr. 2017-18.
16	Installation of 3rd 400/220 kV ,1 x31 5 MVA ICT at Durgapur & New Siliguri Substation	17th SCM & 30th ERPC	NIT done in Sept'16 and Award to be done by Dec' 16
17	Commissioning of 2xl60 MVA, 220/132 kV Auto transformer at Daltonganj substation along with 4 number of 132 kV line bays	17th SCM & 30th ERPC	Award placed, work under Progress, expected commissioning by Jun'17.
18	Extension of under construction 400kV D/C Latehar-Essar lines up to 400kV Chandra Pooling station(PG), under the scope of JUSNL	17th SCM & 30th ERPC	JUSNL to inform
19	Establishment of 2x500 MVA 400/220kV sub-station at Dhanbad by LILO ofboth circuits of Ranchi-Maithon RB 400 kV D/C line atDhanbad	17th SCM & 30th ERPC	Under TBCB
20	Construction of 6 no. 400 kV line bays and bus splitting (765 kV & 400kV) arrangement at Jharsuguda (Sundargarh) as GIS	17th SCM & 30th ERPC	Award placed, work under progress and expected completion by 3 <sup>rd</sup> Qtr. Of 2017-18.
21	Reconductoring of Maithon RB-Maithon 400 kV D/C line with HTLS conductor	17th SCM & 30th ERPC	NIT to be done in Nov'16.
22	Installation of 3rd 400/220 kV 500 MVA Transformer at Muzaffarpur	17th SCM & 30th ERPC	
23	Construction of North Karanpura— Gaya 400 kV D/c & North Karanpura -Chandwa (Jharkhand) Pooling Station 400 kV D/c	17th SCM & 30th ERPC	T/L is under TBCB route, Bay extn. Scope under POWERGRID. Chandwa bay awarded and for Gaya tendering activity under progress.

Further, Powergrid may update the present status on transmission projects approved/revised in  $18^{th}$  SCM which are as given below:

Sl No.	Scheme	ERPC/SCM Meeting	Latest status
1	LILO of both circuits of Bongaigaon-Silliguri 400 kV D/c (Quad) (under TBCB) line at Alipurduar on multi circuit tower for about 2 km	18th SCM	

2	LILO of both circuits of Rourkela-Raigarh 400kV D/c (2nd line) at Jharsuguda on multi circuit towers for about 17 km	18th SCM
3	Installation of 400/220 kV, 1x500 MVA ICT at Gaya S/s (400kV bay in AIS and 220kV bay in GIS)	Scheme revised in 18 <sup>th</sup> SCM
4	Replacement of 400/220kV, 2x315MVA ICTs at Malda S/s with 400/220kV, 2x500 MVA ICTs	Scheme revised in 18th SCM
5	Installation of 3rd 400/220kV, 1x315MVA ICT at New Siliguri S/s: to be sourced from pool of spare ICTs (400kV bay in GIS and 220kV bay in AIS)	Scheme revised in 18th SCM
6	Installation of 3rd 400/220kV, 1x315 MVA ICT at Durgapur S/s: to be sourced from pool of spare ICTs	Scheme revised in 18th SCM
7	Installation of 400/220kV, 2x315MVA ICTs at Jeypore S/s (one each in parallel to the existing ICTs): to be sourced from pool of spare ICTs.	Scheme revised in 18th SCM
8	Installation of 400/220kV, 2x315MVA ICTs at Rourkela S/s (one each in parallel to the existing ICTs): to be sourced from pool of spare ICTs	Scheme revised in 18th SCM
9	Bypassing arrangement of LILO of Meramundali – Bolangir/Jeypore 400kV S/c line and LILO of one circuit of Talcher – Meramundali 400 kV D/c line at Angul	18th SCM
10	installation of 400/220kV, 500MVA ICT (4th) at Biharsharif S/s	18th SCM
11	Establishment of 2x500MVA+2x160 MVA+2x80 MVA 400/220/132 kV S/S at Naubatpur	18th SCM
12	Establishment of 2x500 MVA +2x160 MVA 400/220/132 kV GIS S/S at Bakhtiyarpur	18th SCM
13	Establishment of 2x500 MVA +3x160 MVA+3x80 MVA 400/220/132/33 kV GIS S/S at Jakkanpur	18th SCM
14	Establishment of 400/220/132kV, 2x500MVA + 2x200MVA new S/s at Sitamarhi	18th SCM
15	2x125MVAr, 420kV bus reactors along with bays	18th SCM
16	Darbhanga – Sitamarhi (New) 400kV D/c (Triple Snowbird) line	18th SCM
17	Sitamarhi (New) – Motihari 400kV D/c (Triple Snowbird) line	18th SCM
18	Establishment of 400/220/132kV, 3x500MVA + 3x200MVA new S/s at Chandauti	18th SCM
19	2x125MVAr, 420kV bus reactors along with bays	18th SCM

20	LILO of both circuits of Nabinagar-II – Gaya 400kV D/c (Quad) line of POWERGRID at Chandauti (New)	18th SCM	
21	Establishment of 400/220/132kV, 2x500MVA + 2x200MVA new S/s at Saharsa	18th SCM	
22	2x125MVAr, 420kV bus reactors along with bays	18th SCM	
23	LILO of Kishanganj – Patna 400kV D/c (Quad) line of POWERGRID at Saharsa (New)	18th SCM	
24	Installation of 400/132kV, 315MVA (3rd) ICT at Motihari substations of Essel Infra	18th SCM	
25	Installation of 400/132kV, 315MVA (3rd) ICT at Banka and Lakhisarai substations of POWERGRID	18th SCM	
26	Reconductoring of Rangpo – Siliguri 400kV D/c Twin Moose line with Twin HTLS conductor along with suitable modification in line bay equipment at both ends	18th SCM	
27	Installation of 4th 220/132kV, 100MVA ICT at Rangpo S/s	18th SCM	
28	Conversion of fixed line reactor at Purnea end of Kishanganj – Purnea 400kV D/c line to switchable line reactor	18th SCM	
29	a) Nabinagar-II – Gaya 400kV D/c line with Quad moose conductor (b) Nabinagar-II – Patna 400kV D/c line with Quad moose conductor (c) Additional 1x1500MVA, 765/400kV ICT at Gaya	18th SCM	
30	Derang - Angul 400 kV D/C line along with two 400kV line bays at Angul S/s	18th SCM	
31	Installation of 400/220kV, 500MVA ICT (3rd) at Maithon	18th SCM	
32	replacement of existing 50MVA, 220/132 kV ICT at Malda with new 160 MVA, 220/132 kV ICT	18th SCM	
33	Installation of 420kV, 1x125MVAR bus reactor at Subhasgram S/s of POWERGRID	18th SCM	
34	Provision of 765kV, 80MVAr single phase spare reactor at Ranchi (New) substation of POWERGRID	18th SCM	

Powergrid may update the latest status.

### **Deliberation in TCC meeting**

Powergrid submitted the latest status. The same has been incorporated in TCC minutes.

ITEM NO. D18: Status of Spare Transformers & Reactors approved in various meetings

The status updated as in 34<sup>th</sup> TCC/ERPC meeting on Spare transformers & reactors to be commissioned by Powergrid for use in ER.

Sl No.	Sparetransformer/reactor	Latest status	
1	1 X 315 MVA, 400/220 KV AUTO TRANSFORMERBiharshariff	Available at site.	
2	1 X 315 MVA, 400/220 KV AUTO TRANSFORMERDurgapur	Utilized at 400 kV Farakka. Procurement of spare ICT is under process.	
3	1 X 80 MVAR SHUNT REACTOR AS O&M SPARE RourkelaSubstation	Available at site.	
4	2 X 500 MVA, 765/400 KV single phase ICTs at Angul&Jharsuguda.	Powergrid informed that the work has been awarded on March, 2015 and expected to be delivered by Mar'17.	
5	1 X 110MVAr, 765KV single phase bus reactor at Sasaram	Powergrid informed that the work has been awarded on March, 2015 and expected to be delivered by Mar,2017.	
FOR	MEMBERSTATES:		
1	2 X 315 MVA 400/220 kvICTs	Available	
2	2 X 160/150 MVA 220/132 kvICTs	One ICT utilised at Purnea S/s,2 <sup>nd</sup> ICT available at SiliguriS/s.	
3	1 X 50 MVA 132/66 kvICT	Available	
SUR	SURPLUS FROM OLD ASSPARE		
1	3x 50 MVA, 220/132kV (to be released fromMalda (2nos.) &Birpara (1no.)S/Ss	Replaced with 160MVAtransformer.	
2	2x100 MVA, 220/132kV (to be released from one at Birpara& one at Siliguri)	Taken out and kept at Birpara and Siliguri	
3	2x100 MVA, 220/132kV (to be released from Purnea (2nos.)S/Stn.)	Taken out and kept at Purnea	

DVC vide mail dated 15.02.17 intimated that DVC is in urgent need of a 220KV/132KV ICT which is to be installed at 220KV Dhanbad S/Stn. Availability of spare 160MVA 220/132KV ICT as available at Siliguri S/Stn under the head of "FOR MEMBER STATES." may kindly be conveyed so that necessary formalities can be completed at the appropriate level. The said transformer under subject is a NEW or OLD along with the NAMEPLATE DETAILS may also be kindly conveyed.

Powergrid may update the latest status.

#### **Deliberation in TCC meeting**

Powergrid submitted the latest status which is as given below:

1 X 315 MVA, 400/220 KV AUTO	Under procurement stage. Awarded to M/S.		
TRANSFORMER At Durgapur.	TBEA.		
FOR MEMBER STATES			
2 X 160/150 MVA 220/132 KV ICTs	There is no direct communication received from DVC.		
	Transformer kept at Siliguri is NEW. Name plate details attached. This is procured for handling the contingency requirement of O&M needs. Even though the urgent augmentation required at Malda S/S (PG), WBSETCL is providing their spare unit on loan instead of using this spare ICT identified for O&M needs.		
2 X 315 MVA 400/220 KV ICTs	Available.		
1 X 50 MVA 132/66 KV ICT	Consumed at Gangtok, faulty unit send to factory for repair. (M/s Kanwar, Meerut)		
SURPLUS FROM OLD AS SPARE			
3x 50 MVA, 220/132kV (to be released From Malda (2nos.) & Birpara (1no.) S/S	Already decided to sell as scrap. , With MSTC for tender		
2x100 MVA, 220/132kV (to be released from one at Birpara & one at Siliguri)	Already decided to sell as scrap, in process of scrapping		

ITEM NO. D19:	Persistent over drawl by Jharkhand
---------------	------------------------------------

It has been observed since last few month, Jharkhand is over drawing continuously to the tune of 1.5 to 2mu per day. Jharkhand overdraw for the month November, December and January 2017 were around 40 mu, 63 mu and 52 mu respectively. Several times Jharkhand also advised to take un-requisition surplus power of NTPC plant on real time basis. However the quantum requisitioned by Jharkhand for URS power of NTPC plants was very less compare to its overdraw quantum. Numbers of instructions were also issued from ERLDC Control Room during real time operation to Jharkhand regarding the same issue. However the response of Jharkhand was not commensurate with criticality of the situation. Details of above violations would be presented by ERLDC for discussions/suggestions.

In 130<sup>th</sup> OCC, ERLDC presented the schedule and drawal of JUSNL enclosed at Annexure-B26 and informed that JUSNL is overdrawing on continuous basis.

OCC advised JUSNL to explore for procurement of URS power to minimize the over drawal.

JUSNL informed that they have taken up the issue of URS power procurement with JBVNL but action is yet to be taken by JBVNL.

JBVNL may update.

#### **Deliberation in TCC meeting**

ERLDC informed that after last OCC meeting also Jharkhand is over drawing continuously even though URS power is available. Jharkhand also not paying DSM charges.

TCC took serious concern of this matter and advised JBVNL to avail the URS power available in different NTPC stations to meet their demand.

JBVNL assured that they will avail the URS power.

ITEM NO. D20: Commissioning of Tie bay and main bay of BUS-I of 400 kV Ranchi-New Ranch-I & II circuit at Ranchi Substation

400kV Ranchi-Ranchi ckt-I & II has been commissioned on 30.03.2014 through main its main bay (Bay no. 427 and 430 respectively) and connected to BUS-II only at 400/220kV Ranchi Substation.

The commissioning of Tie bays (Bay no. 426, 429) and main bays (Bay nos. 425, 428) connected to BUS-I of Ranchi-New Ranchi ckt.-I & II were in the scope of M/s Corporate Power Ltd. The party M/s Corporate Power Ltd has commenced their work in the year of 2009 and after erection of switchyard equipment they left the site in the year of 2012 citing bankruptcy of the company. As information gathered from sources , M/s Corporate Power Ltd will not commission the bays for Chitarpur ckt-I & II i.e bay nos. 425,426, 428 & 429.

Due to connection of 400kV Ranchi-New Ranchi 1 & 2 with BUS-II only and the therefore lines are very much unreliable as because in case of S/D of main BUS-II, both the line will remain out of service. Further in case of any fault in their main bay, the line will be out of service.

Hence, it is requested that the above mentioned uncompleted bays may be commissioned by POWERGRID and cost of construction may be capitalized by POWERGRID. OR complete asset may be transferred to POWERGRID and POWERGRID will commission the bays and capitalized the same.

TCC may discuss.

#### **Deliberation in TCC meeting**

TCC technically agreed for commissioning of bays of Chitarpur ckt-I & II i.e bay nos. 425,426, 428 & 429.

TCC expressed that acquiring/modification of assets of Corporate Power Ltd. may create legal problems and advised Powergrid to discuss the issue with Corporate Power Limited to arrive at fruitful decision.

Further, Powergrid was also advised to take up the issue with CERC for amicable solution.

ITEM NO. D21 :	Issues related to associated / downstream systems—Powergrid
----------------	---

#### **BIHAR**

i. 4 nos. 220 kV GIS Bays at Kishenganj under ERSS XII:

2 nos. bays have been commissioned. Program for utilisation of balance 02 no. 220kV line bays to be confirmed by BSPTCL.

#### **JHARKHAND**

i. 4 nos. 220 kV & 4 nos. 132 kV bays at Daltonganj S/S (Anticipated Commissioning – June'17): Status of downstream is as under:

4 nos. 220 kV bays to be connected to 220 kV D/CDaltonganj-Garhwa and 220kV D/CDaltaonganj-Latehar (presently charged at 132 kV). Presently only 220 kV Daltonganj-Latehar charged at 132 kV is available. Plan for completion of 220 kV Daltonganj-Garhwa line and Garhwa S/S to be confirmed by JUSNL.

ii. 4 nos. 132kV bays to be connected to 132kVD/C Daltonganj-Chhatarpur and 132kV Daltonganj (PG) – Daltonganj (JUSNL) :

132kV bays at Daltonganj (PG) to becharged through LILO of 220kV Daltonganj-Latehar line (Presently charged at 132kV). Program for utilisation of above bays to be confirmed by JUSNL.

#### **ODISHA**

- i. 4 nos. 220 kV bays at Bolangir S/S: Out of total 4 nos. 220 kV line bays, 2 nos. are commissioned during Feb'16 and 2 nos. are pending due to unavailability of 220 kV lines of OPTCL. Program for utilisation of balance 2 no. bays to be confirmed by OPTCL.
- **ii. 6 nos.220 kV bays at PandiabilGIS:** Pandiabil (PG) substation has been commissioned in July'16. Downstream network needs to be expedited by OPTCL. Readiness of 220kV feeders by OPTCL for downstream power flow from Pandiabil (PG) S/S needs to be ensured.
- **iii. 4 nos. 220 kV bays at Keonjhar S/S:** Utilisation of total 4 nos. 220 kV line bays is pending due to unavailability of 220 kV lines of OPTCL. Program for readiness of linesfor utilisation of above bays to be confirmed by OPTCL.

#### WEST BENGAL

i. 02 nos. 220 kV line bays at Subhashgram (PG) S/S: Bays are ready and idle charged under ERSS-VIII due to non-readiness of 220kV D/C Subhashgram – Baruipur Tr. line and associated bays at Baruipur. Order recently placed by WBSETCL and expected completion by Dec'17. Program for readiness of lines for utilisation of above bays to be confirmed by WBSETCL.

Members may update.

#### **Deliberation in TCC meeting**

Members noted.

ITEM NO. D22: Commercial issues related to NHPC Stations

#### 1) Payment default by beneficiaries.

#### i) NBPDCL

An amount of Rs. 14.76 Cr. is outstanding for more than 60 days which includes surcharge of Rs. 0.24 Cr.

#### ii) SBPDCL

An amount of Rs.18.99 Cr. is outstanding for more than 60 days which includes surcharge of Rs. 0.28 Cr.

#### iii) WBSEDCL

Beneficiary has not paid surcharge of Rs.29.93 Cr. (TLDP-III – Rs. 28.79 Cr.& Teesta-V / Rangit- Rs.1.14 Cr.)

Matter was also discussed in 34<sup>th</sup> Commercial sub-Committee meeting of ERPC at Kolkata on 6<sup>th</sup> Feb'2017. NBPDCL, SBPDCL & WBSEDCL may be requested to release the outstanding dues as above at the earliest.

#### **Deliberation in TCC meeting**

NHPC revised the outstanding amount to 12 Cr on NBPDCL to which NBPDCL assured to make the payment within next 15 days.

NHPC revised the outstanding amount to 5 Cr on SBPDCL to which SBPDCL assured to make the payment within next 15 days.

WBSEDCL informed the tariff hike matter is in APTEL so requested to waive the outstanding amount for the time till the APTEL decision.

#### 2) Signing of reconciliation statement.

Reconciliation statement is pending for IIndquarter for the F.Y 2016-17 in r/o GRIDCO Matter was also discussed in 34<sup>th</sup> Commercial sub-Committee meeting of ERPC at Kolkata on 6<sup>th</sup> Feb'2017 and GRIDCO intimated that the reconciliation statement will be signed within a week time. Reconciliation statements for 3<sup>rd</sup> quarter of 2016-17 have also been sent to all the beneficiaries and same have not been signed by JBVNL, DVC, GRIDCO & Sikkim till date.

#### 3) Revalidation / Opening of LC of requisite value.

All the beneficiaries are intimated that the calculation sheet of LC for F.Y 2017-18 have been sent which is based upon 105% of average billing w.e.f Jan'2016 to Dec'2016. All the concerned beneficiaries are requested to enhance the existing LC or open the new LC of requisite value before31st March'2017 and same should be valid up to 31<sup>st</sup> March '2018. SBPDCL & NBPDCL have opened the L.C's for short value. They are requested to enhance their L.C's to requisite value immediately.

#### 4) Extension of PPA in r/o TLDP-III & IV Power Stations.

WBSEDCL at present has valid PPAs for TLDP-III & IV power stations for 05 years period only .WBSEDCL had already given consent to extend the PPA of TLDP-III & TLDP-IV power stations for 35 years from the date of COD. Formal signing / execution of PPAs of TLDP-III & TLDP-IV are still pending from WBSEDCL side for 35 years period from the date of COD.

Matter was also discussed in 34th Commercial sub-Committee meeting of ERPC at Kolkata on 6th Feb'2017.

WBSEDCL may be again requested to give consent for extension of PPA at the earliest. 100% power from both the projects has been allocated in favour of West Bengal.

#### **Deliberation in TCC meeting**

JBVNL, DVC and GRIDCO informed that signing of reconciliation is in progress and will be completed shortly.

SBPDCL informed that no revision of LC value is required as per their calculation. NHPC requested to share the calculation procedure with them.

WBSEDCL informed that they did not give any consent or commitment for PPA of 35 years. In their view the present price per unit energy is higher compare to the price at the time of their initial agreement. So extension of PPA at current scenario is not possible. However they agreed to find out a solution by discussion with NHPC.

WBSEDCL informed that this matter can be better discussed and solved bilaterally. NHPC agreed with WBSETCL.

#### 5) Signing of PPA in respect of Tawang H.E. Project, Stage-I & II.

Signing of Power Purchase Agreement is pending with GRIDCO, JUVNL & WBSEDCL. All the three beneficiaries areagain requested to sign the long pending Power purchase agreement at the earliest.

#### 6) Revision of REA in respect of SBPDCL and NBPDCL

SBPDCL & NBPDCL are verifying different energy amount w.r.t their REA statements.Matter was also discussed in 34<sup>th</sup> Commercial sub-Committee meeting of ERPC at Kolkata on 6<sup>th</sup>Feb'2017. As such, they are requested either to verify the same energy amount as per their REA or get revised REA's issued from ERPC. The discrepancies may give rise to disputes at a future date.

NHPC may update.

#### **Deliberation in TCC meeting**

WBSETCL informed that the matter is in progress.

Regarding revision of REA in respect of NBPDCL and SBPDCL, TCC requested them to solve it bilaterally.

Further TCC requested NHPC to try to solve these matter bilaterally as much as possible instead of taking it to TCC forum.

ITEM NO. D23:	Reconciliation of Deviation Accounts.
---------------	---------------------------------------

At the end of 3<sup>rd</sup> quarter of 2016-17, the reconciliation statement (Period: 01.10.16 to 31.12.16) has been issued by ERLDC on 04.01.17 and statements had been sent to the respective constituents and also uploaded the same at ERLDC website (<u>www.erldc.org</u>). The constituents were requested to verify /check the same & comments if any on the same were to be reported to ERLDC by 21.01.2017. The status of reconciliation is enclosed in **Annexure-C11.1**.

JUVNL, WBSETCL, SIKKIM, VEDANTA, APNRL, GATI, IBEUL & JLHEP (Dans Energy) have not signed reconciliation statement for any quarter of 2016-17.

Further BSPHCL, DVC & GMR have not signed reconciliation statement for 3<sup>rd</sup> Quarter of 2016-17.

In the CCM meeting held on 06.02.2017, ERLDC updated that BSPHCL & GMR have reconciled the statement for 3<sup>rd</sup> Quarter for 2016-17. WBSETCL & JUVNL informed that they would get the outstanding reconciliations completed within next week.

APNRL informed that they have sent reconciled statements for two quarters for 2016-17 through post. For 3<sup>rd</sup> quarter there is some discrepancy which would be intimated to ERLDC at the earliest.

ERLDC requested constituents to send scanned copies of reconciliation statement for early settlement.

#### **Deliberation in TCC meeting**

ERLDC informed that SIKKIM, VEDANTA, GATI, IBEUL & BRBCL have not signed the reconciliation statement.

OPTCL informed that they will take care of the Reconciliation of Deviation Accounts related to Vedanta.

Gati informed that they will do the reconciliation within a week.

\*\*\*\*\*\*



# MINUTES OF 35th TCC MEETING

**OF** 

# EASTERN REGIONAL POWER COMMITTEE

Date: 24th February, 2017

Venue: Ranchi

## Index

Item No	Title of Agenda	Page
Item No. A1	Confirmation of the minutes of 34 <sup>th</sup> TCC meeting	1
	Part B :: ITEMS FOR DISCUSSION	
Item No. B1	Status of DPR for PSDF funding in respect of Sikkim & JUSNL	1
Item No. B2	Revision of DPR for establishment of Reliable Communication (Bihar-Portion)	2
Item No. B3	FSTPS Islanding Scheme, NTPC	3
Item No. B4	Status of Bus Splitting schemes in Eastern Region	4
Item No. B5	Status of construction of 400 kV Sterlite-Jharsuguda D/C sections	5
Item No. B6	Status of construction of 400 kV Ind-Barath-Jharsuguda D/C line	6
Item No. B7	Status of construction of Chuzachen bay at Rangpo S/s.	7
Item No. B8	Status of construction of dedicated transmission lines of IPPs which are connected through interim arrangement	7
Item No. B9	Outstanding issues towards charging of 220kV Biharsharif-Tenughat line at 400 kV level	9
Item No. B10	High voltage problem in 400KV Meramundali Grid S/S	10
Item No. B11	Status of PLCC system installed in Eastern Region	12
Item No. B12	Redundancy of data at either of the control centres in case of failure of any one communication path/ICCP link/communication equipments	14
Item No. B13	Consideration of STU lines as Non-ISTS lines carrying ISTS power	17
Item No. B14	Opening of LC by ER constituents for Deviation Charges Payments	18
Item No. B15	Time correction of SEMs in Eastern Region	19
Item No. B16	High amount of Deviation Charges payable by BSPHCL on account of m/s. TALA HEP	20
Item No. B17	Proposal for stepwise completion of Rajarhat – Purnea 400 KV D/C lineunder ERSS-V Scheme	21
Item No. B18	Operationalization of LTA for BRBCL	23
Item No. B19	Nomination of the Bid Evaluation Committees (BECs) for the tranmission projects being implemented through TBCB	23
Item No. B20	Very high loading of 220kV Muzaffarpur(PG)-Kanti D/C line	24
Item No. B21	Augmentation of 400/220kV ICT capacity at Maithon, Patna, Sasaram, Biharshariff	25
Item No. B22	Commissioning of 125 MVAR bus reactor at Jamshedpur	25
Item No. B23	Priority-based commissioning of bus reactor for control of high voltage during lean periods	26
Item No. B24	Status of Transmission projects approved in various meetings	27
Item No. B25	Status of Spare Transformers & Reactors approved in various meetings	33

Item No. B26	Persistent over drawl by Jharkhand	34
Item No. B27	Commissioning of Tie bay and main bay of BUS-I of 400 kV Ranchi-New Ranch-I & II circuit at Ranchi Substation	35
Item No. B28	Issues related to associated / downstream systems Powergrid	36
Item No. B29	Commercial issues related to NHPC Stations	37
	Part C :: ITEMS FOR INFORMATION	
Item No. C1	Status of Projects approved/under consideration of PSDF appraisal committee	40
Item No. C2	Transfer capability declaration by the states of Eastern Region	41
Item No. C3	Anticipated network constraints in the forthcoming summer season, due to non-availability of 400kV Purnea-Biharshaiff D/C and 400kV Patna-Kishanganj D/C lines	42
Item No. C4	Reporting of Energy generated from renewable resources on daily basis	42
Item No. C5	Restricted Governor /Free Governor Mode Operation of generators in ER	43
Item No. C6	Updated status on SCADA telemetry	44
Item No. C7	Submission of detailed disturbance report for PCC Meeting	44
Item No. C8	Status of PCC recommendations	45
Item No. C9	Frequent uncoordinated tripping in 400kV Meramundali of OPTCL system	47
Item No. C10	Payment/Receipt Status from various pool accounts in ER	47
Item No. C11	Reconciliation of Commercial Accounts	48
Item No. C12	Detailed Procedure for Ancillary Services Operations w.e.f 21.11.16	50
Item No. C13	Payment of DSM charges by JUVNL to ER Pool due to incorrect meter reading for 132 KV Joda (Gridco) -Kendoposi (JSEB)	50
Item No. C14	Accounting for Re-import of Kurichhu Energy by Bhutan w.e.f Dec, 2014	51
Item No. C15	Meter readings related issues	52
Item No. C16	Implementation of Automatic Meter Reading in Eastern Region	53
Item No. C17	Incorrect Date Format of Meters at Angul PG and Kishanganj BSPTCL	54
Item No. C18	Location and meters with defective RS-485 port	54
Item No. C19	Procurement of new SEM's and DCD/Laptops	54
Item No. C20	Training for new Genus Make meter handling and software	55
Item No. C21	List of Assets commissioned by POWERGRID	55
Item No. C22	11KV Auxiliary power supply of 400KV Berhampore Powergrid Substation	55
Item No. C23	HIGHLIGHTS & GRID PERFORMANCE FOR THE PERIOD FROM OCT' 2016 TO DEC' 2016	56

#### EASTERN REGIONAL POWER COMMITTEE

#### MINUTES OF 35<sup>TH</sup> TCC MEETING

Date: 24<sup>th</sup> February, 2017 Venue: Ranchi

List of participants is at Annexure-II.

ITEM NO.A1: CONFIRMATION OF THE MINUTES OF 34<sup>TH</sup> TCC MEETING

The minutes of the 34<sup>th</sup> TCC meeting held on 18<sup>th</sup> November, 2016 at Kolkata were circulated vide letter no. ERPC/TCC & Committee/14/2016/1H3436\_H3505 dated 23<sup>rd</sup> December, 2016.

No comments have been received from constituent members on the minutes of the meeting.

Members may confirm the minutes of 34<sup>th</sup> TCC meeting.

#### **Deliberation in the TCC meeting**

*Members confirmed the minutes of 34<sup>th</sup> TCC meeting.* 

#### PART B: ITEMS FOR DISCUSSION

ITEM NO. B1: Status of DPR for PSDF funding in respect of Sikkim & JUSNL

In 33<sup>rd</sup>TCC, JUSNL and Sikkim informed that they need funds for upgradation of protection system. TCC, therefore advised JUSNL and Sikkim to prepare DPR within a month for up gradation of protection system and send to NLDC for PSDF funding with intimation to ERPC Secretariat.

In 34<sup>th</sup> TCC Sikkim informed that they will submit the DPR by January, 2016.

JUSNL informed that they are going to place the order to PRDC for preparation of DPR by the end of November, 2016 and they will submit the DPR to PSDF nodal agency by February, 2017.

Sikkim and JUSNL may update.

#### **Deliberation in TCC meeting**

Sikkim informed that they need some help from ERPC secretariat and assured that DPR will be submitted by 15<sup>th</sup> April 2017. Secretariat assured to extend their help.

JUSNL informed that M/s PRDC, consultant is preparing the DPR and they will submit the DPR to PSDF nodal agency by 15<sup>th</sup> April, 2017.

It was informed that CE, CEA will give a presentation on PSDF in tomorrow's ERPC meeting.

#### **CEA** may give a presentation on PSDF.

ITEM NO. B2:	Revision of DPR for establishment of Reliable Communication (Bihar-
TIENINO. DZ:	Portion)

In 34<sup>th</sup> TCC, it was informed that MoP agreed to fund 30% of the OPGW project through PSDF and rest 70% from states. Chairperson advised that TCC members may explore possibilities of enhancement of the PSDF portion on funding for OPGW project.

Powergrid updated that DPR for installation of OPGW for transmission lines of 132kV and above voltage level for both central and state sectors has been prepared for submission to the PSDF appraisal committee but now as per the decision of MoP the central sector is to be implemented by Powergrid on tariff based scheme and States sectors have to implement their portion on their own or may apply for PSDF funding on grant & investment ratio @30:70.

TCC advised all the States to place the DPR to PSDF appraisal committee for OPGW project with their proposed PSDF funding requirement.

BSPTCL vide letter dated 07.01.17 intimated that the that power sector in Bihar is growing many folds. Since the submission of transmission details and its connectivity diagram to PGCIL, many new transmission lines and sub-station has been commissioned and many of these elements are going to be commissioned shortly. Further, in view of achieving redundancy, some transmission lines have been taken into consideration for laying OPGW under ULDC revised scheme. This scheme is under implementation with PGCIL. So, the DPR need to be revised based on the update information of Sub-stations which is enclosed at **Annexure-B2**.

In Special PRM held on 14.02.2017, Powergrid informed that the State portion has to be implemented by the respective States. Powergrid will only implement for the Central Sector portion.

States may update respective status. TCC may guide.

#### **Deliberation in TCC meeting**

Chairman, TCC informed that states were not attending the higher level meetings being held at CEA and advised all the state representatives to attend.

He added that PSDF grant & investment ratio @30:70 was arrived based the marketing of the OPGW network by the states. However it is not possible for Eastern Region states.

He suggested that all the constituents should approach MoP, GoI for PSDF grant & investment ratio @90:10.

CE, NPC informed that such schemes will be considered for PSDF funding but for changeing the grant & investment ratio to 90:10 the approval needs to be taken from Ministry of power, GOI.

TCC decided that all the states should prepare DPR and send it to PSDF appraisal committee by 5<sup>th</sup> March, 2017 with a request to CE, NPC to take up the matter with ministry for considering the PSDF grant & investment ratio @90:10 for the projects of state sectors.

JUSNL informed that their DPR is ready and will be submitted by next week. Further, JUSNL pointed that the ownership of ties of JUSNL and BSPTCL lines was not yet decided and a procedure should be formulated for installation of OPGW in those lines.

TCC viewed that ownership issues are bilateral and these issues should be resolved by mutual interaction.

#### ERPC may note.

ITEM NO. B3:	FSTPS Islanding Scheme, NTPC
--------------	------------------------------

In 118th OCC, NTPC informed that their part is ready for implementation.

Powergrid informed that the battery charger has been delivered and expected to complete the work by March, 2016.

In 128<sup>th</sup> OCC meeting it was informed that progress of the islanding scheme is being monitored at Ministry level and ERPC Secretariat has already communicated the completion schedule as December, 2016.

OCC took serious note of extending the completion schedule of the islanding scheme in the last moment.

OCC felt that NTPC is not serious about implementation of the islanding scheme advised NTPC to submit their complete action plan to ERPC and ERLDC.

Subsequently NTPC submitted that

#### **OUOTE**

Regarding Farakka Islanding scheme, Cabling work has been done up to unit control room but final hooking with C&I system is pending. After evaluating every aspect, NTPC Farakka is of the view that the connection to C&I system is to be done during unit overhaul only so that proper checking of control system response can be done by simulation. Due to this, there has been a revision of the plan at our end. Our overhauling plan as of now, has been informed through our earlier mail yesterday. We shall hook units one by one during these overhauls.

UNQUOTE

OCC advised NTPC to explore final hooking up with C& I system at an opportune S/D time of the unit.

In 129<sup>th</sup> OCC, NTPC explained that after final hooking up with C&I of units they have to conduct dry simulation for checking the successful operation of the scheme which can only be carried out during overhauling.

Further, they informed that the maintenance programme of U#1 is scheduled from 10<sup>th</sup> March, 2017. So the hooking up with unit-I will be completed by March,2017 and the Islanding scheme will be operational. Unit#2 and Unit #3 will be hooked in April, 2017 and June/July, 2017 respectively during their overhauling.

OCC advised NTPC to strictly maintain the schedule so that the FSTPS islanding scheme can be put into service w.e.f. March, 2017.

In  $130^{th}$  OCC, NTPC assured to complete the islanding scheme with U#1 of FSTPS and they have requisitioned for shutdown of U#1 w.e.f.  $10^{th}$  March, 2017.

NTPC may update.

#### **Deliberation in TCC meeting**

NTPC confirmed that the final hooking of U#1 will be completed during overhauling S/D of U-1 in the month of March-April, 2017. They assured FSTPP islanding scheme with U#1 of FSTPS will be operational positively by April 2017 without further delay. On specific queries NTPC informed that except hooking up with units all their assigned works for implementing FSTPS islanding are satisfactorily completed.

#### ERPC may note.

ITEM NO. B4:	Status of Bus Splitting schemes in Eastern Region
--------------	---

#### A. Bus Splitting of Powergrid Sub-stations

As per decision of Standing Committee of ER CTU was entrusted to do Bus splitting at Maithon, Durgapur & Biharsariff S/Ss or ER. The latest status on the same are:

- 400 kV Maithon --- Completed
- 400 kV Durgapur--Completed
- 400 kV Biharshariff— In 129<sup>th</sup> OCC, Powergrid informed that bus splitting scheme will be completed by February, 2017.

In 130<sup>th</sup> OCC meeting, Powergrid informed that physical bus splitting at 400kV Biharshariff S/s has been completed. Protection part is yet to be completed.

Powergrid added that bus splitting at 400kV Biharshariff S/s will be commissioned by March 2017.

Powergrid may update.

#### **Deliberation in TCC meeting**

Powergrid informed that bus splitting at 400kV Biharshariff S/s will be commissioned by March 2017.

#### ERPC may note.

#### B. Bus Splitting of Kahalgaon STPS Stage I&II, NTPC

In 130<sup>th</sup> OCC, NTPC has given the present status as follows:

- ➤ 400/132kV Switchyard package bid opened on 14.03.16. Awarded on 04.05.2016.
- ➤ Site leveling Site leveling work has been completed.

Transformer package and Shunt reactor—have been awarded.

In 34th TCC, NTPC informed that the bus splitting will be completed by December, 2018.

NTPC may update.

#### **Deliberation in TCC meeting**

NTPC informed that the work is in progress as per the schedule and the bus splitting will be completed by December, 2018.

#### ERPC may note.

ITEM NO. B5:	Status of construction of 400 kV Sterlite-Jharsuguda D/C sections
--------------	---

Several deliberations were held in this forum on the issue of construction of 400 kV Sterlite – Jharsuguda D/C dedicated line of Vedanta Ltd (formerly known as Sesa Sterlite Ltd).

The 34<sup>th</sup> ERPC board, noted the progress made by Vedanta and advised Vedanta to expedite the work and complete the work by February, 2017 as decided by TCC. In this regard Vedanta was further advised to submit a fresh affidavit by 30.11.2016

Further, on appeal of Vedanta, ERPC reiterated that the physical completion of the project should be done by end February 2017. The pending statutory clearances may be obtained post completion of the physical activities and the status may be reviewed in next TCC meeting/March 2017.

Subsequently, Vedanta Ltd submitted a affidavit on 15<sup>th</sup> December, 2016 (Copy of the same is attachéd at **Annexure-B5**).

The latest status updated in 130<sup>th</sup> OCC is as given below:

Activities	Nos	Status as on 15-Nov-16 (as updated in 34 <sup>th</sup> TCC)	Status as on 17-Feb-17 (As updated in 130 <sup>th</sup> OCC)	Target completion as given in 34 <sup>th</sup> TCC Meeting	Remarks
Tower Foundation	64	60	62	30-Dec-16	
Tower Erection	64	42	55	10-Feb-17	
Stringing /OPGW Cabling & Testing	20.5 Km	One stretch completed	5.5 km completed	28-Feb-17	
Sub station Bay	2	Equipment Erection, Cable Trench, Earthing Completed	-	31-Dec-16	

Vedanta may update.

#### **Deliberation in TCC meeting**

*Vedanta updated the latest status as follows:* 

Activities	Nos	Status as on 15-Nov-16 (as updated in 34 <sup>th</sup> TCC)	Status as on 24-Feb-17 (As updated in 35 <sup>th</sup> TCC)	Remarks
Tower Foundation	64	60	64	Completed
Tower Erection	64	42	58	
Stringing /OPGW	20.5	One stretch	8 km completed	
Cabling & Testing	Km	completed	o kiii completeu	
Sub station Bay	2	Equipment Erection, Cable Trench, Earthing Completed	Bay construction completed	Will be completed by 2 <sup>nd</sup> March, 2017.

Vedanta informed that the construction work was delayed due to non-availability of shutdown of 11kV lines during Panchayat election.

Vedanta added that physical construction of the line will be completed by the end of March, 2017 and the line will be commissioned by end of April 2017 after getting the statutory clearances. Vedanta requested TCC to extend the dead line for removal of LILO up to April 2017.

CTU opined that in line with CERC order, they are ready to open the LILO as per the direction of TCC/ERPC.

Gridco, Odisha informed that they could not give the shutdown of 11kV feeders due to Panchayat elections and one month extension up to March 2017 may be granted to Vedanta for completion of line.

TCC opined that Vedanta is not serious about the construction of the line and still asking for 2 months extension. TCC viewed that the line can be commissioned by end of March 2017 if they could take up the activities related to statutory clearances simultaneously.

Accepting OPTCL request TCC decided to extend the dead line to 31.3.17 for commissioning of line including on-load charging of the same. Accordingly advised Vedanta to place item wise schedule for commissioning of line, in 35<sup>th</sup> ERPC meeting on 25.2.17.

Referred to ERPC for further guidance.

#### ERPC may decide.

ITEM NO. B6: Status of construction of 400 kV Ind-Barath-Jharsuguda D/C li	ne.
--	-----

CERC vide order dated 31.08.16 on petition No. 134/MP/2016 clarified the following:

#### **Ouote:**

Unquote

In 130<sup>th</sup> OCC meeting, IBEUL informed that construction of the line has been completed and ready for commission. The line will be commissioned by 28<sup>th</sup> February, 2017.

OCC advised IBUEL to communicate the status to ERPC and ERLDC after commissioning of line for commencement of commercial transaction.

IBEUL may update.

#### **Deliberation in TCC meeting**

It was informed that IBUEL vide mail has submitted the status of their dedicated line to ERPC and ERLDC on 23-02-2017. TCC advised ERPC secretariat to assess the position and do needful in line with CERC order, regulation and decisions taken in several meetings held on this issue.

#### ERPC may note.

ITEM NO. B7:	Status of construction of Chuzachen bay at Rangpo S/s.
--------------	--

Construction of bays at Rangpo S/s meant for evacuation of power from Chuzachen has been undertaken by Department of Power, Govt of Sikkim, under consultancy with Powergrid.

In 33<sup>rd</sup> ERPC, Sikkim placed the road map for construction of the bays as follows:

- Tender will be floated by July 2016
- Bid will be opened by August 2016
- Work will be awarded by September 2016
- Bay will be commissioned by December, 2017

In 34<sup>th</sup> TCC, Sikkim informed that they are going for retendering in November, 2016.

Sikkim assured that they will commission the bay within the target date i.e. December, 2017.

Sikkim may update. TCC may guide.

#### **Deliberation in TCC meeting**

Sikkim informed that retendering work is in progress.

Sikkim assured that they will commission the bay within the target date i.e. December, 2017.

#### ERPC may note.

I I H.VI NU J KX'	Status of construction of dedicated transmission lines of IPPs which
	are connected through interim arrangement

The progress of dedicated transmission lines of IPPs in Eastern Region, which were connected through interim arrangement, was reviewed in 34<sup>th</sup> ERPC meeting held on 19<sup>th</sup> November 2016. Dikchu HEP of Sneha Kinetic Power Projects Pvt. Ltd. is expected to be shortly commissioned on

interim arrangement. Therefore, it is proposed that status of dedicated transmission system of Dickhu HEP may also be monitored in ERPC forum. The status of the dedicated transmission lines as reported by IPPs in ER during the last ERPC meeting and Dikchu HEP is summarized below:

Generation Project in ER connected through temporary LILO arrangement					
Sl. No.	Generation Project	Installed Capacity (in MW)	Present Connectivity through LILO	Final Connectivity Arrangement (not commissioned)	Anticipated Completion Schedule
1	Vedanta (Sterlite Energy Ltd.)	4x600	LILO of one circuit of Rourkela - Raigarh 400kV D/c line (granted in Sept'09)	Sterlite - Jharsuguda 400kV 2xD/c	Feb'17
2	Ind Barath Energy (Utkal) Ltd.	2x350	LILO of one circuit of Jharsuguda - Raigarh 400kV D/c line (granted in Sept'09)	Ind Barath - Jharsuguda 400kV D/c	Completed but CEA clearance awaited
3	Gati Infrastructure Ltd. (Chuzachen)	2X49.5	LILO of Rangpo - Melli 132kV S/c line (granted in Nov'07)	Chuzachen - Rangpo 132kV D/c (with Zebra conductor)	Dec'17
4	Sneha Kinetic Power Projects Pvt. Ltd. (Dikchu)	2x48	(*) LILO of one circuit of Teesta-III – Rangpo 400kV D/c line (granted in Dec'14 by CERC)	Dikchu – Dikchu Pool 132kV D/c	(\$) To be informed by developer & Sikkim

<sup>(\*)</sup> Under Implementation. Interim granted vide CERC order in Petition no. 157/MP/2014 dated 03<sup>rd</sup> Dec 2014.

As per CERC order dated 28.09.2016 on Petition no. 30/MP/2014, "CTU shall take up all the existing cases of connectivity on interim LILO with the RPC of respective regions within a period of one month from the date of issue of this order for review and decision on disconnection of the interim arrangements through LILO. All such interim arrangements through LILO shall be disconnected within a period of three months of the issue of this order unless the RPC grants extension for continuation of LILO keeping in view of all relevant factors."

In view of the CERC order, further decision regarding the disconnection of the interim arrangements through LILO may be taken in the ERPC forum.

TCC may deliberate.

#### **Deliberation in TCC meeting**

CTU opined that in line with CERC order, they are ready to open the LILOs as per the TCC/ERPC direction.

#### ERPC may note.

<sup>( \$ )</sup> Dikchu Pool S/s is being implemented under Sikkim Comprehensive scheme of Govt. of Sikkim (being implemented by POWERGRID on consultancy). The expected commissioning schedule of Dikchu Pool and dedicated transmission line to be informed by Sikkim and SKPPPL, respectively.

ITEM NO. B9:	Outstanding issues towards charging of 220kV Biharsharif-Tenughat
	line at 400 kV level

Powergrid vide letter dated 18.01.2017 informed that the scope of POWERGRID for charging the 220kV Biharsharif-Tenughat line at 400 KV level is construction of (a) 01 no. bay and 0.8Km 400 KV transmission line for termination at Biharsarif S/s and (b) 5 nos. bays including Erection, Testing & Commissioning of OSM Equipments (i.e. 2 x 250 MVA ICTs, 50 MVAR L/R) at Tenughat end of TVNL. The detail scope of work with present status is enclosed at **Annexure-B9**.

In this regard, the following points are being put forward for consideration owing to which the balance work could not be completed till date:

#### A) Biharsharif S/s End (Deposit work of JUSNL):- Cost Plus Basis.

- a. The balance work at Biharsharif S/s end could not be completed due to irregular and delayed payment in past form JUSNL despite repeated reminders for deposit of fund by POWERGRID. Forcing agencies to demobilized frequently for want of fund. *Still payment of Rs. 48.5 Lakh is pending from JUSNL*.
- b. The said T/L is charged at 220 KV level and BSPTCL is currently drawing power from the said line directly. After charging of the said T/L on 400 KV level, BSPTCL will be deprived of power from Tenughat directly. *This issue has been strongly raised by BSPTCL in ERPC forum*.
- c. Work related to 400 KV bays at Biharsarif is nearing completion and line diversion work will be completed by April-2017.

#### B) Tenughat End (TVNL Consultancy project):- Cost Plus Basis.

- a. The balance work at Tenughat end could not be completed due to non-receipt of payment of Rs. 4.07 Crores approx from TVNL despite repeated reminders by POWERGRID. Part payment issues is not resolving.
- b. It is to inform that the agency (M/s Sterling Wilson) at Tenughat end has demobilized from site due to non-receipt of payment. The re-mobilization of agency for completion of balance work shall take approx. 01 month after receipt of pending fund from TVNL. Subsequent to mobilization of agency at site, approx. 03 months shall be required for completion of the balance work at Tenughat end. Other pending issues are enclosed in **Annexure-B9**.
- c. Completion target for above job (B) is by June-17.

34<sup>th</sup> ERPC advised JUSNL to settle the disputes in the bill and do the payment by end of November, 2016. JUSNL agreed.

In 34<sup>th</sup> TCC, Director (Projects), BSPTCL stated that the 4<sup>th</sup> ICT of 500 MVA at Biharshariff must be commissioned in close co-ordination with the up gradation of the subjected line.

Powergrid informed that this ICT may take at least two years as per the schedule.

ERPC requested Powergrid to explore the possibility of diversion of ICT from other projects/region. Director (O), Powergrid agreed to explore.

#### **Deliberation in TCC meeting**

#### A) Biharsharif S/s End (Deposit work of JUSNL):- Cost Plus Basis.

Powergrid informed that payment of Rs. 48.5 Lakh is still pending from JUSNL and they would complete the balance work at Biharsharif S/s end within 2 months from date of receipt of balance payment.

JUSNL has asked some clarifications on balanced payment.

TCC felt that the issue was pending from last two meetings and advised ERPC secretariat to convene a separate meeting at ERPC, Kolkata on 2<sup>nd</sup> March, 2017 at 12:00 hrs to resolve the issues.

TCC advised JUSNL and Powergrid to send their concerned officers at senior level for settlement of the problem.

#### B) Tenughat End (TVNL Consultancy project):- Cost Plus Basis.

TVNL informed that yesterday they have paid Rs 2 cr to Powergrid and they will pay the balance amount by March 2017.

Powergrid informed that they need 6 months from date of receipt to complete the work.

TVNL requested Powergrid to complete the work as per the given schedule by June 2017. Further, TVNL pointed that linking at Tenughat switchyard needs some deliberation.

TCC advised TVNL also to attend the special meeting scheduled on 2<sup>nd</sup> March 2017 with higher level participation and with all the details for effective discussion.

#### ERPC may note.

ITEM NO. B10:	High voltage problem in 400KV Meramundali Grid S/S
---------------	--

GRIDCO vide letter dated 07.01.17 intimated that presently Odisha is going through very high voltages at 400kV bus of Meramundali, Duburi and Mendhashal grid S/S. The situation is further worsened due to high reactive power flow from Meramundali to Angul pooling sub-station, from Duburi to Meramundali sub-station and from Kuchei to Duburi sub-station. It may be noted that, PGCIL has installed two nos. of 330 MVAr Bus reactors at Angul 765kV substation and two nos. of 125 MVAR Bus reactors at Ancul 400kV substation, thus resulting high reactive power flow from Meramundali to Angul & Duburi to Meramundali grid S/S. In view of the above OPTCL suggests the following as short term and long term measures to mitigate the high voltage issue as well as to improve the high reactive power flow situation.

#### **Short term measure**

- OPTCL will install 80 MVAr reactor at Meramundali 400kV S/S.
- The Angul-Meramundali Double circuit tie to be opened at both ends.

#### **Long term measure**

• The Meramundali-Angul Double circuit will be terminated at Meramundali (B). A letter regarding the above change has already been forwarded to CEA and will be placed in the next Standing Committee meeting of CEA. Meremundali(B) will be a new 400kV substation of OPTCL, approved by CEA and the work order to be issued shortly.

In view of the above and as the high voltage situation is menacing, it is requested to grant permission for the short term measures, mentioned above, to get relief from the high voltage issue and high reactive power flow. The system in the above condition will remain stable.

In 129<sup>th</sup> OCC, OPTCL informed that they are incurring substantial financial loss on account of reactive charges due to this overvoltage problem at 400 KV Meramundali substation and requested to explore the high voltage scenario by opening of 400 kV Angul-Meramundali D/C tie on trial basis.

ERLDC informed that the same may be granted as per real time grid conditions.

Further, OPTCL requested OCC to take up the issue of opening of LILOs of 400 kV Talcher-Meramundali & Bolangir –Meramundali lines at 765/400 kV Angul S/s which was already decided in 17<sup>th</sup> SCM meeting.

In 17<sup>th</sup> SCM it was pointed that the 400 kV LILO lines are feeding the load centres of Orissa at Meramundali and Mendasal. It is proposed that the above LILOs at Angul pooling station may not be disconnected. Instead, switching arrangements may be made at Angul substation such that above 400 kV LILOs may be operated either by-passing Angul substation or terminating at Angul substation as and when required, depending upon the power flow condition. Members agreed to the proposal as a part of Easter Region strengthening scheme-17 (ERSS-17)

The issue was also discussed in the special meeting on High voltage issues of ER, the minutes of the meeting is enclosed at **Annexure-B10**. In the meeting it was decided that OPTCL would ensure absorption of maximum possible reactive power (as per capability curve) by the units of JSPL, Vedanta and GMR(Odisha). Also, OPTCL should endeavor to restore the 50MVAR line reactor at Meramundali end of Vedanta-Meramundali-I at the earliest.

The issue was placed in 129<sup>th</sup> OCC and OCC viewed that as it is the matter related to Standing Committee of ER the same may be taken up with CEA/CTU.

Subsequently, MS took up the issue with CTU and it was agreed that ERLDC will carry out study for Reactive power flow in OPTCL system.

In 130<sup>th</sup> OCC, ERLDC has presented the study results and informed the following:

- The voltage at Meramundali is increasing during winter season due low demand at Meramundali, Dubri and Mendhasal and insufficient reactive power support.
- In the present scenario the 765/400 kV Angul S/s is acting like sink of Reactive power for OPTCL system in around 400kV Meramundali S/s.
- With opening 400kV Angul-Meramundali line the export of reactive power to the ISTS network is reduced drastically but the voltage at 400kV Meramundali S/s is increasing by 4 kV which may affect the sub-station equipment.
- Further due to outage of one ckt of 400 kV Meramundali- Mendhasal the voltage at Meramundali is on higher side. This line may be restored at the earliest.

OPTCL informed that 400 kV Meramundali- Mendhasal line will be restored within a week and 315 MVA, 400/220kV ICT will be restored by 15<sup>th</sup> March, 2017.

OCC advised OPTCL to plan for adequate reactive power compensation at 400kV Meramundali, New Dubri and Mendhasal S/s as a long term a measure.

ERLDC may elaborate. TCC may guide.

#### **Deliberation in TCC meeting**

ERLDC informed that VAR is being generated at OPTCL system and the 765/400 kV Angul S/s is acting like sink of Reactive power for OPTCL system in around 400kV Meramundali S/s. The opening of 400kV Angul-Meramundali line will not the solution. Further due to outage of one ckt of 400 kV Meramundali- Mendhasal the voltage at Meramundali is on higher side. This line may be restored at the earliest.

*OPTCL* informed that 400 kV Meramundali- Mendhasal line will be charged on tomorrow and 315 MVA, 400/220kV ICT will be restored by 15<sup>th</sup> March, 2017.

Powergrid informed that the flexible LILO scheme as approved in 18<sup>th</sup> SCM was approved in their Board and it is in final stage and the scheme will be implemented by 2018.

TCC opined that the high voltage issue should be reviewed after restoration of 400 kV Meramundali- Mendhasal line and commissioning of 315 MVA, 400/220kV ICT at Meramundali in OCC meeting.

TCC advised all generators in around 400kV Meramundali S/s to absorb VAR up to maximum extend as per the capability curve. TCC also advised OPTCL to plan for proper reactive power compensation at 400kV Meramundali, New Dubri and Mendhasal S/s.

CE, CEA opined that reactive power compensation is part of grid security and it is eligible for PSDF grant. OPTCL may apply for PSDF.

#### ERPC may note.

ITEM NO. B11:	Status of PLCC system installed in Eastern Region
---------------	---

#### 1) Restoration of PLCC system of important lines of JUSNL

I) 220 KV Chandil –Santaldih line

In 130th OCC meeting, JUSNL intimated that PLCC for 220 kV Chandil-Santaldih line has been tested and commissioned successfully on 25.01.17.

WBPDCL informed that the PLCC was activated but the auto-reclosure could not be put into service as the R-Ph pole of Circuit Breaker is not getting closed during auto-reclosure operation. The same is taken up with the OEM (i.e. ABB) and they will be rectifying the CB.

#### II) 220 KV Ramchandrapur-Joda line

In 130th OCC meeting, OPTCL informed that PLCC panels at 220kV Joda end will be commissioned within a week. JUSNL informed that the Ramchandrapur end is ready in all respect for implementation of PLCC.

JUSNL/WBPDCL/OPTCL may update.

#### **Deliberation in TCC meeting**

WBPDCL informed that overhauling of the R-ph pole of CB will be done by 15<sup>th</sup> March 2017. Subsequently, auto-reclosure feature will be enabled.

OPTCL informed that PLCC panels at 220kV Joda end will be commissioned by March 2017.

#### ERPC may note.

#### 2) Restoration of PLCC system of important lines of OPTCL and BSPTCL

In 34<sup>th</sup> TCC, OPTCL updated the latest status as follow:

- 1. Jeypore(PG)-Jayanagar (Commn. in OPGW exists): SDH tendering is in progress
- 2. Rourkela(PG)-Tarkera (Commn. in OPGW exists): SDH received commissioning by January, 2017
- 3. Rengali(PG)-Rengali S/Y (Proposal for Commn. in OPGW is pending): tendering is in progress
- 4. Indravati(PG)-Indravati(PH) (Proposal for Commn. in OPGW pending): tendering is in progress
- 5. Baripada(PG)-Baripada (Tendering in Progress for OPGW): Contract awarded
- 6. Baripada(PG)-Rairangpur (Tendering in Progress for OPGW): Contract awarded

#### BSPTCL informed the latest status as follows:

- 1. 220kV Patna-Fatua S/C line---Will commission the PLCC system by 31st December, 2016
- 2. 220kV Patna-Khagul S/C line---Will commission the PLCC system by 31st December, 2016
- 3. 220kV Gaya-Dehri D/C line--- The line is under breakdown. After coming of line in service, the work will be completed within another one month.
- 4. 220kV Gaya-Bodhgaya D/C line--- There is T-connection in line after removal of T connection PLCC will be installed.

Further, in PCC meetings the need of PLCC system was felt for the following lines of BSPTCL:

- 1. 220kV Purnea (PG)-Madhepura line
- 2. 220 kV Biharshariff- Begusarai line
- 3. 220 kV Biharshariff- Bodhgaya line

UNDER JURISDICTION OF BSPTCL

OPTCL and BSPTCL may update.

#### **Deliberation in TCC meeting**

OPTCL informed that PLCC system for Rourkela(PG)-Tarkera (Commn. in OPGW exists) line will be commissioned by March, 2017.

#### BSPTCL updated the following.

- 1. 220kV Patna-Fatua S/C line---*PLCC system has been installed and relays were reconfigured. PLCC system will be commissioned by March, 2017*
- 2. 220kV Patna-Khagul S/C line--- *PLCC system has been installed and relays were reconfigured. PLCC system will be commissioned after completion of re-conductoring work*
- 3. 220kV Gaya-Dehri D/C line--- *PLCC system has been installed and relays were reconfigured. PLCC system will be commissioned by March, 2017*
- 4. 220kV Gaya-Bodhgaya D/C line--- PLCC system has been installed and relays were reconfigured. PLCC system will be commissioned by March, 2017
- 5. 220kV Purnea (PG)-Madhepura line
- 6. 220 kV Biharshariff- Begusarai line
- 7. 220 kV Biharshariff- Bodhgaya line

Digital PLCC will be implemented.

#### ERPC may note.

There was a total failure of real time SCADA data to all control centres from 05:53 Hrs of 08-August-16. As an interim arrangement, real time SCADA data was restored on 10-August-16 at 03:19Hrs. The root cause was yet to be arrived and fixed.

In 126<sup>th</sup> OCC, it was raised that in case of failure of ICCP link/other communication equipment, the data availability needs to be assured at Back-up control centres.

OCC advised Powergrid to submit in 34<sup>th</sup> TCC their detail plan for data redundancy in case of failure of any one communication system at either of the control centres (Main & Back-up).

34<sup>th</sup> TCC felt that in case of failure of ICCP link/other communication equipment, the data availability needs to be assured at Main as well as Back-up control centres.

Powergrid informed that the alternate communication path was not available for SLDCs and ERLDC. Powergrid added that backup equipment is available and alternate communication path can be planned.

TCC advised to convene a special SCADA meeting to discuss the issue and report back.

In Special PRM meeting was held on 14.02.2017 to deliberate the issue. The minutes of the meeting is available at ERPC website (http://www.erpc.gov.in/event-calendar/). In the meeting the following two major issues emerged which need to be addressed:

# 1) Replacement of old RTU in Eastern Region for reporting of RTU / SAS to back-up control centres-

In the meeting, POWERGRID informed that independent reporting of RTU/SAS to backup ERLDC control center may consume lots of bandwidth and independent reporting will be easier through VLAN in 104 protocols but the old RTU in Central sector is not having 104 protocols provision. POWERGRID further informed that provision of dual reporting of RTUs / SAS would be possible in 104 protocols only after replacement of old RTUs.

ERLDC informed that new SCADA system is designed for dual reporting considering VLAN in 104 protocols and unless until, the dual data reporting of each RTUs / SAS would be configured in 104 protocols, complete control centre backup will not be achieved. So, it is quite necessary to replace the old RTUs / SAS at the earliest.

GM, ERLDC informed that process of replacement of similar old RTUs has taken up at Western Region also after getting proper approval at RPC level. GM, ERLDC suggested that a committee may be constituted to begin with to assess the requirement of the replacement of the old RTUs.

All members agreed and referred to TCC for further guidance.

TCC may guide.

#### **Deliberation in TCC meeting**

ERLDC informed that new SCADA system is designed for dual reporting. It is possible through LOOP PDH and SAS at main ERLDC control centre and extended directly to backup ERLDC control centre. But for Alcatel PDH it would not be possible. As these RTUs have already completed 15 years and need to be replaced by 2020, the replacement process may be initiated by the respective utilities.

Further ERLDC informed that as per the draft communication regulation the life of RTUs is fifteen years so the utilities should take care for their RTUs.


NTPC informed that the RTUs will be completing their life by 2020 and if any replacement is required before 2020 it may be considered after proper assessment.

After detailed discussion, TCC decided that a committee may be formed by ERLDC with Powergrid as nodal agency for assessment of old RTUs and further necessary action on replacement. Progress reports in this regard are to be placed before TCC on regular basis.

#### ERPC may guide.

#### 2) Redundancy of ICCP links between control centres:

ERLDC informed that ICCP links from ERLDC / backup ERLDC to all control centres should be available as mentioned in the diagram below:

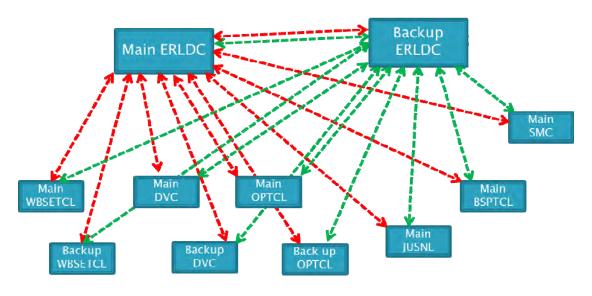

POWERGRID intimated that the ICCP connectivity of Backup ERLDC with all the control centers will be fully implemented after complete route redundancy of optical fiber. There are few paths (especially last mile) where there is no fiber redundancy. POWERGRID requested constituents to explore and implement the last mile redundant fiber connectivity. Such path having no redundancy has been identified for each sector and redundant route is shown in ICCP flow diagram in **Annexure** – **B12.2**. Following are the sections where fiber laying is to be done/under implementation:

#### **Central Sector:**

<u>ERLDC</u> to Kasba-POWERGRID informed that one UGFO link between ERLDC to Kasba is under implementation by them. POWERGRID further informed that alternate FO link connectivity may be implemented after getting the fiber connectivity from CESC (Kasba S/S – Jadavpur S/S – ERLDC) for route diversity for redundancy. POWERGRID requested ERLDC to take up the matter with CESC so that the same fiber can be used between ERLDC to Kasba for route diversity for redundancy.

<u>Farakka to Jeerat</u> – POWERGRID informed that presently, FO link connectivity is available between Farakka to Jeerat through Behrampur which doesn't have route diversity. POWERGRID further informed that route diversity for redundancy would be available after commissioning of OPGW link from Farakka to Jeerat through Gokarna, Rajarhat & Subhashgram.

#### WBSETCL Sector:

<u>Kasba</u> to Arambag – POWERGRID informed that presently, FO link connectivity is available between Kasba to Arambag through Jeerat, Behrampur, Farakka & Durgapur which doesn't have route diversity. POWERGRID further informed that route diversity for redundancy would be available after commissioning of OPGW link from Kasba to Arambag through Jeerat &Krishnanagar as mentioned in the ICCP flow diagram of WBSETCL. POWERGRID further informed that the same would be implemented by December 2017.

#### **DVC Sector:**

Howrah SLDC to ERLDC– POWERGRID informed that presently, FO link connectivity between Howrah SLDC to ERLDC is available through leased line. POWERGRID further informed that route diversity for redundancy would be available after commissioning of OPGW link from Howrah SLDC to Maithon SLDC & Howrah SLDC to Waria as mentioned in the ICCP flow diagram of DVC. POWERGRID further informed that the same would be implemented by June 2017.

<u>Kalyaneshwari to Mathon SLDC</u> – POWERGRID informed that presently, FO link connectivity is available between Kalyaneshwari to Maithon SLDC through Maithon HPS which doesn't have route diversity. POWERGRID further informed that route diversity for redundancy would be available after commissioning of OPGW link from Maithon SLDC to Howrah SLDC as mentioned in the ICCP flow diagram of DVC. POWERGRID further informed that the same would be implemented by June 2017.

#### **OPTCL Sector:**

<u>Rourkela to Bhubaneswar SLDC</u> – POWERGRID informed that presently, FO link connectivity between Rourkela to Bhubaneswar SLDCis available through TSTPS, Meeramundali& Mendhasal which doesn't have route diversity.

OPTCL informed that route diversity for redundancy would be available after commissioning of repeater station at Bhabanipatna between Jeypore – Bolangir line and FO link connectivity from Meeramundali to Bhubaneswar SLDC through Duburi New, Jagatsingpur & Cuttack as mentioned

in the ICCP flow diagram of OPTCL. OPTCL further informed that the same would be implemented by March 2018.

#### **BSPTCL Sector:**

<u>Biharsharif 400 kV (PG) to Patna SLDC</u> –POWERGRID informed that presently, FO link connectivity between Biharsharif 400 kV (PG) to Patna SLDC is available through Biharsharif 220,Fatwa &Jakkanpur which doesn't have route diversity.

BSPTCL informed that FO link connectivity between Biharsharif 220to Jakkanpur would be available through Bodhgaya, Chandwa, Jahanabad& Sipara. The same would be implemented by July 2017.

POWERGRID informed that route diversity for redundancy between Biharshariff 400 (PG) to Jakkanpur could not be achieved until unless FO connectivity from Patna to Sipara or/and Biharshariff 400 (PG) to Biharshariff 220 would be implemented. POWERGRID requested BSPTCL to get this FO link implemented. BSPTCL requested POWERGRID to include the same in the existing FO link implementation contract.

POWERGRID requested BSPTCL to explore the possibility of FO connectivity from Jakkanpur to Patna SLDC from their DISCOM for route diversity and redundancy between Jakkanpur to Patna SLDC. BSPTCL agreed for the same.

#### JUSNL Sector:

Ranchi 400 kV (PG) to JUSNL SLDC (Kushai Colony) –POWERGRID informed that presently, FO link connectivity between Ranchi 400 kV (PG) to JUSNL SLDC is available through Hatia 220 kV which doesn't have route diversity.

POWERGRID further informed that route diversity for redundancy between Ranchi 400 kV (PG) to JUSNL SLDC (Kushai Colony) could not be achieved until unless OPGW connectivity from Chandil to JUSNL SLDC through Namkum (132 kV) i.e. 95 Km could be completed. POWERGRID further informed redundant fiber route is to be explored and implemented by JUSNL.

#### Sikkim:

<u>Gangtok to Sikkim SLDC</u> –POWERGRID informed that presently, FO link connectivity between Gangtok to Sikkim SLDC is available which doesn't have route diversity.

POWERGRID further informed redundant fiber route is to be explored and implemented by Sikkim.

TCC may deliberate.

#### **Deliberation in TCC meeting**

TCC advised all the respective constituents to explore for the last mile connectivity of fibre.

#### ERPC may guide.

ITEM NO. B13:	Consideration of STU lines as Non-ISTS lines carrying ISTS power
---------------	--

Subsequently, in line with 34<sup>th</sup> TCC decision, ERPC and ERLDC conducted the load flow study using WebNet software for first three quarters of validated data. Summary of the results for percentage utilization of the transmission line by STU to meet the own demand is given at **Annexure-B13.** 

Balance (100 - utilization of the transmission line by the STU) is the ISTS power flowing through the line.

128<sup>th</sup> OCC decided that ISTS power flowing through STU lines greater than 50% of the total power as per the WebNet software of the validated data for each quarter will be considered as ISTS line.

In 129<sup>th</sup> OCC, OPTCL pointed that the PoC charges for STU lines should be calculated based on the actual ISTS power flow through STU lines as per the WebNet software of the validated data for each quarter.

However, after detailed deliberation all the STUs including OPTCL agreed that STU lines carrying ISTS power greater than 50% of the total power as per the WebNet software of the validated data for each quarter will be considered as non-ISTS line carrying ISTS power.

Further, GM-ERLDC informed that in Western Region the same principle is being followed for STU lines.

OCC requested concerned utilities to file petition before CERC in this regard with this recommendation.

TCC may guide.

#### **Deliberation in TCC meeting**

TCC advised all the respective states to file petition before CERC for consideration of non-ISTS lines under respective control areas as ISTS lines with OCC recommendation.

TCC also advised ERPC/ERLDC to continue study in this regard on each quarter.

# ERPC may guide.

ITEM NO. B14:	Opening of LC by ER constituents for Deviation Charges Payments
---------------	---

Clause 10 (4) of CERC Deviation Settlement Mechanism and related matters Regulations, 2014 vide notification No. L-1/132/2013/CERC dated 6<sup>th</sup> January, 2014 to be implemented from 17.02.2014 is reproduced below:

#### Ouote

......Provided further that LC amount shall be increased to 110% of the payable weekly liability in any week during the year, if it exceeds the previous LC amount by more than 50%.

Unquote

As intimated by ERLDC, the details of LC amount required to be opened in 2016-17 by ER constituents is given in **Annexure – B14.** Letters to this effect has already been issued by ERLDC to the defaulting entities viz, BSPHCL, JUVNL, GATI, SIKKIM and Ind Barath. Rest of the constituents which were required to open/recoup the LC, they have opened/recoup the LC.

In the last CCM on 06.02.2017, BSHPCL informed that they would get the LC opened by the end of February, 2017. JUVNL informed that the matter had been taken with their bank and LC would be opened shortly. Sikkim representative was not present.

ERLDC may update.

#### **Deliberation in TCC meeting**

BSPHCL informed that they have renewed their LC. GATI informed that LC will be opened shortly. Sikkim informed that LC will be opened by March, 2017.

# ERPC may note.

ITEM NO. B15:	Time correction of SEMs in Eastern Region
---------------	---

The drifting of meter time was important in commercial terms since the reading for a block for a time drifted meter might not be true and lead to erroneous calculation of Deviation Charge for that constituent. Further, it was decided to keep this as a standing agenda in Commercial Sub Committee meetings for monitoring. List of Time drifted (more than 5-6 min) meters in ER as on 30.01.17 is enclosed in **Annexure-B15.** 

It has been seen that constituents are not making any time correction in SEM. Further after AMR implementation due to non-use of the DCDs, many DCDs are not working in many places. Time correction from laptops is not possible. In Last CCM, It was decided that all the constituents would give a list of DCD with them and their status. Powergrid is requested to keep some spare DCD for the purpose of time correction of meters.

In the last CCM held on 06.02.2017, POWERGRID proposed purchase of about 10 to 15% new L & T meters and some DCDs so that time correction could be taken up urgently by replacing the time drifted meters from highest drift first. Then the drifted meters could be sent to the works of M/s L&T for bulk time correction. It was further informed that the new Genus make meters are yet to be interfaced with AMR system so procurement of new L&T meters could help relieve the drift issue.

ERLDC observed that the integration of Genus meters with AMR system are already ongoing by TCS and may be successful in a few days. Therefore, it may be prudent to replace the L & T meters with Genus meters, which have bulk time correction facility on site. The replaced L & T meters may be sent to factory for bulk time correction.

Powergrid was requested to prepare a list of L& T meters which were faulty or have exhausted their specification so that the same may be taken up for replacement immediately by Genus meters (as and when interface with AMR was complete)

GRIDCO representative informed that smart meters may be considered in future so that online time simultaneous time correction could be incorporated. ERLDC informed that the revision of metering regulations was under process in CEA and smart features may be incorporated.

Powergrid may update regarding integration of new Genus make meter in ER AMR.

# **Deliberation in TCC meeting**

Constituents felt that the performance of the new Genus make meter should be confirmed before replacing all the SEMs.

Powergrid informed that new Genus meters were procured after conforming the specifications as per the CEA meter regulations and the bulk time drift in these meters can be corrected in one attempt through Laptop. The interfacing issues of Genus meters with AMR will be resolved by April 2017.

It was felt that the meters with severe drift greater than 10 min need to be replaced first and if replacement is done with Genus then readings are to be collected manually using Laptop till interfacing with AMR is completed.

TCC advised Powergrid to replace the 10% of the heavily drifted SEMs and monitor the performance of the new meters. Powergrid should present this performance before constituents and subsequently the decision on replacement of the other time drifted meters will be taken up.

# ERPC may advise.

ITEM NO. B16:	HIGH AMOUNT OF DEVIATION CHARGES PAYABLE BY BSEB
	ON ACCOUNT OF M/s. TALA HEP

SBPDCL vide letter dated 07.01.17 informed that the deviation charges incurred by M/s TALA HEP are to be borne by its beneficiaries, and BSEB being a major beneficiary, having a share of 25.5% has to bear a major portion of these deviation charges.

For the last 8 weeks, it has been observed, to their great concern that the deviation charges incurred by M/s TALA HEP have been continually high, amounting to as high as few crores per week. A summary report of the amount incurred by M/s TALA HEP as deviation charges, and consequently the amount to be borne by BSP(H)CL erstwhile BSEB was also submitted.

From the statistics in this table; & discussion with ERLDC, it was concluded that a major percentage of bill for UI & Deviation payable by BSP(H)CL erstwhile BSEB, is on account of huge deviation charges incurred by M/s TALA HEP.

As such, ERLDC should keep scheduled generation near to actual generation or devise a mechanism to make deviation zero or minimum. Beneficiaries should not be charged for the high declared capacity (DC) given by TALA or CHUKHA HEP, as they are not responsible for the high mismatch between scheduled generation and actual generation of Bhutan generating station.

So, it was requested that the future scheduling for power purchase on behalf of M/s TALA HEP and M/s CHUKHA HEP should be done keeping in mind the concerns of its beneficiaries.

In 129<sup>th</sup> OCC, MS- ERPC assured that the matter is under consideration and will be resolved at the earliest.

In 130<sup>th</sup> OCC, ERPC/ERLDC explained the adjustment of Tala, and Chukha power in DSM and Regional Energy Accounting of ERPC. It was informed that the there is no applicability of DSM for Tala/Chukha power. However, in DSM Account the deviation of Tala/Chukha is being adjusted at their respective rates not at frequency variable DSM rate.

BSPTCL may note.

# **Deliberation in TCC meeting**

SBPDCL pointed that they need some more clarification on the issue.

TCC advised SBPDCL to interact with ERPC Secretariat and resolve the issue.

# ERPC may note.

THE RIVE NUMBER 15	Proposal for stepwise completion of Rajarhat – Purnea 400 KV D/C lineunder ERSS-V Scheme
--------------------	--

Investment approval for the following transmission project associated with Eastern Region Strengthening Scheme-V (ERSS-V) was accorded by the competent authority in 292<sup>nd</sup> Board meeting on 23<sup>rd</sup> Oct'2013.

- 1. Rajarhat Purna 400 KV D/C line (with triple snow bird conductor) with LILO of one circuit at Gokarna(WBSETCL) and other circuit at Farakka(NTPC).
- 2. LILO of Subhasgram Jeerat 400 KV S/C line at Rajarhat.
- 3. Establishment of 400/220 KV, 2X500 MVA Gas Insulated Sub-station at Rajarhat in west Bengal.

Keeping in view of the facts and priorities, the project element "Rajarhat – Purnea 400 KV D/C line (with triple snow bird conductor) with LILO of one circuit at Gokarna (WBSETCL) and other circuit at Farakka (NTPC)" associated with ERSS-V was proposed to be rearranged and commissioned stepwise as detailed below:


Sl. No.	Description of rearranged Element
1	Rajarhat - Farakka portion of Rajarhat - Purnea 400 KV D/C transmission line including LILO of one ckt. of Rajarhat - Purnea Line at Farakka
2	LILO of one Circuit of 400 KV D/c Rajarhat- Purnea Line at Gokarna Substation
3	Farakka – Purnea portion of Rajarhat - Purnea 400 KV D/C transmission line

34<sup>th</sup> TCC agreed for the above rearrangement.

In 129<sup>th</sup> OCC, Powergrid informed that the construction work of 400 KV GIS Sub-station and tower package of 400 KV D/C Rajarhat –Purnea Transmission line at Rajarhat end has completely brought to a standstill condition since last one month due to agitation of local villagers.

However, Farakka-Gokarna portion of the said line along with associated bays at Farakka may be completed within the FY 2016-17. Further, Sub-station work including ICT at Gokarna (under jurisdiction of WBSETCL) is ready for charging and 400 KV line bays including 80 MVAR B/R

(under scope of POWERGRID) is also ready for commissioning. Accordingly, 400 KV D/C Farakka-Gokarna portion of Rajarhat-Purnea 400 KV D/C transmission line including LILO of one circuit at Farakka and other circuit at Gokarna can be commissioned within March, 2017. This is also to be noted that commissioning of Farakka-Gokarna portion of the Rajahat-Purnea transmission line can connect Gokarna S/s at 400 KV level which will improve the power situation in and around Berhampur area.

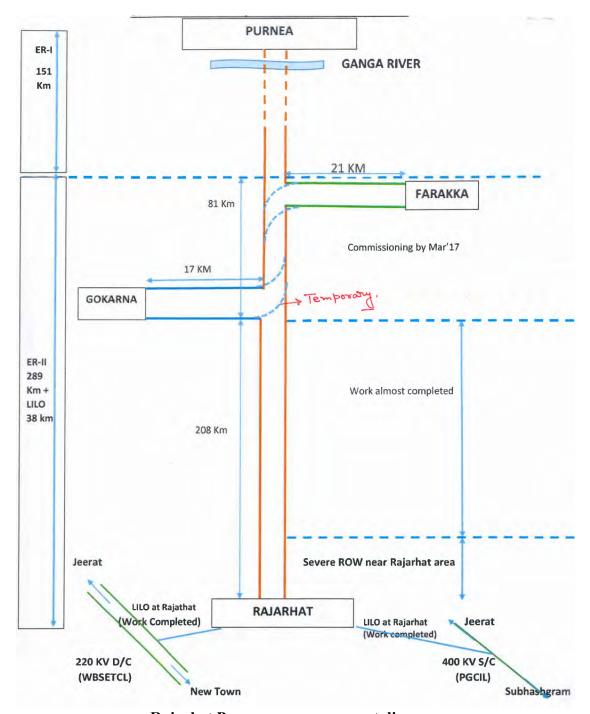

Rajarhat Purnea re-arrangement diagram

Keeping in view of the above facts and priorities the project element "Rajarhat-Purnea 400 KV D/C transmission line (with triple snow bird conductor) with LILO of one circuit at Gokarna (WBSETCL) and other circuit at Farakka (NTPC)" associated with ERSS-V is proposed to be rearranged and commissioned stepwise as detailed below:

SL	DESCRIPTION OF REARRANGED ELEMENT
NO	
1.	400 KV Farakka-Gokarna portion of Rajarhat-Purnea 400 KV D/C Transmission
	line including LILO of one circuit at Farakka & other circuit at Gokarna.
2.	Rajarhat-Gokarna portion of the 400 KV D/C Rajarhat-Purnea Line.
3.	Farakka – Purnea portion of Rajarhat - Purnea 400 KV D/C transmission line.

After commissioning of element at Sl. No. 1 the effective transmission line shall be 400 KV D/C Gokarna-Farakka TL with 1 No. 80 MVAR B/R at Gokarna end and 1 No. 80 MVAR line reactor at Farakka end.

OCC agreed and recommended for TCC approval.

TCC may deliberate.

# **Deliberation in TCC meeting**

TCC approved the changes and referred to ERPC for further concurrence.

TCC decided that the scheme will be referred to Standing Committee after approval of ERPC.

# ERPC may approve.

ITEM NO. B18:	Operationalization of LTA for BRBCL
---------------	-------------------------------------

In the special meeting on the issue of Scheduling of BRBCL station which was held on 25<sup>th</sup> January, 2017 at Kolkata, it was decided that CTU will notify Operationalization of LTA after detailed studies before ensuing 35<sup>th</sup> TCC/ ERPC meetings. LTA will be operationalized upto the state periphery with total available transfer capability from the station.

CTU may update.

# **Deliberation in TCC meeting**

It was informed that BRBCL has filed a petition before CERC and the issue is pending with CERC. Therefore the agenda was dropped and no discussions were held.

# ERPC may note.

ITEM NO. B19:	Nomination	of th	e Bid	Evaluation	Committees	(BECs)	for	the
	tranmission projects being implemented through TBCB							

CEA vide letter dated 30.11.16 & 16.02.17 informed that Ministry of Power had notified the below scheme vide Gazette Notification dated 31.10.2016.

As per the Tariff based Competitive Bidding Guidelines for Transmission Service notified by Govt. of India nomination of officers at Director level are sought for constituting the scheme specific Bid Evaluation Committee (BEC) which is as follows:

Sl.	Name of Transmission Scheme	Bid Process	Nomination of
No.		Coordinator	officers (in no.)
1.	Eastern Region Strengthening-XXI(ERSS-XXI)		
	(i) Establishment of 400/220/132 kV, 2x500		
	MVA+2x200 MVA S/s at Sitamarhi(New)		
	(ii) Establishment of 400/220/132 kV, 3x500	DEC Toursies	
	MVA+3x200 MVA S/s at Chandauti(New)	REC Transmission	2
	iii) Establishment of 400/220/132 kV, 2x500	Projects Co. Ltd.	
	MVA+2x200 MVA S/s at Saharsa(New)		
	iv) Substation extension at Darbhanga S/s		
	v) Substation extension at Motihari S/s		

It is requested that two no. of officers at Director level may be nominated for BEC for above ERSS-XXI projects.

TCC may nominate.

# **Deliberation in TCC meeting**

TCC advised Bihar and Jharkhand to nominate for BEC at the earliest.

# ERPC may nominate.

ITEM NO. B20:	Very high loading of 220kV Muzaffarpur(PG)-Kanti D/C line
---------------	---

Due to heavy import by BSPHCL at Muzaffarpur, power flow through the said line generally remains above 150MW/ckt and even crosses 195 MW/ckt in the peak. Though the situation is likely to ease after commencement of generation at KBUNL Stg-2, for facilitating planned shutdown of the line, it is desirable to have additional 220kV circuits in parallel to the existing line. In the 34<sup>th</sup> TCC meeting it was informed that circuits 3 and 4 between Muzaffarpur(PG) and and Kanti (Extn) would be completed by November, 2016.

BSPTCL / PGCIL may kindly expedite commissioning of 220kV circuits 3 and 4 between Muzaffarpur(PG) and Kanti (Extn).

BSPTCL/Powergrid may update.

# **Deliberation in TCC meeting**

Powergrid informed that 2 nos line bays will be commissioned at Muzaffarpur by March 2017 but the line construction is not in the scope of Powergrid.

BSPTCL informed that there is uncertainty in commissioning of line. However, BSPTCL is taking measures to relive the overloading of 220 kV Muzaffarpur-Kanti.

# ERPC may note.

ITEM NO. B21:	Augmentation	of	400/220kV	ICT	capacity	at	Maithon,	Patna,
	Sasaram, Biharshariff							

ICTs of (1X315+1X500) MVA capacity exists at Maithon, Patna and Sasaram. In the peak period, the total power catered by each of the sub-stations is high enough to cause tripping of the parallel 315MVA ICT, if the 500MVA ICT trips. Similarly, if one out of the 3X315 MVA ICTs at Biharshariff trips, the other two ICTs are also likely to trip on overload.

The 315 MVA ICTs at Patna and Sasaram are already planned to be replaced by 500MVA ICTs while a 500MVA ICT is scheduled to be added each at Maithon and at Biharshariff.

As the peak demands of Bihar and DVC systems are likely to rise sharply in the coming summer season, PGCIL may kindly expedite augmentation of 400/220kV ICT capacities at the above mentioned sub-stations

Powergrid may update.

# **Deliberation in TCC meeting**

Powergrid informed that the augmentation 400/220kV ICTs at Maithon S/s will be completed by July, 2017.

Powergrid added that type test of 400/220kV ICT of Sasaram and Patna S/s has been failed and the design of the ICT is being reviewed by OEM. The augmentation of 400/220kV ICTs at Sasaram and Patna will take time.

Powergrid also informed that augmentation of 400/220kV ICTs at Biharshariff will take one and half year.

Bihar requested Powergrid to divert ICTs from any other sub-stations for early argumentation at Biharsariff, Sasaram and Patna S/s. Bihar added that immediate argumentation of ICTs at Biharsariff S/s is essential to meet increasing demand in Bihar.

Powergrid informed that diversion of ICT to Biharshariff S/s is not possible at this juncture. However Powergrid assured to explore further possibilities to expedite.

## ERPC may note.

ITEM NO. B22:	Commissioning of 125 MVAR bus reactor at Jamshedpur
---------------	---

Voltage of 400kV Jamshedpur remains above 420kV (IEGC upper limit) for nearly 100% of the time.

In the Standing Committee Meeting of ER held on 05-01-2013, it was inter-alia agreed to install 2X125 MVAR bus reactors in parallel with the existing 2X50 MVAR reactors at Jamshedpur. The same decision was reiterated in the next Standing Committee Meeting of ER held on 02-05-2014. While 125 MVAR reactors for voltage control have been installed by PGCIL at Rourkella, Patna, Sasaram, Maithon, Durgapur etc. the reactors at Jamshedpur are yet to be commissioned. PGCIL

may be requested to kindly accord topmost priority in mitigating high voltage at Jamshedpur and expedite installation of the 125 MVAR reactors there.

In 130<sup>th</sup> OCC, ERLDC informed that severe high voltage is being observed at 400kV Jamshedpur S/s on continuous basis and advised Powergrid to commission 2X125 MVAR bus reactors at the earliest.

Powergrid informed that the reactor will be commissioned by April, 2017.

Powergrid may update.

# **Deliberation in TCC meeting**

Powergrid informed that the reactor will be commissioned by May, 2017.

# ERPC may note.

I I I H VI NI I B / 3.	Priority-based voltage during	commissioning lean periods	of	bus	reactor	for	control	of	high	
------------------------	-------------------------------	-------------------------------	----	-----	---------	-----	---------	----	------	--

In 34<sup>th</sup> TCC, Powergrid updated the latest status as follows:

S.N.	Reactor	Status
1	125 MVAR reactor of Jeypore	Commissioned
2	125 MVAR Bus reactor of	
	Jamshedpur	Expected commissioning by Feb'17
3	125 MVAR Bus reactor of	(Jamshedpur) and Jan'17 (Biharshariff)
	Biharshariff	
4	Additional bus-reactor of 125	Will be made available for commissioning
	MVAR capacity at Beharampur	by Oct, 2017.
	on urgent basis.	
5	50 MVAR at Behrampur on	Reactor has reached Behrampur.
	urgent basis by diverting from	Commissioning by Nov'16 end.
	Rourkela which is kept as a spare	

Powergrid may update the latest status.

# **Deliberation in the meeting**

Powergrid updated the latest status as follows:

S.N.	Reactor	Status
1	125 MVAR reactor of Jeypore	Commissioned
2	125 MVAR Bus reactor of Jamshedpur	Expected commissioning at Jamshedpur
3	125 MVAR Bus reactor of Biharshariff	and Biharshariff by April'17
4	Additional bus-reactor of 125 MVAR	Commissioning expected by April'18.
	capacity at Beharampur on urgent basis.	
5	50 MVAR at Behrampur on urgent	Commissioned in Dec'16.
	basis by diverting from Rourkela which	
	is kept as a spare	

OPTCL informed that the high voltage problem persists even after the commissioning of 125MVAR reactor at Jeypore.

TCC referred the issue to OCC for further deliberation.

# ERPC may note.

ITEM NO. B24:
---------------

The status as updated in 34<sup>th</sup> TCC/ERPC meeting on transmission projects approved to various meetings is given below:

Sl No.	Scheme	ERPC/SCM Meeting	Latest status
1	Modification of 132 kV Bus arrangement at 220/132 kV Birpara S/s of Powergrid from existing single main & transfer bus scheme to double mainscheme.	28 <sup>th</sup> ERPC Meeting	Powergrid informed that the work undr progress and expected commissioning by Aug'17.
2	Change in proposed the Associated 765 kV System Strengthening Scheme in ER	28 <sup>th</sup> ERPC Meeting	Under TBCB
3	Retrofitting of pilot wire protection of 132 kV Purnea (PG) – Purnea (BSPHCL) feeders	26 <sup>th</sup> ERPC Meeting	Powergrid informed that the scheme was covered in the scheme of modification of 132 kV Bus arrangement at 220/132 kV Purnea S/S of Powergrid under GIS package. The work has been awarded and expected to be completed by Jan'17.
4	Transmission System for immediate evacuation of power from North Karanpura STPP (3x660 MW) to Chandwa and Gaya Pooling stations of Powergrid	25 <sup>th</sup> ERPC Meeting	T/L is under TBCB, POWERGRID informed that Chandwa bay awarded and for Gaya tendering activity under progress.
5	Procurement of two single phase spare ICT units (2x500 MW), 765/400 kV for Eastern Region - to be stationed at Angul&JharsugudaS/S).	25 <sup>th</sup> ERPC Meeting	Powergrid informed that work has been awarded on March, 2015 and expected to be completed by Mar'17.
6	Augmentation of transformation capacity at the existing 400/220 kV Jamshedpur (PG) &Sasaram (PG)S/S	25 <sup>th</sup> ERPC Meeting	Powergrid informed that for Sasaram-  1 <sup>st</sup> ICT commissioned, 2 <sup>nd</sup> ICT in supply, expected commissioning by Mar'17. For Jamshedpur, commissioning expected to be completed by November,2016
7	Establishment of 220 kV MTPS (Extn.) – Muzaffarpur (PG) D/C line (3 <sup>rd</sup> & 4 <sup>th</sup> Circuits)	25 <sup>th</sup> ERPC Meeting	Bay construction at Muzaffarpurto be done by Powergrid under consultancy projected. Expected to be completed by Dec,2016.
8	Modification of 132 kV Bus arrangementat 220/132 kV Siliguri S/S(PG)	25 <sup>th</sup> ERPC Meeting	Powergrid informed that the work has been awarded and expected to be complete by November,2016.
9	Procurement of 110 MVAR, 765 kV Single Phase spare Reactor unit at Sasaram	25 <sup>th</sup> ERPC Meeting	Powergrid informed that the work has been awarded on March, 2015 and expected to be delivered by Mar' 2017.

10	Establishment of Gazol 220/132 kV S/S in Malda by LILO of Malda-Dalkhola 220 kV D/C line of Powergrid	25 <sup>th</sup> ERPC Meeting	Not pertaining to POWERGRID
11	Construction of down linking transmission network for drawal of power from Kishanganj 400/220 kV S/S ofPowergrid	25 <sup>th</sup> ERPC Meeting	Powergrid informed that four numbersof 220 kV bays at 440 kV Kishanganj (PG) for 2xD/C 220 kV Kishanganj (PG)-Kishanganj (BSPHCL) will be under regional scheme as informed by CEA. Powergrid bays ready, 2 bays charged and another 2 no. bays expected in Dec'16.
12	Modification of 132 kV Bus arrangementat 220/132 kV Purnea S/S ofPowergrid	25 <sup>th</sup> ERPC Meeting	Powergrid informed that the scheme will be implemented by Jan'17.
13	Single phase spare converter transformer units of 1x234MVA for pole 1 and 1x201.2 MVA for pole 2 at 2x500 MW HVDC Back-to- Back station at Gazuwaka (one for eachpole)	25 <sup>th</sup> ERPC Meeting	NIT completed. OBD scheduled by end Nov'16
14	GIS bays for 400 kV, 125 MVAR Bus Reactor atBaripada	24th ERPC Meeting	Powergrid informed that the work has been awarded and expected to be completed by 3 <sup>rd</sup> qtr of 2017-18.
15	Eastern Region Strengthening Scheme- XV; Construction of Farakka—Baharampur 400kV D/C (HTLS) line and Subsequent modification of LILOs	17th SCM & 30th ERPC	Linked with Bangladesh, Work awarded and construction of line under progress, expected completion by 2 <sup>nd</sup> Qtr. 2017-18.
16	Installation of 3rd 400/220 kV ,1 x31 5 MVA ICT at Durgapur & New Siliguri Substation	17th SCM & 30th ERPC	NIT done in Sept'16 and Award to be done by Dec' 16
17	Commissioning of 2xl60 MVA, 220/132 kV Auto transformer at Daltonganj substation along with 4 number of 132 kV line bays	17th SCM & 30th ERPC	Award placed, work under Progress, expected commissioning by Jun'17.
18	Extension of under construction 400kV D/C Latehar-Essar lines up to 400kV Chandra Pooling station(PG), under the scope of JUSNL	17th SCM & 30th ERPC	JUSNL to inform
19	Establishment of 2x500 MVA 400/220kV sub-station at Dhanbad by LILO ofboth circuits of Ranchi-Maithon RB 400 kV D/C line atDhanbad	17th SCM & 30th ERPC	Under TBCB
20	Construction of 6 no. 400 kV line bays and bus splitting (765 kV & 400kV) arrangement at Jharsuguda (Sundargarh) as GIS	17th SCM & 30th ERPC	Award placed, work under progress and expected completion by 3 <sup>rd</sup> Qtr. Of 2017-18.
21	Reconductoring of Maithon RB-Maithon 400 kV D/C line with HTLS conductor	17th SCM & 30th ERPC	NIT to be done in Nov'16.
22	Installation of 3rd 400/220 kV 500 MVA Transformer at Muzaffarpur	17th SCM & 30th ERPC	
23	Construction of North Karanpura— Gaya 400 kV D/c & North Karanpura -Chandwa (Jharkhand) Pooling Station 400 kV D/c	17th SCM & 30th ERPC	T/L is under TBCB route, Bay extn. Scope under POWERGRID. Chandwa bay awarded and for Gaya tendering activity under progress.

Further, Powergrid may update the present status on transmission projects approved/revised in 18<sup>th</sup> SCM which are as given below:

Sl	Scheme	ERPC/SCM	Latest status
No.		Meeting	
1	LILO of both circuits of Bongaigaon-Silliguri 400 kV D/c (Quad) (under TBCB) line at Alipurduar on multi circuit tower for about 2 km	18th SCM	
2	LILO of both circuits of Rourkela-Raigarh 400kV D/c (2nd line) at Jharsuguda on multi circuit towers for about 17 km	18th SCM	
3	Installation of 400/220 kV, 1x500 MVA ICT at Gaya S/s (400kV bay in AIS and 220kV bay in GIS)	Scheme revised in 18 <sup>th</sup> SCM	
4	Replacement of 400/220kV, 2x315MVA ICTs at Malda S/s with 400/220kV, 2x500 MVA ICTs	Scheme revised in 18th SCM	
5	Installation of 3rd 400/220kV, 1x315MVA ICT at New Siliguri S/s: to be sourced from pool of spare ICTs (400kV bay in GIS and 220kV bay in AIS)	Scheme revised in 18th SCM	
6	Installation of 3rd 400/220kV, 1x315 MVA ICT at Durgapur S/s: to be sourced from pool of spare ICTs	Scheme revised in 18th SCM	
7	Installation of 400/220kV, 2x315MVA ICTs at Jeypore S/s (one each in parallel to the existing ICTs): to be sourced from pool of spare ICTs.	Scheme revised in 18th SCM	
8	Installation of 400/220kV, 2x315MVA ICTs at Rourkela S/s (one each in parallel to the existing ICTs): to be sourced from pool of spare ICTs	Scheme revised in 18th SCM	
9	Bypassing arrangement of LILO of Meramundali – Bolangir/Jeypore 400kV S/c line and LILO of one circuit of Talcher – Meramundali 400 kV D/c line at Angul	18th SCM	
10	installation of 400/220kV, 500MVA ICT (4th) at Biharsharif S/s	18th SCM	
11	Establishment of 2x500MVA+2x160 MVA+2x80 MVA 400/220/132 kV S/S at Naubatpur	18th SCM	
12	Establishment of 2x500 MVA +2x160 MVA 400/220/132 kV GIS S/S at Bakhtiyarpur	18th SCM	
13	Establishment of 2x500 MVA +3x160 MVA+3x80 MVA 400/220/132/33 kV GIS S/S at Jakkanpur	18th SCM	
14	Establishment of 400/220/132kV, 2x500MVA + 2x200MVA new S/s at Sitamarhi	18th SCM	
15	2x125MVAr, 420kV bus reactors along with bays	18th SCM	

16	Darbhanga – Sitamarhi (New) 400kV D/c (Triple Snowbird) line	18th SCM
17	Sitamarhi (New) – Motihari 400kV D/c (Triple Snowbird) line	18th SCM
18	Establishment of 400/220/132kV, 3x500MVA + 3x200MVA new S/s at Chandauti	18th SCM
19	2x125MVAr, 420kV bus reactors along with bays	18th SCM
20	LILO of both circuits of Nabinagar-II – Gaya 400kV D/c (Quad) line of POWERGRID at Chandauti (New)	18th SCM
21	Establishment of 400/220/132kV, 2x500MVA + 2x200MVA new S/s at Saharsa	18th SCM
22	2x125MVAr, 420kV bus reactors along with bays	18th SCM
23	LILO of Kishanganj – Patna 400kV D/c (Quad) line of POWERGRID at Saharsa (New)	18th SCM
24	Installation of 400/132kV, 315MVA (3rd) ICT at Motihari substations of Essel Infra	18th SCM
25	Installation of 400/132kV, 315MVA (3rd) ICT at Banka and Lakhisarai substations of POWERGRID	18th SCM
26	Reconductoring of Rangpo – Siliguri 400kV D/c Twin Moose line with Twin HTLS conductor along with suitable modification in line bay equipment at both ends	18th SCM
27	Installation of 4th 220/132kV, 100MVA ICT at Rangpo S/s	18th SCM
28	Conversion of fixed line reactor at Purnea end of Kishanganj – Purnea 400kV D/c line to switchable line reactor	18th SCM
29	a) Nabinagar-II – Gaya 400kV D/c line with Quad moose conductor (b) Nabinagar-II – Patna 400kV D/c line with Quad moose conductor (c) Additional 1x1500MVA, 765/400kV ICT at Gaya	18th SCM
30	Derang - Angul 400 kV D/C line along with two 400kV line bays at Angul S/s	18th SCM
31	Installation of 400/220kV, 500MVA ICT (3rd) at Maithon	18th SCM
32	replacement of existing 50MVA, 220/132 kV ICT at Malda with new 160 MVA, 220/132 kV ICT	18th SCM
33	Installation of 420kV, 1x125MVAR bus reactor at Subhasgram S/s of POWERGRID	18th SCM
34	Provision of 765kV, 80MVAr single phase spare reactor at Ranchi (New) substation of POWERGRID	18th SCM

Powergrid may update the latest status.

# **Deliberation in TCC meeting**

Powergrid submitted the latest status. The latest updated status is as given below:

Sl No.	Scheme	ERPC/SCM Meeting	Latest status
1	Modification of 132 kV Bus arrangement at 220/132 kV Birpara S/s of Powergrid from existing single main & transfer bus scheme to double main scheme.	28 <sup>th</sup> ERPC Meeting	Powergrid informed that the work under progress and expected commissioning by Nov'18.
2	Change in proposed the Associated 765 kV System Strengthening Scheme inER	28 <sup>th</sup> ERPC Meeting	Under TBCB
3	Retrofitting of pilot wire protection of 132 kV Purnea (PG) – Purnea (BSPHCL) feeders	26 <sup>th</sup> ERPC Meeting	Powergrid informed that the scheme was covered in the scheme of modification of 132 kV Bus arrangement at 220/132 kV Purnea S/S of Powergrid under GIS package. The work has been awarded and expected to be completed by Mar'17.
4	Transmission System for immediate evacuation of power from North Karanpura STPP (3x660 MW) to Chandwa and Gaya Pooling stations ofPowergrid	25 <sup>th</sup> ERPC Meeting	T/L is under TBCB, POWERGRID informed that Investment approval accorded in Feb'17 BOD. Commissioning of Chandwa is expected in Sep'17, commissioning of Gaya is expected in Sept'19.
5	Procurement of two single phase spare ICT units (2x500 MW), 765/400 kV for Eastern Region to be stationed at Angul& JharsugudaS/S).	25 <sup>th</sup> ERPC Meeting	Powergrid informed that work has been awarded on March, 2015 and expected to be completed by June'17.
6	Augmentation of transformation capacity at the existing 400/220 kV Jamshedpur (PG) &Sasaram (PG)S/S	25 <sup>th</sup> ERPC Meeting	Powergrid informed that for Sasaram-1 <sup>st</sup> ICT commissioned, 2 <sup>nd</sup> ICT supply expected by June'17. Design review under progress due to failure of ICT at Alstom factory.  For Jamshedpur, commissioning expected to be completed by Mar'17.
7	Establishment of 220 kV MTPS (Extn.) – Muzaffarpur (PG) D/C line (3 <sup>rd</sup> & 4 <sup>th</sup> Circuits)	25 <sup>th</sup> ERPC Meeting	Bay construction atMuzaffarpur completed in consultancy works. To be commissioned in March'17.
8	Modification of 132 kV Bus arrangementat 220/132 kV Siliguri S/S(PG)	25 <sup>th</sup> ERPC Meeting	Completed in November, 2016.
9	Procurement of 110 MVAR, 765 kV Single Phase spare Reactor unit at Sasaram	25 <sup>th</sup> ERPC Meeting	Powergrid informed that the workhas been awarded on March, 2015 and expected to be delivered by May' 2017.
10	Establishment of Gazol 220/132 kV S/S in Malda by LILO of Malda-Dalkhola 220 kV D/C line of Powergrid	25 <sup>th</sup> ERPC Meeting	Not pertaining to POWERGRID

11	Construction of down linking transmission	25 <sup>th</sup> ERPC	Powergrid informed that four
	network for drawal of power from Kishanganj 400/220 kV S/S ofPowergrid	Meeting	numbers of 220 kV bays at 400 kV Kishanganj (PG) for 2xD/C 220 kV Kishanganj (PG)- Kishanganj (BSPHCL) will be under regional scheme as informed by CEA. 4 nos. bays have been charged.
12	Modification of 132 kV Bus arrangementat 220/132 kV Purnea S/S ofPowergrid	25 <sup>th</sup> ERPC Meeting	POWERGRID informed that the scheme will be implemented by Mar'17.
13	Single phase spare converter transformer units of 1x234MVA for pole 1 and 1x201.2 MVA for pole 2 at 2x500 MW HVDC Back-to- Back station at Gazuwaka (one for eachpole)	25 <sup>th</sup> ERPC Meeting	NIT completed. Tender evaluation in process.
14	GIS bays for 400 kV, 125 MVAR Bus Reactor at Baripada	24th ERPC Meeting	Powergrid informed that the work has been awarded and expected to be completed by 3 <sup>rd</sup> qtr of 2017-18.
15	Eastern Region Strengthening Scheme- XV; Construction of Farakka—Baharampur 400kV D/C (HTLS) line and Subsequent modification of LILOs	17th SCM & 30th ERPC	Work awarded and construction of line under progress, expected completion by 2nd Qtr. 2017-18.
16	Installation of 3rd 400/220 kV ,1 x31 5 MVA ICT at Durgapur & New Siliguri Substation	17th SCM & 30th ERPC	NIT done in Sept'16.Investment approval on Feb'17 BOD. Completion schedule-28 months.
17	Commissioning of 2xl60 MVA, 220/132 kV Auto transformer at Daltonganj substation along with 4 number of 132 kV line bays	17th SCM & 30th ERPC	Award placed, work under Progress, expected commissioning by Nov'17.
18	Extension of under construction 400kV D/C Latehar-Essar lines up to 400kV Chandra Pooling station(PG), under the scope of JUSNL	17th SCM & 30th ERPC	JUSNL to inform
19	Establishment of 2x500 MVA 400/220kV sub-station at Dhanbad by LILO ofboth circuits of Ranchi-Maithon RB 400 kV D/C line atDhanbad	17th SCM & 30th ERPC	Under TBCB
20	Construction of 6 no. 400 kV line bays and bus splitting (765 kV & 400kV) arrangement at Jharsuguda (Sundargarh) as GIS	17th SCM & 30th ERPC	Award placed. 2 no's 400kV bays by July'17 & balance by April'19.
21	Reconductoring of Maithon RB-Maithon 400 kV D/C line with HTLS conductor	17th SCM & 30th ERPC	NIT held on 20.12.16 . LOA expectedby April'17.
22	Installation of 3rd 400/220 kV 500 MVA Transformer at Muzaffarpur	17th SCM & 30th ERPC	Commissioned
23	Construction of North Karanpura— Gaya 400 kV D/c & North Karanpura -Chandwa (Jharkhand) Pooling Station 400 kV D/c	17th SCM & 30th ERPC	T/L is under TBCB, POWERGRID informed that Investment approval accorded in Feb'17 BOD. Commissioning of Chandwa is expected in Sep'17, commissioning of Gaya is expected in Sept'19.

# Members noted.

The status updated as in 34<sup>th</sup> TCC/ERPC meeting on Spare transformers & reactors to be commissioned by Powergrid for use in ER.

Sl No.	Sparetransformer/reactor	Latest status
1	1 X 315 MVA, 400/220 KV AUTO TRANSFORMERBiharshariff	Available at site.
2	1 X 315 MVA, 400/220 KV AUTO TRANSFORMERDurgapur	Utilized at 400 kV Farakka. Procurement of spare ICT is under process.
3	1 X 80 MVAR SHUNT REACTOR AS O&M SPARE RourkelaSubstation	Available at site.
4	2 X 500 MVA, 765/400 KV single phase ICTs at Angul&Jharsuguda.	Powergrid informed that the work has been awarded on March, 2015 and expected to be delivered by Mar'17.
5	1 X 110MVAr, 765KV single phase bus reactor at Sasaram	Powergrid informed that the work has been awarded on March, 2015 and expected to be delivered by Mar,2017.
FOR	MEMBERSTATES:	
1	2 X 315 MVA 400/220 kvICTs	Available
2	2 X 160/150 MVA 220/132 kvICTs	One ICT utilised at Purnea S/s,2 <sup>nd</sup> ICT available at SiliguriS/s.
3	1 X 50 MVA 132/66 kvICT	Available
SUR	PLUS FROM OLD ASSPARE	
1	3x 50 MVA, 220/132kV (to be released fromMalda (2nos.) &Birpara (1no.)S/Ss	Replaced with 160MVAtransformer.
2	2x100 MVA, 220/132kV (to be released from one at Birpara& one at Siliguri)	Taken out and kept at Birpara and Siliguri
3	2x100 MVA, 220/132kV (to be released from Purnea (2nos.)S/Stn.)	Taken out and kept at Purnea

DVC vide mail dated 15.02.17 intimated that DVC is in urgent need of a 220KV/132KV ICT which is to be installed at 220KV Dhanbad S/Stn. Availability of spare 160MVA 220/132KV ICT as available at Siliguri S/Stn under the head of "FOR MEMBER STATES." may kindly be conveyed so that necessary formalities can be completed at the appropriate level. The said transformer under subject is a NEW or OLD along with the NAMEPLATE DETAILS may also be kindly conveyed.

Powergrid may update the latest status.

# **Deliberation in TCC meeting**

Powergrid submitted the latest status which is as given below:

Sl No.			Spa	aretransfo	ormer/reac	tor		Latest status	
1	1	X	315	MVA,	400/220	KV	AUTO	Available at site.	
	TR	ANS	FORM	ERBihars	hariff				

2	1 X 315 MVA, 400/220 KV AUTO TRANSFORMER at Durgapur	Utilized at 400 kV Farakka. Procurement of spare ICT is under process. Awarded to M/S. TBEA. Expected to be delivered at site in Dec, 17.
3	1 X 80 MVAR SHUNT REACTOR AS O&M SPARE Rourkela Substation	Available at site.
4	2 X 500 MVA, 765/400 KV single phase ICTs at Angul &Jharsuguda.	Powergrid informed that the work has been awarded on March, 2015. Delivery at Angul expected in Mar'17. Delivery at Jharsuguda expected in Dec'17.
5	1 X 110MVAr, 765KV single phase bus reactor at Sasaram	Powergrid informed that the work has been awarded on March, 2015 and expected to be delivered by June, 2017.
FOR	MEMBERSTATES:	
1	2 X 315 MVA 400/220 kvICTs	Available
2	2 X 160/150 MVA 220/132 kvICTs	One ICT available at Purnea S/s, 2 ICT available at SiliguriS/s.
3	1 X 50 MVA 132/66 kvICT	Consumed at Gangtok. Gangtok transformer under repair.
SUR	PLUS FROM OLD ASSPARE	
1	3x 50 MVA, 220/132kV (to be released from Malda (2nos.) & Birpara (1no.)S/Ss	Replaced with 160MVA transformer. 50 MVA ICT scrapped.
2	2x100 MVA, 220/132kV (to be released from one at Birpara & one at Siliguri)	Taken out and kept at Birpara and Siliguri
3	2x100 MVA, 220/132kV (to be released from Purnea (2nos.)S/Stn.)	Consumed . Installed at Muzaffarpur for Muzaffarpur- Dhalkebar line.

Powergrid informed that there is no direct communication received from DVC.

Transformer kept at Siliguri is NEW. This is procured for handling the contingency requirement of O&M needs. Even though the urgent augmentation required at Malda S/S (PG), WBSETCL is providing their spare unit on loan instead of using this spare ICT identified for O&M needs.

## ERPC may note.

ITEM NO. B26:	Persistent over drawl by Jharkhand
---------------	------------------------------------

It has been observed since last few month, Jharkhand is over drawing continuously to the tune of 1.5 to 2mu per day. Jharkhand overdraw for the month November, December and January 2017 were around 40 mu, 63 mu and 52 mu respectively. Several times Jharkhand also advised to take un-requisition surplus power of NTPC plant on real time basis. However the quantum requisitioned by Jharkhand for URS power of NTPC plants was very less compare to its overdraw quantum. Numbers of instructions were also issued from ERLDC Control Room during real time operation to Jharkhand regarding the same issue. However the response of Jharkhand was not commensurate

with criticality of the situation. Details of above violations would be presented by ERLDC for discussions/suggestions.

In 130<sup>th</sup> OCC, ERLDC presented the schedule and drawal of JUSNL enclosed at Annexure-B26 and informed that JUSNL is overdrawing on continuous basis.

OCC advised JUSNL to explore for procurement of URS power to minimize the over drawal.

JUSNL informed that they have taken up the issue of URS power procurement with JBVNL but action is yet to be taken by JBVNL.

JBVNL may update.

# **Deliberation in TCC meeting**

ERLDC informed that after last OCC meeting also Jharkhand is over drawing continuously even though URS power is available. Jharkhand also not paying DSM charges.

TCC took serious concern of this matter and advised JBVNL to avail the URS power available in different NTPC stations to meet their demand.

JBVNL assured that they will avail the URS power.

# ERPC may note.

ITEM NO. B27:	Commissioning of Tie bay and main bay of BUS-I of 400 kV Ranchi-
TIENTINO. B27.	New Ranch-I & II circuit at Ranchi Substation

400kV Ranchi-Ranchi ckt-I & II has been commissioned on 30.03.2014 through main its main bay (Bay no. 427 and 430 respectively) and connected to BUS-II only at 400/220kV Ranchi Substation.

The commissioning of Tie bays (Bay no. 426, 429) and main bays (Bay nos. 425, 428) connected to BUS-I of Ranchi-New Ranchi ckt.-I & II were in the scope of M/s Corporate Power Ltd. The party M/s Corporate Power Ltd has commenced their work in the year of 2009 and after erection of switchyard equipment they left the site in the year of 2012 citing bankruptcy of the company. As information gathered from sources , M/s Corporate Power Ltd will not commission the bays for Chitarpur ckt-I & II i.e bay nos. 425,426, 428 & 429.

Due to connection of 400kV Ranchi-New Ranchi 1 & 2 with BUS-II only and the therefore lines are very much unreliable as because in case of S/D of main BUS-II, both the line will remain out of service. Further in case of any fault in their main bay, the line will be out of service.

Hence, it is requested that the above mentioned uncompleted bays may be commissioned by POWERGRID and cost of construction may be capitalized by POWERGRID. OR complete asset may be transferred to POWERGRID and POWERGRID will commission the bays and capitalized the same

TCC may discuss.

# **Deliberation in TCC meeting**

TCC technically agreed for commissioning of bays of Chitarpur ckt-I & II i.e bay nos. 425,426, 428 & 429.

TCC expressed that acquiring/modification of assets of Corporate Power Ltd. may create legal problems and advised Powergrid to discuss the issue with Corporate Power Limited to arrive at fruitful decision.

Further, Powergrid was also advised to take up the issue with CERC for amicable solution.

## ERPC may note.

ITEM NO. B28:	Issues related to associated / downstream systems—Powergrid
---------------	---

#### BIHAR

i. 4 nos. 220 kV GIS Bays at Kishenganj under ERSS XII:
 2 nos. bays have been commissioned. Program for utilisation of balance 02 no. 220kV line bays to be confirmed by BSPTCL.

#### **JHARKHAND**

- i. 4 nos. 220 kV & 4 nos. 132 kV bays at Daltonganj S/S (Anticipated Commissioning June'17): Status of downstream is as under:
  4 nos. 220 kV bays to be connected to 220 kV D/CDaltonganj-Garhwa and 220kV D/CDaltaonganj-Latehar (presently charged at 132 kV). Presently only 220 kV Daltonganj-Latehar charged at 132 kV is available. Plan for completion of 220 kV Daltonganj-Garhwa line and Garhwa S/S to be confirmed by JUSNL.
- ii. 4 nos. 132kV bays to be connected to 132kVD/C Daltonganj-Chhatarpur and 132kV Daltonganj (PG) Daltonganj (JUSNL):
   132kV bays at Daltonganj (PG) to becharged through LILO of 220kV Daltonganj-Latehar line (Presently charged at 132kV). Program for utilisation of above bays to be confirmed by JUSNL.

#### **ODISHA**

- i. 4 nos. 220 kV bays at Bolangir S/S: Out of total 4 nos. 220 kV line bays, 2 nos. are commissioned during Feb'16 and 2 nos. are pending due to unavailability of 220 kV lines of OPTCL. Program for utilisation of balance 2 no. bays to be confirmed by OPTCL.
- **ii. 6 nos.220 kV bays at PandiabilGIS:** Pandiabil (PG) substation has been commissioned in July'16. Downstream network needs to be expedited by OPTCL. Readiness of 220kV feeders by OPTCL for downstream power flow from Pandiabil (PG) S/S needs to be ensured.

**iii. 4 nos. 220 kV bays at Keonjhar S/S:** Utilisation of total 4 nos. 220 kV line bays is pending due to unavailability of 220 kV lines of OPTCL. Program for readiness of linesfor utilisation of above bays to be confirmed by OPTCL.

#### WEST BENGAL

i. 02 nos. 220 kV line bays at Subhashgram (PG) S/S: Bays are ready and idle charged under ERSS-VIII due to non-readiness of 220kV D/C Subhashgram – Baruipur Tr. line and associated bays at Baruipur. Order recently placed by WBSETCL and expected completion by Dec'17. Program for readiness of lines for utilisation of above bays to be confirmed by WBSETCL.

Members may update.

# **Deliberation in TCC meeting**

Members noted.

#### ERPC may note.

ITEM NO. B29:	Commercial issues related to NHPC Stations
---------------	--

#### 1) Payment default by beneficiaries.

#### i) NBPDCL

An amount of Rs. 14.76 Cr. is outstanding for more than 60 days which includes surcharge of Rs. 0.24 Cr.

#### ii) SBPDCL

An amount of Rs.18.99 Cr. is outstanding for more than 60 days which includes surcharge of Rs. 0.28 Cr.

#### iii) WBSEDCL

Beneficiary has not paid surcharge of Rs.29.93 Cr. (TLDP-III – Rs. 28.79 Cr.& Teesta-V / Rangit- Rs.1.14 Cr.)

Matter was also discussed in  $34^{th}$  Commercial sub-Committee meeting of ERPC at Kolkata on  $6^{th}$  Feb'2017. NBPDCL, SBPDCL & WBSEDCL may be requested to release the outstanding dues as above at the earliest.

# **Deliberation in TCC meeting**

NHPC revised the outstanding amount to 12 Cr on NBPDCL to which NBPDCL assured to make the payment within next 15 days.

NHPC revised the outstanding amount to 5 Cr on SBPDCL to which SBPDCL assured to make the payment within next 15 days.

WBSEDCL informed the tariff hike matter is in APTEL so requested to waive the outstanding amount for the time till the APTEL decision.

## ERPC may note.

#### 2) Signing of reconciliation statement.

Reconciliation statement is pending for IIndquarter for the F.Y 2016-17 in r/o GRIDCO Matter was also discussed in 34<sup>th</sup> Commercial sub-Committee meeting of ERPC at Kolkata on 6<sup>th</sup> Feb'2017 and GRIDCO intimated that the reconciliation statement will be signed within a week time. Reconciliation statements for 3<sup>rd</sup> quarter of 2016-17 have also been sent to all the beneficiaries and same have not been signed by JBVNL, DVC, GRIDCO & Sikkim till date.

#### 3) Revalidation / Opening of LC of requisite value.

All the beneficiaries are intimated that the calculation sheet of LC for F.Y 2017-18 have been sent which is based upon 105% of average billing w.e.f Jan'2016 to Dec'2016. All the concerned beneficiaries are requested to enhance the existing LC or open the new LC of requisite value before31st March'2017 and same should be valid up to 31<sup>st</sup> March '2018. SBPDCL & NBPDCL have opened the L.C's for short value. They are requested to enhance their L.C's to requisite value immediately.

#### 4) Extension of PPA in r/o TLDP-III & IV Power Stations.

WBSEDCL at present has valid PPAs for TLDP-III & IV power stations for 05 years period only .WBSEDCL had already given consent to extend the PPA of TLDP-III & TLDP-IV power stations for 35 years from the date of COD. Formal signing / execution of PPAs of TLDP-III & TLDP-IV are still pending from WBSEDCL side for 35 years period from the date of COD.

Matter was also discussed in 34th Commercial sub-Committee meeting of ERPC at Kolkata on 6th Feb'2017.

WBSEDCL may be again requested to give consent for extension of PPA at the earliest. 100% power from both the projects has been allocated in favour of West Bengal.

# **Deliberation in TCC meeting**

JBVNL, DVC and GRIDCO informed that signing of reconciliation is in progress and will be completed shortly.

SBPDCL informed that no revision of LC value is required as per their calculation. NHPC requested to share the calculation procedure with them.

WBSEDCL informed that they did not give any consent or commitment for PPA of 35 years. In their view the present price per unit energy is higher compare to the price at the time of their initial agreement. So extension of PPA at current scenario is not possible. However they agreed to find out a solution by discussion with NHPC.

WBSEDCL informed that this matter can be better discussed and solved bilaterally. NHPC agreed with WBSETCL.

# ERPC may note.

#### 5) Signing of PPA in respect of Tawang H.E. Project, Stage-I & II.

Signing of Power Purchase Agreement is pending with GRIDCO, JUVNL & WBSEDCL. All the three beneficiaries areagain requested to sign the long pending Power purchase agreement at the earliest.

#### 6) Revision of REA in respect of SBPDCL and NBPDCL

SBPDCL & NBPDCL are verifying different energy amount w.r.t their REA statements.Matter was also discussed in 34<sup>th</sup> Commercial sub-Committee meeting of ERPC at Kolkata on 6<sup>th</sup>Feb'2017 . As such, they are requested either to verify the same energy amount as per their REA or get revised REA's issued from ERPC. The discrepancies may give rise to disputes at a future date.

NHPC may update.

# **Deliberation in TCC meeting**

WBSETCL informed that the matter is in progress.

Regarding revision of REA in respect of NBPDCL and SBPDCL, TCC requested them to solve it bilaterally.

Further TCC requested NHPC to try to solve these matter bilaterally as much as possible instead of taking it to TCC forum.

# ERPC may note.

## PART C: ITEMS FOR INFORMATION

# TCC noted the following items:

ITEM NO. C1:	Status of Projects approved/under consideration of PSDF appraisal
TIEMINO.CI.	committee

The latest status of projects which are being funded by PSDF as updated in 129<sup>th</sup> OCC meeting is as given below:

SN	Name of Constituent	Name of Project	Date of approval from PSDF	Target Date of Completion	PSDF grant approved (in Rs.)	Amount drawn till date (in Rs.)	Status as updated in 129 <sup>th</sup> OCC
1	WBSETCL	Renovation & up-gradation of protection system of 220 kV & 400 kV Substations in W. Bengal	31-12-14		120.67 Cr	11.04 Cr.	95 % Supply Completed
2	WBSETCL	Transmission System improvement of WBSETCL					
3	OPTCL	Renovation & Up-gradation of protection and control systems of Sub-stations in the State of Odisha in order to rectify protection related deficiencies.	10.05.15	10.05.17	162.5 Cr.	19.53 Cr	Total contract awarded for Rs. 67.73 Cr  Erection work for received equipment is in progress.
4	ERPC	Creation & Maintenance of web based protection database and desktop based protection calculation tool for Eastern Regional Grid	17.03.16		20 Cr.	4.94 Cr. + 9.88 Cr.	1) Hardware supplied and installed. 2) SAT completed for pilot state 3) Protection database management software (PDMS) delivered. 4) Training on PDMS organised at Odisha.
5		Renovation and up-gradation of 220/132/33 KV GSS Biharsharif, Bodhgaya, Fatuha, Khagaul, Dehri on -sone & 132/33 kV GSS Kataiya	11/5/2015	Feb'2017	64.33 crore	23.68 crore	Project is on going.  Order for supply of equipment placed for Rs.13.51 Cr.
6	BSPTCL	Installation of capacitor bank at different 35 nos. of GSS under BSPTCL	5/9/2016		18.88 crore		Approved (triparty agreement among NLDC, Govt. of Bihar & BSPTCL is in under process)
7		Renovation & up-gradation of protection and control system of 12 nos. 132/33 KV GSS under BSPTCL.					Recommendation of appraisal committee is awaited. Estimated cost 54.69 crore.
8	DVC	Renovation and upgradation of control & protection system and replacement of Substation Equipment of 220/132/33 kV Ramgarh Substation			25.96		Approved by Ministry of Power
9		Renovation and upgradation of control & protection system including replacement of substation equipment at Parulia, Durgapur, Kalyaneshwari, Jamshedpur, Giridih, Barjora, Burnpur, Dhanbad and Burdwan Substation of DVC			140		Appraisal committee has recommended. It will be placed in next monitoring Committee meeting.
10a	WBPDCL	Implementation of Islanding scheme at Bandel Thermal Power Station					Appraisal committee has recommended. It will be placed in next monitoring Committee

10b		Upgradation of Protection and SAS	26.09	Approved by Ministry of Power
11	OHPC	Renovation and up-gradation of protection and control system of 4 nos OHPC substations.		OHPC will submit the detailed proposal soon as per the requirement of Appraisal committee.
12a	ERPC	Training for Power System Engineers		The proposal was examined by the Techno Economic sub group of PSDF and advised to submit revised proposal with consideration of views of the group.
12b		Training on Integration of Renewable Energy resources		The proposal was examined by the Techno Economic sub group of PSDF and advised to
12c		Training on Power market trading at NORD POOL Academy for Power System Engineers of Eastern Regional Constituents		submit revised proposal only for training at NORD POOL Academy with consideration of views of the group.

In 129<sup>th</sup> & 130<sup>th</sup> OCC, all the respective constituents are advised to furnish the status to NLDC & NPC as per the desired format as attached at **Annexure-C1** 

# Members noted for compliance

ITEM NO. C2:	Transfer capability declaration by the states of Eastern Region
--------------	---

It was decided in the NPC meeting that power system study for assessment of operational limits / power transfer capability for each state will be done by the concerned RLDC in association with concerned SLDC. Monthly TTC /ATC will be uploaded by the SLDCs at their respective websites and also communicated to concerned RLDC & NLDC on regular basis, mentioning the assumptions, limiting constraints etc.

TCC members in the 33rd meeting held on 24-06-2016 felt that grid operator should have the information on how much power they can export and import and they should restrict to that figures in order to avoid major grid disturbances.

Accordingly, TCC advised all the constituents to place the details in monthly OCC meetings till they upload the information in their respective websites.

TCC also advised JUSNL to send their representatives to ERLDC so that they could get acquainted with the ATC/TTC calculation procedure.

Subsequently, OCC members in the 120th, 123rd and 124th meetings again advised all the SLDCs to mention the constraints along with ATC/TCC figures

SLDC JUSNL already acquainted themselves with the basic procedure of TTC calculation in the month of September, 2016, by deputing a team of 3 members to ERLDC.

The present status of various SLDCs in this regard is as follows:

- All the states are computing TTC/ATC except Sikkim.
- DVC is calculating their import/export TTC/ATC and not uploading in DVC website

- BSPTCL is calculating their import TTC/ATC but neither uploading the information in their website nor declaring the same in OCC meetings.
- WBSLDC is calculating their import TTC/ATC and uploading in their website without mentioning assumptions and constraints.
- OPTCL is calculating their import TTC / ATC and sending the detail calculations to ERLDC. They would start uploading the information in their website, after it is redesigned.
- JUSNL is calculating their import TTC / ATC and sending the detail calculations to ERPC/ERLDC.

In order to ensure, safe and secure operation of the regional grid, it is essential that the states regularly carry out power system study for their operational planning and declare their power transfer capability w.r.t. ISTS through their respective transmission links with the rest of the grid for both peak and off-peak conditions on monthly basis.

Since declaration of TTC/ATC by states together with their respective assumptions and limiting constraints on regular basis is getting delayed, TCC may kindly pursue the matter with the states with topmost priority and advise SLDCs to share their computations with ERLDC.

	Anticipated network constraints in the forthcoming summer season,
ITEM NO. C3:	due to non-availability of 400kV Purnea-Biharshaiff D/C and 400kV
	Patna-Kishanganj D/C lines

400kV Purnea-Biharshaiff D/C and 400kV Patna-Kishanganj D/C lines are under breakdown w.e.f. 23-08-2016 and 26.07.2016 respectively due to unprecedented floods in Ganga and Kankai rivers.

In the 129<sup>th</sup> OCC meeting ENICL informed that 400kV Purnea-Biharshariff line would be restored by June-2017 while PGCIL in the 127<sup>th</sup> OCC meeting had informed that 400kV Patna-Kishanganj D/C line would be restored by July, 2017.

As power requirement of N. Bengal, N. Bihar, NR, NER, Nepal and Bhutan would be high during the same period, constraints may arise in meeting the full demand of these areas. ERLDC is also experiencing severe difficulty in allowing planned shutdown of transmission elements that have become critical due to long absence of the said transmission lines

ITEM NO. C4:	Reporting of Energy generated from renewable resources on dail basis
--------------	--

As per directions of MOP, energy injected from the renewable generating plants into the grid also needs to be monitored on daily basis and incorporated in the daily reports published by RLDCs and NLDC, to determine the correct percentage of energy mix for the whole country on any particular day.

The subject was deliberated in the 126<sup>th</sup> as well as earlier OCC meetings. Energy data from 10MW NTPC solar plant at Kaniha is already being received at ERLDC.

Regional entity RE generators and all SLDCs are once again requested furnish following data for their respective control areas on daily basis:

a) Grid connected RES whose scheduling and metering is done as regional entity: Maximum generation (MW) with Time and energy injected(MWh) for the previous day (from the SEM meters on a daily basis through email, till the AMR is commissioned/working) b) Grid connected RES which is under state purview:

Maximum generation (MW) with Time and energy injected(MWh) for the previous day. Concerned SLDCs to compile station wise / connection point wise energy injected into the state grid and email it RLDC on a daily basis.

Despite repeated persuasion from by OCC and ERLDC, only OPTCL and NTPC, Kaniha are providing the requisite information on daily basis.

BSPHCL, JUVNL, DVC and WBSEDCL to kindly comply with the requirement on topmost priority.

ITEM NO. C5:	Restricted Governor /Free Governor Mode Operation of generators in
TIEM NO. C5:	Eastern Region

Primary response (FGMO/RGMO) by generators (200MW and above thermal and 10MW and above hydro) is a fundamental requirement for maintaining the reliability of the bulk interconnected power system.

In the  $123^{rd}$  OCC meeting, it was emphasized that since the grid frequency is being maintained within the IEGC stipulated range (49.9 Hz – 50.05 Hz) for more than 70% of the time, concerned generators are not expected to face difficulty in providing primary response. Accordingly, it was decided to put the generators in FGMO/RGMO w.e.f. 15-08-2016.

In 124th OCC, DVC informed that all their units are in RGMO.

WBPDCL informed that Santaldih U#5 is in RGMO from 16th Aug 2016 and U#6 will be kept in RGMO after overhauling. WBPDCL added that other units are old and not capable to run in RGMO. In such cases, OCC advised the respective generators to approach CERC for exemption. WBPDCL also clarified that KTPS units cannot be put into FGMO/RGMO as these units are not having Electro Hydraulic Governor (EHG) system.

OCC requested WBPDCL to put Santaldih (U#6) and Sagardighi units on FGMO/RGMO.

In subsequent events of sudden frequency change / major load-generation imbalance, it was observed that most of the ER generators were providing response less than 70% of the ideal governor response (assuming 5% droop setting). However, some of the generators (FSTPS, KhSTPS, BkTPP) are giving responses below 37 % which is inadequate to restore the frequency within the band within the shortest possible time. This aspect was illustrated in the 129<sup>th</sup> OCC meeting.

Moreover, except DVC and CESC, in regular basis, none of the utilities are sharing their unit responses as captured by their respective DCS, through the webgroup, as agreed in earlier OCC meetings.

In view of the need of compliance of the statutory provisions of IEGC and maintenance of grid security at all times, TCC may kindly advise all concerned generating utilities to

- strictly provide adequate primary response, whenever required
- ensure availability of real time data from generator terminals (GT primary side) at ERLDC, at all times
- share their unit responses as recorded by DCS, through the webgroup created for this purpose

# ITEM NO. C6: Updated status on SCADA telemetry

CERC order (7/SM/2014) dated 29.01.2016 regarding the telemetry CERC at sl. no. 18 of their order have mentioned that

"NLDC and respective RLDC are directed to up-date the status of telemetry every month at their web-site and persistent non-availability of data from the generating stations/sub-stations be taken up in RPC meetings for appropriate direction and action".

Accordingly, ERLDC is preparing the monthly telemetry status in the prescribed CERC format every month and it is being uploaded it in ERLDC website; http://erldc.org/telemetry.aspx

33<sup>rd</sup> TCC advised all the constituents to go through the ERLDC website on regular basis and take appropriate action to make the data available to ERLDC.

The latest status of data/telemetry is enclosed at **Annexure-C6**.

ITEM NO. C7:	Submission of detailed disturbance report for PCC Meeting
--------------	---

Constituents of Eastern Region on many occasions in the recent past have failed to provide requisite data and detailed timely report with DR., EL etc. to ERPC/ERLDC for disturbances in respective control area. Thereby PCC faced immense difficulties in meaningful analysis and concluding the incidences with remedial actions/suggestions for system improvement.

33<sup>rd</sup> ERPC advised secretariat to give regular feedback to board members on non-compliance.

33<sup>rd</sup> & 34<sup>th</sup> TCC took serious note of non-submission of reports and advised all constituents to submit within reasonable time from the day of tripping the reports along with the following details as required by secretariat & enumerated in the agenda.

- Single line diagram of the affected area/region
- Pre fault conditions (Real power, Reactive power and Bus voltage)
- Tripping incident details with proper relay indication
- Disturbance record (All relays which have triggered including Main I & II)
- Analysis of the tripping incident
- Remedial measures taken
- Conclusion
- Relay settings of the relay tripped

TCC also advised all to send proper representatives in PCC forum and present respective case before PCC for effective analysis of each tripping.

# The status of data submission by ER constituents is as given below:

Sl	Name of the incidence	Status of the detailed disturbance report	
No			
	49 <sup>th</sup> PCC Meeting:		
1.	Disturbance at 400/220 kV Meramundali (OPTCL) S/s	Submitted	
	on 05-10-16 at 18:10 hrs		

2.	Disturbance at 400 kV Meramundali (OPTCL) S/s on	Submitted
	10-10-16 at 16:35 Hrs	
3.	Disturbance at JUSNL system on 09-10-16 at 18:25 Hrs	Report not received from JUSNL and PTPS
4.	Disturbance at 220 kV Ramchandrapur (JUSNL) S/s on 22-10-16 at 19:16 hrs	Submitted
5.	Disturbance at 400kV Rourkela(PG) S/s on 28-10-16 at 16:39 hrs	Submitted
6.	Disturbance at 400 kV Rangpo(PG) S/s on 05-10-16 at 14:25hrs	Submitted
7.	Disturbance at 220 kV Begusarai (BSPTCL) S/s on 21-10-16 at 12:12hrs	Submitted
8.	Multiple tripping at 132kV Purnea (PG) and 132kV	Detail report not received from BSPTCL
	Forbisgunj (BSPTCL) system on 08-10-16 at 03:33hrs	and Powergrid
	50 <sup>th</sup> PCC Meeting:	
9.	Disturbance at 220kV Bokaro (DVC) S/s on 20-11-16 at 07:50 hrs	Submitted
10.	Disturbance at 400 kV Meramundali (OPTCL) S/s on 12-11-16 at 23:11 hrs	Submitted
11.	Disturbance at 220 kV MTPS (BSPTCL) on 01-11-16	MTPS, NTPC not submitted the report in
	at 10:58 hrs	time
	51 <sup>st</sup> PCC Meeting:	
12.	Disturbance at 400/220 kV Arambag (WBSETCL) S/s on 17-12-16 at 12:11hrs	Submitted
13.	Disturbance at Budge Budge, CESC on 16-12-16 at 09:18 Hrs	Submitted
14.	Disturbance at 220 kV Theruvali (OPTCL) S/s on 15-12-16 at 07:22 hrs	<b>Disturbance record:</b> Not Submitted by OPTCL
15.	Disturbance at 400 kV Meramundali (OPTCL) S/s on 13-12-16 at 12:36 Hrs	Submitted

ITEM NO. C8:	Status of PCC recommendations
--------------	-------------------------------

Based on the deliberation in the meetings, PCC advised several recommendations for overall improvement of the protection system. The recommendations given by the PCC forum post  $34^{th}$  TCC/ERPC meetings are given below:

Name of the incidence	PCC Recommendation	Latest status
49 <sup>th</sup> PCC Meeting:		
Disturbance at 400/220 kV Meramundali (OPTCL) S/s on 05-10-16 at 18:10 hrs	<ul> <li>OPTCL was advised to carry out the following:</li> <li>PT selection scheme during bus change over should be checked and modified.</li> <li>Verify the PT fuse supervision settings in Micom relays of 220 kV lines and advised to enable if it was not enabled.</li> </ul>	OPTCL informed that they have already installed the line CVT in 220kV Kaniha line and they are planning to install the line CVTs in all the other 220kV lines.

48 <sup>th</sup> PCC Meeting:		
Disturbance at 220/132 kV NJP System on 01.09.2016 at 09:40 hrs  Disturbance at 220kV	<ul> <li>PCC advised WBSETCL to take the following measures</li> <li>To review the bus bar protection scheme at 220kV NJP</li> <li>To submit the enquiry committee report on malfunction of 220 kV Isolator arm driving mechanism of 220/132 kV ATR I.</li> <li>OPTCL was advised to change non directional over current</li> </ul>	In 50 <sup>th</sup> PCC, OPTCL
Tarkera S/s on 22-09-16 at 15:38 hrs	E/F relays in 132 KV lines at 220/132kV Tarkera S/s with directional relays Review the Bus bar protection (SIEMENS 7SS52) scheme at 220kV Tarkera	informed that old EM type distance relays have been replaced with new numerical relays at 220kV Tarkera S/s except 132kV Rourkela line-1
45 <sup>th</sup> PCC Meeting:		
Disturbance at 400/220kV Indravati (PG) and 400/220kV Indravati (OPTCL) S/s on 11-06-16 at 19:59 hrs	<ul> <li>OHPC should check and restore the bus bar protection at 220 kV Indravati (OHPC) S/s.</li> <li>PCC felt that 400/220kV ICT-I&amp;II should clear the fault on backup overcurrent protection before tripping of 400kV lines from PG end and advised OHPC to install directional O/C relays at both HV &amp; LV side of 400/220kV ICT-I&amp;II. Proper time coordination should be done with the adjacent line relays.</li> </ul>	OHPC informed that they will test the bus bar protection of 220 kV Indravati (OHPC) S/s on 25th Aug, 2016.
Special meeting convened of	on 18-04-2016 for blackout of Kanti TPS at ERPC, Kolkata	
Total station power failure (Blackout) incident at Kanti TPS on 07.04.16.	In the special meeting the following decisions were taken:  a) Powergrid was advised to change the zone 3 time settings at Muzaffarpur (PG) end as per protection philosophy of ERPC.  b) NTPC and Powergrid were advised to activate the PLCC scheme for 220kV Muzaffarpur-Kanti D/C by 26 <sup>th</sup> April, 2016 and give feedback in 42 <sup>nd</sup> PCC Meeting.	Powergrid informed that they will revise the zone 3 time setting at Muzaffarpur (PG) end by 20 <sup>th</sup> November 2016.  NTPC informed that PLCC has been installed in 220kV Kufen line.
		PCC advised BSPTCL to install PLCC system for all the transmission lines connected to 220kV Gopalgunj, Darbhanga and Begusarai and enable the carrier tripping for reliable protection.

# Respective constituents were requested to comply.

ITEM NO. C9:	Frequent	uncoordinated	tripping	in	400kV	Meramundali	S/s	of
TIEMINO.CJ.	OPTCL sy	stem						

For the last few months, system disturbances as well as multiple elements tripping in 400kV Meramundali S/s of OPTCL system are occurring frequently. These disturbances are mostly either related to protection system mal-operation or non-operation of protection system at OPTCL system. Some of the instances of disturbance are:

- Disturbance at 400/220 kV Meramundali (OPTCL) S/s on 05-10-16 at 18:10 hrs
- Disturbance at 400 kV Meramundali (OPTCL) S/s on 10-10-16 at 16:35 Hrs
- Disturbance at 400 kV Meramundali (OPTCL) S/s on 12-11-16 at 23:11 hrs
- Disturbance at 400 kV Meramundali (OPTCL) S/s on 13-12-16 at 12:36 Hrs

In 51<sup>st</sup> PCC, members felt that the protection system at 400kV Meramundali S/s is not foolproof and not operating perfectly in number of occasions. PCC decided to send a protection team of ERPC to visit 400kV Meramundali S/s to review the protection system.

ITEM NO. C10:	Payment/Receipt Status from various pool accounts in ER
---------------	---

#### 1. Payment of Deviation Charge – Present Status.

As informed by ERLDC, the status of Deviation Charge payment as on 24.01.2017 is enclosed at Annexure – C10.1. The current principal outstanding Deviation Charge of BSPHCL & JUVNL is Rs. 12.43 Cr & Rs. 38.39 Cr respectively considering bill up to 08.01.2017. Moreover, an interest amount of Rs. 2.18 Cr (as on 31.12.2016) is also payable by JUVNL due to delay payment of DSM charges. BSPHCL & JUVNL have not paid the deviation charge since 21.11.16 & 05.01.17 respectively. ERLDC has also given letter on 24.01.2017 to JUVNL requesting to liquidate the entire Deviation charges along with delayed payment interest and open the LC for required amount failing which Regulation 25A of the Open Access Regulations will be invoked and STOA will be denied.

In the CCM meeting held on 06.02.2017, ERLDC updated that the principal outstanding against JUVNL & BSPHCL had increased to Rs. 41.61 Cr & Rs. 14.07 Cr respectively.

JUVNL & BSPHCL intimated that payment would be released by the end of Feb'17.

#### 2. Reactive Energy Charges – present status.

The updated position of Receipt/Payment of Reactive Energy Charges in the pool as on 24.01.2017 (considering bill up to 08.01.2017) is indicated in **Annexure – C10.2**. The total outstanding receivable on account of Reactive charges from WBSETCL/WBSEDCL is **Rs. 3.64 Cr, GRIDCO** is **0.48 Cr** & from **BSPHCL** is **Rs. 0.94 Lac**.

Outstanding reactive amount receivable from WBSEDCL prior to 04.01.2016 is **Rs. 1.82** Cr (prior to Suo-moto order dated 21.07.2016 of the Hon'ble WBERC in the matter of case no: SM-14/16-17)

In the CCM meeting held on 06.02.2017, GRIDCO representative informed that they have released the payment on 04.02.2017.

It was further informed that Member Secretary, ERPC has communicated to Hon'ble WBERC regarding clarification to suo moto order dated 21.07.2016 for resolution of WBSETCL/WBSEDCL dues prior to 04.01.2016.

#### **Workshop & Expenditure details**

ERPC Secretariat and ERLDC in co-ordination with GRIDCO LIMITED had organized a Two day workshop on "Black Start & Restoration" and "Emerging Issues in Power System Operation" held at Hotel Sandy's Tower, Bhubaneswar on 17.06.16 & 18.06.16. An expenditure of Rs. 5.51456 Lacs incurred for arranging the above workshop have been reimbursed to GRIDCO from Reactive account on 30.11.2016.

#### 3. RRAS Account ---- Present Status.

As furnished by ERLDC, The updated position of Payments to the RRAS Provider(s) from the DSM pool and Payments by the RRAS Provider(s) to the DSM pool as on 24.01.2017 (considering bill up to 08.01.2017) is indicated in **Annexure** – **C10.3.** So far Rs. 123.0 Cr have been settled under RRAS in ER.

#### 4. Congestion Account - Present Status

The status of congestion charge payment after full settlement is enclosed at Annexure – C10.4.

#### 5. Status of PSDF

As informed by ERLDC, an amount of **Rs. 10.0 Cr** from Reactive account have been transferred to PSDF after 33<sup>rd</sup> Commercial sub-committee meeting held on 03.11.16. With this the total amount of **Rs. 900.40 Cr** has been transferred to PSDF so far. No amount from Deviation pool has been transferred to PSDF A/c since 29.06.16 and surplus amount in deviation pool is being utilized for settlement of RRAS Bill. The break up details of fund transferred to PSDF (till 24.01.17) is enclosed in **Annexure-C10.5.** 

ITEM NO. C11:	Reconciliation of Commercial Accounts
---------------	---------------------------------------

#### 1. Reconciliation of Deviation Accounts.

At the end of 3<sup>rd</sup> quarter of 2016-17, the reconciliation statement (Period: 01.10.16 to 31.12.16) has been issued by ERLDC on 04.01.17 and statements had been sent to the respective constituents and also uploaded the same at ERLDC website (<u>www.erldc.org</u>). The constituents were requested to verify /check the same & comments if any on the same were to be reported to ERLDC by 21.01.2017. The status of reconciliation is enclosed in **Annexure-C11.1**.

JUVNL, WBSETCL, SIKKIM, VEDANTA, APNRL, GATI, IBEUL & JLHEP (Dans Energy) have not signed reconciliation statement for any quarter of 2016-17.

Further BSPHCL, DVC & GMR have not signed reconciliation statement for 3<sup>rd</sup> Quarter of 2016-17.

In the CCM meeting held on 06.02.2017, ERLDC updated that BSPHCL & GMR have reconciled the statement for 3<sup>rd</sup> Quarter for 2016-17. WBSETCL & JUVNL informed that they would get the outstanding reconciliations completed within next week.

APNRL informed that they have sent reconciled statements for two quarters for 2016-17 through post. For 3<sup>rd</sup> quarter there is some discrepancy which would be intimated to ERLDC at the earliest.

ERLDC requested constituents to send scanned copies of reconciliation statement for early settlement.

#### **Deliberation in TCC meeting**

ERLDC informed that SIKKIM, VEDANTA, GATI, IBEUL & BRBCL have not signed the reconciliation statement.

OPTCL informed that they will take care of the Reconciliation of Deviation Accounts related to Vedanta.

Gati informed that they will do the reconciliation within a week.

#### 2. Disbursement of Interest due to delayed payment of deviation charges

ERLDC had received an amount of **Rs. 30.53692 Lac** from Vedanta on 25.11.16 towards interest due to delayed payment of deviation charges in FY 2016-17. The above amount was paid towards Ancillary services for Week-30 (Period: 17.10.16 to 23.10.16).

#### 3. Reconciliation for STOA payments made to SLDC / STU:

ERLDC have informed that the reconciliation statements of STOA payments for the period Apr'16 to Dec'16 have been send to the DVC, OPTCL and WBSETCL for checking at their end and confirmation.

- ⇒ WBSETCL and OPTCL are yet to confirm for the month of June'16 to Dec'16.
- ⇒ DVC has confirmed for the entire period.

As per clause 15.1 of CERC approved STOA bilateral procedure since the confirmations have not been received within 2 weeks from the date of issuance of the letters the statement issued by ERLDC have been deemed to be reconciled. However, signing of reconciliation statement is desirable.

In the CCM meeting held on 06.02.2017, ERLDC updated that WBSETCL had reconciled for the month of June'16 to Dec'16. OPTCL informed that they have sent reconciliation statement through post.

ERLDC once again requested to send scanned copies for early settlement.

#### 4. Reconciliation for payments received from STOA applicants:

The reconciliation statements of STOA payments for the period of Apr'16-Dec'16 have been send to the CESC, DVC, GMRKEL, JITPL, JUVNL, SAIL-RSP, TATA Steel and WBSEDCL for checking at their end and confirmation.

- ⇒ DVC has confirmed for the entire period.
- ⇒ CESC, GMRKEL, JITPL are yet to confirm for the period of Oct-16 to Dec-16.

- ⇒ JUVNL has not confirmed for the entire period of Apr-16 to Dec-16.
- ⇒ SAIL-RSP is yet to confirm for the period of Jul-16 to Dec-16.
- ⇒ TATA Steel is yet to confirm for the period of Jul-16 to Sep-16.

As per clause 15.1 of CERC approved STOA bilateral procedure since the confirmations have not been received within 2 weeks from the date of issuance of the letters the statement issued by ERLDC have been deemed to be reconciled. However, signing of reconciliation statements is desirable

The details is attached in the **Annexure-C11.4**.

In the CCM meeting held on 06.02.2017, ERLDC updated that CESC, GMR & JITPL have confirmed the reconciliation statement for Oct-16 to Dec-16. JUVNL informed that reconciliation would be completed very shortly.

ITEM NO. C12: Detailed Procedure for Ancillary Services Operations w.e.f 21.11.16

Hon'ble CERC vide notification no. 1/10/2012-Reg.Aff. (REC-Gen)/CERC issued Final Detailed Procedure for Ancillary Services Operations. It is effective from 21.11.16 onwards. The following important new clauses are added /amended with in the Detailed Procedure for Ancillary Services Operations:-

As per clause 12.4 of Detailed Procedure for Ancillary Services Operations, Deviation charges shall be worked out by RPCs strictly in accordance with the CERC (Deviation Settlement Mechanism and related matters) Regulations, 2014. *The deviation charges for each entity shall be accounted without any adjustment for Payable= Receivable.* 

In the last CCM on 06.02.2017, it was informed from Secretariat that the required modifications have been implemented from the week beginning 28.11.2016.

ITEM NO. C13: Payment of DSM charges by JUVNL to ER Pool due to incorrect meter reading for 132 KV Joda (Gridco) -Kendoposi (JSEB)

Due to reverse polarity of Joda end meter for Inter-state tie of Joda –Kendoposi line deviation account needs to be revised. The reverse polarity of Joda end meter couldn't be identified due to bypassing of Kendiposi end meter of 132 KV Joda(Gridco)-Kendoposi(JSEB) line, and data validation of the meter data of Joda end couldn't be done during period 04.05.11 to 03.05.15.

Total UI/DSM charges paid by GRIDCO due to faulty recording of meter on 132 Joda-Kendiposi Line is Rs 6,01,62,446 i.e (6.01 Cr),but actually Gridco have to receive Rs 6,01,62,446 due to reversal of power flow from Joda to Kendiposi.

So, Net UI/DSM charges receivable by Gridco is Rs 12,03,24,892 (2 times above Figure). The same amount (i.e Rs 12,03,24,892) has to be paid by JUVNL as it is a tie line between Odisha and Jharkhand.

Data has been checked by ERLDC & ERPC. The adjustment would be done from week beginning 06.02.2017.

In the last CCM on 06.02.2017, ERLDC explained in details. It was decided that the adjustment for GRIDCO and JUVNL would be done in 6 equal weekly installments in monetary terms instead of energy terms. The adjustment would begin w.e.f 06.02.2017 and the calculation sheet will be shared.

ITEM NO. C14:	Accounting for Re-import of Kurichhu Energy by Bhutan w.e.f
TIEMINO. C14:	December, 2014 Agenda items submitted by APDCL in 34 <sup>th</sup> CCM

Based on decision in a meeting convened at ERPC on 03.11.2014, APDCL filed a Petition before the CERC seeking rectification on the accounting anomalies in monthly REAs of ERPC from April'2003 to November'2014 on re-import of Bhutan power through Assam grid. After hearing of that Petition No. 150/MP/2015, CERC issued order dated 13.06.2016 and on that basis APDCL has submitted the Energy Bill of Rs. 2,13,84,866.00 on account of re-import of Kurichhu energy by Bhutan for the period from April'2003 to November'2014.

However, as the energy drawl / exchange of Bhutan is a continuous process, APDCL has been continuing supply of energy to Bhutan on the basis of existing arrangement considering the intercountry relation between India and Bhutan. The said CERC order is silent in the methodology of accounting and billing for subsequent period from December'2014 onwards. Meanwhile, the DSM rate also comes down drastically with the improvement of average frequency within the range of 50 Hz resulting average DSM tariff in and around zero; as a result there is little chance of recovery of cost of energy supplied by APDCL on the average UI / DSM mechanism during present unbilled period. APDCL therefore is unable to raise bill on this mechanism.

APDCL therefore requests the ERPC forum to deliberate on the issue and take decision:

- (a) Ensuring the cost of supply of power to Bhutan from December'2014 onwards either at the average cost of power purchase of APDCL at 33 KV level from the DSM pool account till the present arrangement continues.
- (b) Else, APDCL be reimbursed with the energy quantum with necessary Transmission losses and another 5% additional loss to compensate for default in reimbursement in line with the system followed at present in case of Banking arrangement of power.
- (c) Take any other decision ensuring the justice of both ends.

PTC vide their letter vide No-PTC/MTFG/ERLDC/11428 dated-17.10.2016 requested for a meeting to address the issue. Letter of PTC/APDCL at **Annexure-C14.** 

In the last CCM held on 06.02.2017, APDCL explained in brief. ERPC & ERLDC were of the view that installation of SEM meters at 33 Kv & 11kV inter-connection with Bhutan would be the best solution to the problem. APDCL submitted that the concerned sub-stations were unmanned & remote and collection of weekly meter reading would be feasible.

It was decided that a separate meeting would be held with APDCL, PTC, NERLDC, NERPC & ERLDC for seeking a solution to this issue.

ITEM NO. C15: Meter readings related issues

#### A. Erroneous Data/meter reading

#### i. Siliguri (PG)

Siliguri(PG) end meter NP-5950-A installed for 132 KV Melli (Sikkim) line is recording 5-10 % as compared to Melli end meter data since shifting of Bays from AIS to GIS at Siliguri i.e on 29.10.16. The above problem was informed to Sliguri PGCIL telephonically as well as through email with request to check CT and PT connection to meter at Siliguri. Meter data validation of the aforesaid line is not possible until meter data at siliguri end is correct.

In the last CCM held on 06.02.2017, PGCIL informed that the meter had been rectified and data has been sent of ERLDC for checking. ERLDC informed that they would check the data and accordingly intimate Powergrid.

#### ii. Rangpo (PG)

Meter NP-8713-A installed at Rangpo PG end of 400 KV Teesta-III is recording almost 66 % as compared to actual export from Teesta-III since 14.01.17. Initially the line was idle charged so it was not possible to verify the Rangpo end meter data of the said Line. The problem was identified after synchronization of Line from Teesta-III end for evacuation of power wef 14.01.17.

PGCIL Rangpo was requested by ERLDC to check CT and PT connection to meter and also to check the voltage and current of all 3-phase to meter terminal. Rangpo informed that the problem has been identified and rectified on 17-01-17 around 16:00 Hrs. However problem is still persisting.

In the last CCM held on 06.02.2017, PGCIL informed that the correct CT ratio would 3000/1 instead of 2000/1 present in the data base.

## iii. Forbisganj at BSPTCL

Kishanganj(BSPTCL) end meter of 132 KV Purnea(PG) Line is not recording any flow compared to Purnea PGCIL end since 14:00 hrs of 29th June 2015. It was gathered that line is feeding load to Farbisganj at BSPTCL regularly through Transfer Bus of Kishanganj bypassing the SEM at Kishanganj. Accordingly 02 nos of SEM were installed at Forbesganj on 03.02.16 and DCD for downloading the data was handed over to BSPHCL. BSPHCL informed that due to installation problem of meter software, data is not being sent to ERLDC. In 34<sup>th</sup> TCC/ERPC, BSPTCL informed that the line would be shifted from transfer bus to main bus and there would no longer be any metering issue. **However, the issue is still unresolved.** 

In the last CCM held on 06.02.2017, BSPHCL informed that the line had been transferred to main bus on 0501.2017. ERLDC was requested to check the data.

#### iv. Testing of Main Energy Meter for Tala-Siliguri 400kV Feeder No.1 at Siliguri end.

Druk Green Power Corportion Limited (DGPC) has informed that during the months of November,2016 and December,2016, the energy recorded by main meter for 400kV Tala- New Siliguri feeder No.I was found insistent as difference in energy recorded between main meter and check meter was beyond the permissible limit of 0.3. Further on 28.12.2016 the energy recorded by main meter at Siliguri end was less by 195.32% compared to energy recorded by main at Tala end. In the absence of reliable energy recorded by the main energy meter, the energy bill for the month of November and December,2016 was rised on energy recorded by the check meter.

Accordingly, DGPC have requested to test the energy meters at Siliguri end for all Tala-Siliguri feeders, particularly No.I main energy meter for its functioning & arrange for the replacement if found out of order at the earliest.

In the last CCM held on 06.02.2017, Powergrid informed that the meters at Binaguri were checked and found ok. PTC is requested to provide further details to Powergrid so that the issue could be identified.

#### B. Non Receipt of SEM data from Various Locations

#### i. PPSP and Arambagh

400 KV PPSP-Ranchi New (PG) Line & 400 KV Arambagh-Ranchi New (PG) Line has already been charged and synchronized on 06.01.17. Interface meter has been installed at PPSP and Arambagh end of aforesaid Line. The aforesaid Line is a Tie Line and PPSP and Arambagh are 02 new Tie points in WBSETCL system wef 06.01.17. WBSETCL was requested to advise its vendor M/s Squarem Tech to collect the SEM data of above 02 locations also apart from the existing Tie Point locations and send the same to ERLDC by every Tuesday. ERLDC is not receiving the SEM data of PPSP and Arambagh regularly.

In the last CCM held on 06.02.2017, WBSETCL informed that henceforth data would be sent regularly.

#### ii. Pandiabili at PG

SEM data of Pandiabili end of 400 KV Baripada line is not being sent from Pandiabili since last week of Nov 2016. The same meter is also not integrated in AMR till now. The matter is already communicated to PGCIL.

In the last CCM held on 06.02.2017, POWERGRID informed that the AMR port is defective and they have arranged manual downloading of data from Pandiabil.

ITEM NO. C16:	Implementation of Automatic Meter Reading in Eastern Region
---------------	---

AMRs have been installed at 97 locations in 1<sup>st</sup> phase and 25 locations in 2nd phase in Eastern region. Due to addition of new substations/generating stations/transmission lines in Eastern Region, another 32 new locations required to be added under AMR project as 3<sup>rd</sup> phase of implementation.

Inclusion of new locations and total cost involvement for AMR 3<sup>rd</sup> phase were last discussed in 34<sup>th</sup> TCC/ERPC meeting held on 18.11.16/19.11.16 wherein TCC/ERPC approved the cost of *Rs.1.72 Cr including 4 years of AMC. ERLDC updated that priority list of substations to be progressively integrated in AMR has been* enclosed in **Annexure-C16.** 

In the last CCM held on 06.02.2017, POWERGRID informed that in the 3<sup>rd</sup> Phase 37 new locations (173 meters) and 21 old locations (76 new meters) had been integrated. It has been planned that the 21 old locations would be completed on priority by March,2017. Thereafter remaining locations would be taken up for completion by end of May,2017.

ITEM NO. C17:	Incorrect	Date	Format	of	Meters	at	Angul	PG	and	Kishanganj
TIEMINO.CI7:	BSPTCL									

Angul end L&T Meter NP-7995-A installed at ICT-3 and NP-8076-A at 765 KV Angul-Srikaulam Line-2 is having incorrect date since installation of meter. Further similar problem of incorrect date is also found at Kishanganj BSPTCL end Elster make meter for 220 KV Kishanganj-Kishangaj Line-3. These meters were installed by PGCIL and needs necessary correction of dates.

In the last CCM held on 06.02.2017, Powergrid informed that they have replaced the concerned meters.

ITEM NO. C18:
---------------

In 1<sup>st</sup> and 2<sup>nd</sup> phase, AMR have been installed at 122 locations in ER. Out of 122 locations there are 12 locations with 15 nos of meter having defective RS-485 port and for this reason meter's are not communicating with AMR system. The above problem was also reported by the implementing Vendor i.e M/s TCS with a request to change the defective RS-485 meter with healthy one so that the entire meter from the above locations may report in AMR system. Due to the above problem, non-reporting meter data is being sent by respective substations by downloading through Optical port by DCD/Laptop. The details of location and meters are enclosed in **Annexure-C18.** Powergrid was requested to replace the meter with healthy meter.

In the last CCM held on 06.02.2017, it was decided that the defective meters would be replaced with Genus make new meters as soon as the integration of AMR data formats was completed by TCS.

ITEM NO. C19:	Procurement of new SEM's and DCD/Laptops
---------------	--

In 30<sup>th</sup> ERPC meeting procurement of 965 no of SEM's and 110 nos of Laptop/DCD (in 111<sup>th</sup> OCC meeting) was approved. Further 31st TCC/ERPC approved the cost sharing mechanism of expenditure on SEM's and DCD/Laptops along with POWERGRID overhead charges @ 15% to be shared by the beneficiaries constituents of Eastern Region in proportional to the share allocation for the month in which the proposal was approved in the ERPC meeting. In 32<sup>nd</sup> TCC/ERPC, Powergrid intimated that order had been placed on 15.03.2016. In 33<sup>rd</sup> TCC/ERPC, PGCIL

informed that delivery is expected in six phases starting August'16. In last CCM, Powergrid informed that the new meters were under inspection and scheduled to start delivery from 1st week of December'16.

In the last CCM held on 06.02.2017, Powergrid informed that receipt of Genus make meters have already started and had been installed in some locations and their integration with AMR was under process by M/s TCS.

ITEM NO. C20: Training for new Genus Make meter handling and software

In the last CCM held on 06.02.2017, on request of constituents Powergrid proposed to organize a training on new Genus make meter handling and software at ERPC on 3<sup>rd</sup> March, 2017 and a repeat training on 17<sup>th</sup> March, 2017 at Patna. ERPC, Secretariat requested Powergrid forward formal proposal.

ITEM NO. C21: List of Assets commissioned by POWERGRID

Powergrid has submitted a list of assets commissioned in the last CCM held on 06.02.2017. The same is at Annexure- C21.

ITEM NO. C22: 11KV Auxiliary power supply of 400KV Berhampore Powergrid Substation

In 34<sup>th</sup> TCC, WBSEDCL informed that the construction of dedicated line has been delayed due to ROW issues. The same has been resolved now and the construction of dedicated line will be completed by December, 2016.

WBSEDCL added that cable needs to be laid out for highway crossing for which cost estimate will be given to Powergrid within a week.

Powergrid agreed to do the payment after receiving the estimate.

WBSEDCL assured that on receipt of deposit from Powergrid all efforts will be made to resolve the issue on reasonable time.

In 129<sup>th</sup> OCC, PGCIL informed that requisite amount will be deposited by tomorrow (i.e. 18.01.2017). WBSEDCL informed that work is in progress and expected to be completed by another 10 days.

In 130<sup>th</sup> OCC, WBSEDCL informed that the requisite amount has been received from Powergrid and the work will be completed by 15<sup>th</sup> March, 2017.

ITEM NO COO.	HIGHLIGHTS &	GRID	PERFORMANCE	FOR	THE	PERIOD
ITEM NO. C23 :	FROM OCT' 2016	TO DE	C' 2016			

#### A) Real time operation:

During the period under review, power supply position in the region was as under:

	Oct-15	Nov-15	Dec-15	Jan-16	Oct-16	Nov-16	Dec-16	Jan17
Avg Frq. (Hz)	49.98	49.99	49.98	49.98	50.0	49.99	49.99	50.0
PkDmd (MW)	18268	17668	17120	17485	19634	18799	17502	18142
Energy Consum. (MU/day)	377	341	333	341	381	332	325	341
ISGS Gen (MU)	3964	3653	3556	3445	4750	3967	3864	3795
Region Gen (MU)	13751	12334	12459	12392	14961	12903	12920	13151
% increase in Reg					8.80	4.61	3.70	
Gen.								6.12

#### B) System Operational Discipline during the period from Oct-16 to Jan-17

i) The month-wise energy drawls of ER constituents were as given hereunder:

	Oct	Oct-16		Nov-16		Dec-16		Jan-17	
	SCH	ACT	SCH	ACT	SCH	ACT	SCH	ACT	
BSPHCL	2110.2	2074.0	1822.2	1812.0	1781.6	1794.4	1842.0	1849.3	
JUVNL	488.3	512.1	435.5	476.4	449.9	512.9	477.3	531.0	
DVC	-886.4	-878.0	-1022.8	-1051.5	-983.6	-1012.3	-1017.4	-1034.9	
OPTCL	565.0	553.5	599.2	602.4	571.8	546.8	534.4	526.9	
WBSETCL	1133.7	1145.4	744.5	765.2	641.4	662.6	737.8	782.0	
SIKKIM	40.7	32.0	38.9	36.0	45.2	40.9	48.8	42.4	

#### C) Frequency & Voltage

i) Frequency profile for the period during **Oct-16 to Jan-17** is given hereunder. The frequency mostly remained within the allowable range for the entire period

		% of time for which frequency							
Month	<49.9	49.9-50.05	> 50.05	IEGC band 49.9-50.05					
Oct-16	5.72	74.78	19.50	74.78					
Nov-16	9.28	72.22	18.50	72.22					
Dec-16	11.04	69.57	19.39	69.57					
Jan-17	6.20	70.42	23.38	70.42					

# ii) Maximum and minimum voltages recorded at some important 400 kV sub-stations were as follows:

GVID GT A TYONY	Oct-	16	Nov-16		Dec-16		Jan17	
SUB-STATION/ POWER STN.	MAX.	MIN	MAX.	MIN	MAX.	MIN	MAX.	MIN
TOWER STN.	(KV)	(KV)	(KV)	(KV)	(KV)	(KV)	(KV)	(KV)
FARAKKA	422	407	425	409	429	410	426	406
SUBHASGRAM	426	369	437	380	434	392	434	386
DURGAPUR	421	403	421	404	422	405	422	404
JEERAT	423	372	432	379	430	390	429	387
PURNEA	422	389	425	395	426	396	426	396
MUZAFFARPUR	416	381	416	386	417	387	417	388
JAMSHEDPUR	430	414	431	415	434	418	433	418
RENGALI	410	371	411	397	411	398	414	386
JEYPORE	421	382	421	380	431	380	431	381

### **D)** Constituent-wise demand met is given below:

		Oct-15	Nov-15	Dec-15	Jan-16	Oct-16	Nov-16	Dec-16	Jan-17
BSPHCL	AVG MAX DMD(MW)	3222	3211	3277	3280	3493	3466	3364	3535
	MU/DAY	67	64	66	67	70	64	62	65
JUVNL	AVG MAX DMD(MW)	1083	1108	1079	1084	1099	1101	1105	1138
00,172	MU/DAY	24	24	24	24	23	23	24	24
DVC	AVG MAX DMD(MW)	2500	2483	2497	2592	2601	2426	2443	2543
	MU/DAY	58	58	59	60	62	59	59	62
ODISHA	AVG MAX DMD(MW)	3930	3813	3609	3731	3765	3558	3509	3575
	MU/DAY	79	73	68	71	72	67	65	68
W.	AVG MAX DMD(MW)	7255	6517	6087	6191	7806	6601	6336	6632
BENGAL	MU/DAY	149	123	116	120	153	119	114	123

### E) Inter-regional energy exchange during the review period were as follows: (Figures in MU)

Region	Oct-16		Nov-16		Dec	Jan -17		
Region	SCH	ACT	SCH	ACT	SCH	ACT	SCH	ACT
NER	-53	406	49	429	139	498	144	-146
SR	742	516	693	668	373	526	386	395
WR	-99	-42	130	-40	199	-332	-120	35
NR	2253	1943	1775	1545	1859	1724	1846	1945
TOTAL	2842	2823	2646	2602	2569	2519	2255	2229

**F)** Reservoir levels of important hydro stations in ER during Jun-16 to Oct-16 (as on last day of the month) is given below:

STATION	MDDL/ FRL	Oct-16	Nov-16	Dec-16	Jan-17
BURLA	630.06	629.25	628.25	630.06	625.62
BALIMELA	1507.20	1506.80	1504.20	1507.20	1500.90
RENGALI	123.00	122.91	122.54	123.00	122.16
U. KOLAB	856.66	856.37	856.39	856.66	855.82
INDRAVATI	639.32	638.88	639.01	639.32	638.25
MACHKUND	2747.50	2745.00	2740.60	2747.50	2735.05

#### **G) IMPORTANT EVENTS :**

- 1) 400/220 kV, 500MVA ICT-I at Kishangani S/s first time loaded at 20:12HRS of 03/10/16.
- 2) 400/220 kV, 125MVAr B/R-II at Maithon charged for the first time at 15:15HRS of 04/10/16.
- 3) LILO of 132kV Baripada (PG) Rairangapur (OPTCL) at Bangiriposi (OPTCL) was charged for the first time at 15:55HRS of 04/10/16.
- 4) 220kV Kishanganj(PG)-Kishanganj\_New (BSPTCL) ckt- III & IV were charged for the first time at 13:15HRS and 13:29HRS of 05/10/16 respectively.
- 5) 220/132kV, 160 MVA ICT-I & II at Kishanganj\_New(BSPTCL) were charged for the first time at 17:55HRS and 18:07HRS of 05/10/16 respectively.
- 6) 50 MVAr L/R I & II (taken as B/R) of 400kV New Ranchi-PPSP-I & II at New Ranchi were charged for the first time at 15:24HRS and 14:14HRS respectively of 15/10/16.
- 7) 132 kV Kishanganj (New)-Forbisganj D/C first time loaded at 11:38HRS of 20/10/16.
- 8) 125MVAr B/R-II at Durgapur was charged for the first time in parallel with the existing 50MVAr B/R-I at 17:06HRS of 21/10/16.
- 9) 63MVAr L/R of 400kV Chaibasa-Kolaghat at Chaibasa was charged for the first time (along with the line) at 17:14HRS of 25/10/16.
- 10) 400kV Kharagpur-Chaibasa-II was charged for the first time at 23:30 HRS of 10/11/16.
- 11) 132 kV GIS Main Bus I & II of Bajkula 132/33 kV GIS (WBSETCL) S/s were charged(from Contai S/s) at 16.19 Hrs & 16.20 Hrs of 27.10.16 respectively.
- 12) 132/33 kV 50 MVA ICT I at Bajkul 132/33 kV GIS (WBSETCL) S/s was charged at 16.50 Hr(HV side) & 16.55 Hrs(LV side) of 27.10.16.


- 13) Test synchronization of 500 MW, Unit#4 of Sagardighi TPP was done at 13.32 Hrs of 15.10.16.
- 14) 500MVA, single phase  $(765/\sqrt{3} / (400/\sqrt{3}) \text{ kV Spare ICT at Angul (in place of ICT-III, B-ph)}$  was charged for the first time at 11:38 Hrs of 16.11.16.
- 15) 400kV Jamshedpur-Rourkela-II was LILOed successfully at Chaibasa and 400kV Jamshedpur-Chaibasa-II and 400kV Chaibasa-Rourkela-II were charged for the first time at 23:28 HRS of 19/11/16 and 00:16 HRS of 20.11.16 respectively.
- 16) 765kV Angul-Srikakulam -II along with Switchable Line Reactor (3X80MVAR) at both end were charged for the first time at 11:20 Hrs of 27.11.16.
- 17) 220kV Bidanasi-Cuttak line charged on 29th November 2016
- 18) 400/132kV ICT-I at Nabinagar first time charged on no load at 19:27hrs of 02/12/16.
- 19) Unit 3 of KBUNL(Muzaffarpur) along with GT-III( 250 MVA, 220/15.75kVA) synchronised for first time as regional entity on 03/01/17 at 10:10hrs.
- 20) 220kV Gaya- Sonenagar-I charged on 04/12/16 at 17:18hrs.
- 21) Bokaro-A Unit-I along with GT(400/21KV) was synchronised for the first time 04/12/16 at 22:44hrs
- 22) 400KV, 125MVAr B/R-II at Kishanganj was charged for the first time on 07/12/16 at 18:44hrs.
- 23) 220/132kV, 100 MVA ICT-II at Muzaffarpur was idle charged for the first time in parallel with existing 100 MVA ICT-I at Muzaffarpur (for feeding power to Nepal) on 16/12/16 at 05:02hrs. Subsequently the same was loaded at 06:40hrs of 16/12/16.
- 24) 132kV Purnea-Purnea-III charged first time after re-conductoring to HTLS ACCC (Casablanca) on 20/12/16 at 18:01hrs.
- 25) LILO of 400kV Binaguri-Bongaigaon line -III and IV at Alipurduar (Powergrid) Sub-station were charged for first time on 22/12/16. Binaguri Alipurduar I & II were charged at 17:57 hrs and 19:04 hrs respectively of 22/12/16. Alipurduar Bongaigaon I & II were charged at 20:49 hrs and 21:43 hrs respectively of 22/12/16.
- 26) 125MVAr BR-III at Durgapur was charged for the first time on 28/12/16 at 16:10 hrs.
- 27) 220kV Kishanganj(PG)-Kishanganj\_New(BSPTCL) I & II were anti-theft charged for the first time from Kishanganj\_New(BSPTCL) end by keeping isolator open at Kishanganj(PG) end on 28/12/16 at 17:55hrs.
- 28) 50MVAR B/R at Berhampur was charged for the first time on 29/12/16 at 16:18 hrs.
- 29) 132kV Purnea-Purnea-I TL charged first time after re-conductoring to HTLS ACCC (Casablanca) on 30/12/16 at 10:23hrs.

- 30) LILO of 132 KV Gopalganj-Siwan one Ckt; 18.9 km at 132/33 KV Hathua S/s along with 20 MVA, 132/33 kV transformer commissioned on 06.12.2016.
- 31) LILO on 132 KV Supoul-Phoolparas one Ckt; 18.8km at 132/33 KV Nirmali S/s along with 20 MVA, 132/33 kV transformer commissioned on 28.12.2016.
- 32) 132 kV Dalsingsarai- Bachhwara(TSS) S/c commissioned on 20.12.2016.
- 33) 50MVAr LR of 400kV RTPS-Ranchi-II charged for the first time at 20:01Hrs 03/01/17.
- 34) 400kV Main bay of Nabinagar-Sasaram-II at Nabinagar charged for the first time at 18:44Hrs of 06/01/17.
- 35) 400kV New Ranchi New PPSP-I (charged as 400kV New Ranchi PPSP) charged for the first time at 17:38Hrs of 06/01/17 and 400kV New Ranchi New PPSP-II (charged as 400kV New Ranchi Arambagh) charged for the first time on 18:21Hrs of 06/01/17.
- 36) 132kV Purnea (PG)-Purnea (BSPTCL)-II was charged for the first time after re-conductoring with HTLS ACCC (Casablanca) conductor at 15:28Hrs of 07/01/17.
- 37) 400kV Teesta-III- Rangpo charged for the first time at 18:14Hrs of 13/01/17.
- 38) Teesta-III has charged its GTs along with units for the first time as follows:

i) GT 1 & Unit 1: 22:00Hrs of 14/01/17 ii) GT 3 & Unit 3: 18:55Hrs of 15/01/17 iii) GT 5 & Unit 5: 22:26Hrs of 24/01/17 iv) GT 2 & Unit 2: 20:23Hrs of 27/01/17

v) GT 6 & Unit 6: 16:44Hrs of 28/01/17

\*\*\*\*\*\*



### LIST OF PARTICIPANTS IN THE 35<sup>th</sup> ERPC MEETING

Date: 25.02.2017 Venue: Hotel BNR Chanakya, Ranchi

Sl. No.	Name S/Shri	Designation	Contact Number e-mail id
Govt. of Sikkim			
1.	N.T.Bhutia	Principal Chief Engineer-cum-	7797631298
		Secretary, Energy & Power Dept.	ntbhutiapower@gmail.com
2.	K.B. Kunwar	Principal Chief Engineer,	9434032924
		Energy & Power Dept.	kunwarkb@gmail.com
3.	Dinesh Kharel	Addl. Chief Engineer	7797756309
		Energy & Power Dept.	dkharel64@gmail.com
BSPTCL			
1.	Sandip K.R. Pudkalkatti	Managing Director	
			md.bsptcl @gmail.com
2.	Bhaskar Sharma	Director (Project)	9771496900
			bsharma2407@gmail.com
3.	Ravi Shankar Prasad	EEE(P& E)	7091097887
4.	Rambaboo Singh	Executive Engineer	7763817723
			eeecritl@gmail.com
5.	Biresh Kumar	EEE,SLDC	7763814005
			Kbiresh76@gmil.com
6.	Dipak Kumar	AEE,SLDC	9472218038
			dkumar27107@gmail.com
NBPDCL	Pranav Kumar	SE(Electrical)	7763815023
			pranav7901@gmail.com
SBPDCL			
7.	P. Prasad	EEE(Com)	Purush5676@gmail.com
WBSEDCL	•		
8.	A.K. Pandey	Director (R&T)	9830403597
		,	ajay.pandey@wbsedcl.in
9.	T.K. De	Chief Engineer (PT&P)	7449300221
			cc.ptp.wbsedcl@gmail.com
WBSETCL	•		70
10.	Sabyasachi Roy	Director (Operations)	9434910015
		,	sabya 60@yahoo.co.in
11.	Mrs. Arundhati Ghosh	Chief Engineer (CPD)	9434910019
			arundhati.ghosh@wbsetcl.in
12.	D.K. Das	Addl. Chief Engineer (CTD)	9434910544
			dilip.das@wbsetcl.in
13.	Asit Karmakar	Addl. Chief Engineer(CPD)	9434910090
			asit.karmakar@wbsetcl.in
CESC	•		
14.	Sandip Pal	General Manager(SO)	9831054651
<del></del>	r		sandip.pal@rp-sg.in
15.	Rahul Chakravarty	Dy. General Manager (P-SC)	9831054619
		,	rahul.cjakravarty@rp-sg.in
DPL	1	1	
16.	M.K. Mitra	Managing Director	9434706553
- *-			md.tdpl@gmail.com
17.	Debasis Sinha	Director(Regulatory Affairs)	9434706516
±		, , , , , , , , , , , , , , , , , , ,	debasis d1@yahoo.co.in
18.	Partha Pratim Roy	General Manager(Corporate)	9434706349
		- International Components	royparp@gmail.com
GRIDCO			1 1 km k (2) Brimiti (4) iii
19.	M.K. Das	Director(Commercial)	7606000337
17,	Wi.ix. Dus	Director (Commercial)	manaskudas@yahoo.com
20.	U.N. Mishra	CGM (PP)	9437108917, 9438907774
40.	U.14. 141151114	COM (11)	/ 13/100/11, /T30/0/1/1T

Sl. No. Name S/Shri		Designation	Contact Number e-mail id		
	5/3111		sgm.pp@gridco.co.in		
OPTCL			og.mpp (og. rate i.e.)		
21.	MR. Mohanty	CGM (O&M)	9438907310 mrmohanty113@gmail.com		
22.	Nilamber Dash	CGM (SLDC)	9438908105 ele.ndash@optcl.co.in		
23.	P.S. Sahu	Chief Load Despatcher	9438907778		
24.	L. Nayak	GM (Elec)	9438907801 ele.lanayak@optcl.co.in		
ОНРС			oreman, un coopteneed.		
25.	A. K. Mishra	Director (Operation)	7328840003 aswinikmishra@gmail.com ohpc.co@gmail.com		
26.	Prakash Kumar Patra	Manager	7328840017 prakashpatra@yahoo.com		
OPGC	•				
27.	P.K. Mahapatra	DGM	9338715401 pradeep.mahapatra@opgc.co.in		
JUVNL, JUSNL,	JBVNL				
28.	Rahul Kumar Purwar	Managing Director, JBVNL			
29.	Niranjan Kumar	Managing Director, JUSNL			
30.	Atul Kumar	Director (Project), JUSNL	9431135532 dir.p.jusnl@gmail.com		
31.	Akshaya Kumar	Chief Engineer(SLDC/ULDC)	9431917973 sldcranchi@gmail.com		
32.	Ajoy Prasad	Chief Engineer(Transmission)	9431584785 ajayjseb@gmail.com		
33.	Sunil Kumar Thakur	Chief Engineer (Com & Rev)	9431708984 comml.rev@rediffmail.com		
34.	Rishi Nandan	ESE (Com & Rev).	comlrec@rediffmail.com		
TVNL					
35.	Sanatan Singh	General Manager	9031049921 sanatantvnl@gmail.com		
36.	S.K.Choudhary	ESE	9031049931 shailesh.TTPS@yahoo.co.in		
37.	R. Rajan	ESE			
38.	S.R. Singh	EEE	9431929187 shritvnl@rediffmail.com		
DVC					
39.	M. Biswas	Executive Director	9007928697 mabendra.biswas@dvc.gov.in		
40.	A. Debnath	Chief Engineer-I & I/C (System)	9831954257		
41.	B. Pan	Chief Engineer-I (SLDC)	9903247102 bpan.dvc@gmail.com		
42.	D.K. Aich	Chief Engineer-I (Comml.)	9831954303 deb.aich@dvc.gov.in		
43.	S. Bose	Chief Engineer(SPE)Kolkata	8145524994 suman.bose@dvc.gov.in		
MPL			Suman.bose@uvc.gov.m		
44.	Asok Sethi	Chairman, MPL & ED, Tata Power			
45.	K. Chandrashekar	Executive Director	7091493339 k.chandrashekar@tatapower.com		
46.	Rakesh Singh	Chief (O & M)			
NTPC					
47.	K.S. Garbyal	Regional Executive Director (ER-I)	9430288963 ksgarbyal@ntpc.co.in		
48.	K.K. Sinha	GM (Comml), CC	9650993558 kksinha02@ntpc.co.in		
49.	G.C. Mohapatra	AGM(Commercial ), ER-II	9437049372 gcmohapatra@ntpc.co.in		

CI N	1 27		
Sl. No.	Name S/Shri	Designation	Contact Number e-mail id
50.	P.R. Maharana	AGM(OS), ER-II	9437043681 prmaharana@ntpc.co.in
51.	S.D. Jha	AGM I/C(Comml), ER-I	9471004728 sdjha@ntpc.co.in
52.	S.K.Sharma	AGM(OS), ER-I	9471008359
53.	Sunit Kumar	DGM(Comml.), Ranchi	sksharma06@ntpc.co.in 7091091020
		, ,	sunitkumar@ntpc.co.in
54.	V.K.Jain	DGM(Comml.)	Vinodjain01@ntpc.co.in
55.	Faisal Ahmad	DGM(Comml.), ER-I	9470001120 faisalahmad@ntpc.co.in
56.	Vijay Gulati	Advisor to BRBCL	9650990431 vijaygulatintpc@gmail.com
POWERGRID		<b>I</b>	vija y garatim poto ginam.com
57.	D.Kumar	Executive Director ER-I	9560325444
			ed10patna@co.in
58.	Bharat Bhushan	Executive Director (ER-II)	9403777811 bbhushaner2@gmail.com
59.	N.K.Ohdar	GM(ECC) ER-II	9434740031 nkohdar@yahoo.co.in
60.	M.M. Baidya	General Manager (AM),ER-II	9434742017
00.	Wi.Wi. Balaya	General Wanager (AWI),ER-II	mmbaidya@powergridindia.com
61.	S.V.P. Selvakumar	General Manager (AM)	9873549039
	S. V.I. Servaramar	General Manager (1111)	victor@powergridindia.com
62.	A.K. Behera	DGM, Odisha	9437575638
		,	akbehera@powergridindia.com
63.	S.K. Singh	DGM(AM), ER-I	8544401030
			singhsk@powergridindia.com
64.	Ramchandra	DGM (CTU-Planning)	9910378128
			ramachand@powergridindia.com
65.	Anjan Das	Chief Manager(AM)	9434740029 anjandas@powergridindia.com
NHPC		1	J J CI
66.	Janardan Choudhary	Executive Director(O & M)	9958819003 janardan.choudhary@gmail.com
67.	Parag Saxena	Chief Engg(Comml.)	8527563777
07.	Tarag Saxena	Cinci Engg(Commi.)	parags@nhpc.nic.in
68.			
VEDANTA			
69.	J.K. Mohanty	VP (Power)	9937251432
C) (D) (D)			jk.mohanty@vedanta.co.in
GMRKEL	A1.1. D	111/0 0 340	7752020444
70.	Arabinda Pani	Head (O & M)	7752020444
71.	Pradeep Mohanty	GM(Electrical)	arabinda.pani@gmrgroup.in 7894450332
/1.	1 raucep monanty	OM(Electrical)	Pradeep.mohanty@gmrgroup.in
72.	Gyan Prakash Gupta	AGM(Powersale)	9711192639
			Gyanprakash.gupta@gmrgroup.in
Gati Infrastructure	Devajyoti Gogoi	Head- O & M	8170005692 Devajyoti.gogoi@gati.infra.com
PTC			
73.	Harish Saran	Executive Director (Marketing)	9810394429
		(1	harishsaran@ptcindia.com
TPTCL	Coming M. 1	Managina Di	0250001771
74.	Sanjeev Mehra	Managing Director	9250001771
75. 76.	Vikram Singh Rajendran M Nair	Head Marketing Head IR	9810626743 8587900961
/0.	Kajenuran Ivi Ivali	Head IX	mrajen@tatapower.com
77.	Rakesh Ranjan		Rakesh.ranjan@tatapower.com
Teesta Urja Ltd.			
78.	D.P. Bhargava	Sr. Consultant	9958833995
I		i de la companya de	

Sl. No.	Name S/Shri	Designation	Contact Number e-mail id
			dpbhargava@teestaurja.com
79.	Jaideep Lakhtakia	General Manager	9810519283
APNRL	_		
80.	Sandeep Kumar Agarwal	Manager	9873644307 sandeepkumaragarwal@adhunikgroup.co.in
CEA			
81.	B.C.Mallick	Chief Engineer (NPC)	9821766055 bikashmallik@yahoo.co.in
BHUTAN	<u> </u>		
82.	U.D. Dahal	GM(PSO), BPC	975-77101322 ujwaldahal@bpc.bt
83.	Tashi Wangchuk	Chief Technical Officer,RCO	975-17610606 tashiwangchuk@bpc.bt
84.	Shamsher Pradhan	Associate Director	975-17925623 shamsherpradhan@bpc.bt
DGPC			
85.	Rinzin Dorji	Head,EPD, O & M Department	975-17757627 r.dorji237@drukgreent.bt
DHPS			
86.	Passang	Executive Engineer	975-17592968 Pyt.doc@gmail.com
87.	Ugyen Chopel	Engineer	975-17377018 uchopel@mou.gov.bt
PRDC Pvt. Ltd.			
88.	Mrs. Debarati Basu	Head (East)	Debarati.basu@prdcinfotech.com
NLDC		<del>,</del>	
89.	G. Chakraborty	Dy. General Manager	9433041815
ERLDC	1		
90.	U.K. Verma	General Manager	8902496220 ujwalkumar.verma@gmail.com
91.	P. Mukhopadhyay	General Manager	9836542777/9869438073 pmukhopadhyay@posoco.in
92.	G. Mitra	DGM(MO)	9831297392 gopalmitra@posoco.in
93.	S. Banerjee	DGM (SS&MIS)	9433041823 surojit.banerjee@ posoco.in
94.	P.P.Chand	Dy. Mgr(GM)	9432351834 purnprakash@gmail.com
95.	Biswajit Mondal	Engineer	9903329271 biswajitmondal@gmail.com
ERPC	·		
96.	A.K. Bandyopadhyay	Member Secretary	9433068533 mserpc-power@nic.in
97.	S.P. Datta	Addl. General Manager	9433067022 dattasp@gmail.com
98.	D.K. Bauri	Executive Engineer	9883617236 eeop.erpc@gov.in
99.	P.K. De	Executive Engineer	9433125844 rpc.erpc@gov.in
100.	G. R. Jada	Executive Engineer	9547891353 ereb_cea@yahoo.com
101.	P.P. Jena	AEE	8143673051 ppjena.erpc@gov.in

### LIST OF PARTICIPANTS IN THE 35<sup>th</sup> TCC MEETING

Date: 24.02.2017 Venue: Hotel BNR Chanakya, Ranchi

Sl. No.	Name S/Shri	Designation	Contact Number e-mail id
BSPTCL	5,5222		V 2244
1.	Bhaskar Sharma	Chairperson, TCC &	9771496900
		Director (Project), BSPTCL	bsharma2407@gmail.com
2.	Ravi Shankar Prasad	EEE(P& E)	7091097887
3.	Rambaboo Singh	Executive Engineer	7763817723
	D: 1.77		eeecritl@gmail.com
4.	Biresh Kumar	EEE,SLDC	7763814005
	D: 1 I/	AFE OLD C	Kbiresh76@gmil.com
5.	Dipak Kumar	AEE,SLDC	9472218038
NBPDCL			dkumar27107@gmail.com
6.	Pranav Kumar	SE(Electrical)	7763815023
0.	Tranav Kumar	SE(Electrical)	pranav7901@gmail.com
SBPDCL			pranav 770 r(a/gman.com
7.	P. Prasad	EEE(Com)	Purush5676@gmail.com
Govt. of Sikkim			- 32 42 22 2 7 9 (2) 82 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2
8.	K.B. Kunwar	Principal Chief Engineer, Energy &	9434032924
		Power Dept.	kunwarkb@gmail.com
9.	Dinesh Kharel	Addl. Chief Engineer	7797756309
		Energy & Power Dept.	dkharel64@gmail.com
WBSEDCL			
10.	A.K. Pandey	Director (R&T)	9830403597
			ajay.pandey@wbsedcl.in
11.	T.K. De	Chief Engineer (PT&P)	7449300221
***********			cc.ptp.wbsedcl@gmail.com
WBSETCL	C 1 1: D	D: (0 (; )	9434910015
12.	Sabyasachi Roy	Director (Operations)	
13.	Mrs. Arundhati Ghosh	Chief Engineer (CPD)	sabya_60@yahoo.co.in 9434910019
13.	Wifs. Afundhati Ghosh	Chief Elighteet (CLD)	arundhati.ghosh@wbsetcl.in
14.	D.K. Das	Addl. Chief Engineer (CTD)	9434910544
1	D.R. Dus	riddi. Cilici Eligineer (C1B)	dilip.das@wbsetcl.in
15.	Asit Karmakar	Addl. Chief Engineer(CPD)	9434910090
			asit.karmakar@wbsetcl.in
CESC			
16.	Sandip Pal	General Manager(SO)	9831054651
			sandip.pal@rp-sg.in
17.	Rahul Chakravarty	Dy. General Manager (P-SC)	9831054619
DDI			rahul.cjakravarty@rp-sg.in
DPL	MIZ DE	M : D:	1 0424706552
18.	M.K. Mitra	Managing Director	9434706553
10	Dahasia Sinka	Director(Regulatory Affairs)	md.tdpl@gmail.com 9434706516
19.	Debasis Sinha	Director(Regulatory Affairs)	debasis d1@yahoo.co.in
20.	Partha Pratim Roy	General Manager(Corporate)	9434706349
40.	1 arma i ramii Roy	General Manager (Corporate)	royparp@gmail.com
GRIDCO	1		1 To J Par Pay Sman. Com
21.	M.K. Das	Director(Commercial)	7606000337
			manaskudas@yahoo.com
22.	U.N. Mishra	CGM (PP)	9437108917, 9438907774
•		- ( )	sgm.pp@gridco.co.in
OPTCL	•		
23.	MR. Mohanty	CGM (O&M)	9438907310

Sl. No.			Contact Number
	S/Shri		e-mail id
			mrmohanty113@gmail.com
24.	Nilamber Dash	CGM (SLDC)	9438908105
25.	P.S. Sahu	Chief Load Despatcher	ele.ndash@optcl.co.in 9438907778
26.	L. Nayak	GM (Elec)	9438907778
20.	L. Nayak	GW (Elec)	ele.lanayak@optcl.co.in
ОНРС			cic.iunuy uk (6)0 peri.co.iii
27.	A. K. Mishra	Director (Operation)	7328840003
			aswinikmishra@gmail.com
			ohpc.co@gmail.com
28.	Prakash Kumar Patra	Manager	7328840017
ORGG			prakashpatra@yahoo.com
OPGC 29.	D.V. Mahamatus	DGM	9338715401
29.	P.K. Mahapatra	DGM	pradeep.mahapatra@opgc.co.in
JUVNL, JUSNL, J	IRVNI		pradeep.manapatra@opge.co.m
30.	Atul Kumar	Director (Project), JUSNL	9431135532
			dir.p.jusnl@gmail.com
31.	Akshaya Kumar	Chief Engineer(SLDC), JUSNL	9431917973
	•		sldcranchi@gmail.com
32.	Ajoy Prasad	Chief Engineer(Trans.), JUSNL	9431584785
			ajayjseb@gmail.com
33.	Sunil Kumar Thakur	Chief Engineer (Com & Rev)	9431708984
2.4	Disting 4	EGE (Come & Door)	comml.rev@rediffmail.com
TVNL	Rishi Nandan	ESE (Com & Rev).	comlrec@rediffmail.com
35.	R. Sahu	Managing Director	
36.	Sanatan Singh	General Manager	9031049921
	Sundan Singi	General Manager	sanatantvnl@gmail.com
37.	S.K.Choudhary	ESE	9031049931
	, and the second		shailesh.TTPS@yahoo.co.in
38.	R. Rajan	ESE	
39.	S.R. Singh	EEE	9431929187
DUC			shritvnl@rediffmail.com
40.	M. Biswas	Europytica Dimenton	9007928697
40.	M. Biswas	Executive Director	mabendra.biswas@dvc.gov.in
41.	A. Debnath	Chief Engineer-I & I/C (System)	9831954257
71.	71. Deonath	Cinci Engineer 1 & 1/2 (System)	7031734237
42.	B. Pan	Chief Engineer-I (SLDC)	9903247102
			bpan.dvc@gmail.com
43.	D.K. Aich	Chief Engineer-I (Comml.)	9831954303
			deb.aich@dvc.gov.in
44.	S. Bose	Chief Engineer(SPE)Kolkata	8145524994
MDI			suman.bose@dvc.gov.in
MPL 45.	K. Chandrashekar	Executive Director	7091493339
43.	K. Chandrashekar	LACCULIVE DIRECTOR	k.chandrashekar@tatapower.com
46.	Rakesh Singh	Chief (O & M)	A.c.iunorusiickur (a/murpo wor.com
NTPC		1 - (	1
47.	K.S. Garbyal	Regional Executive Director (ER-I)	9430288963
	-	` ,	ksgarbyal@ntpc.co.in
48.	K.K. Sinha	GM (Comml), CC	9650993558
46	0.000	1.0240	kksinha02@ntpc.co.in
49.	G.C. Mohapatra	AGM(Commercial ), ER-II	9437049372
50.	P.R. Maharana	AGM(OS), ER-II	gcmohapatra@ntpc.co.in 9437043681
30.	F.K. Manarana	AUNI(US), ER-II	prmaharana@ntpc.co.in
51.	S.D. Jha	AGM I/C(Comml), ER-I	9471004728
J.,	5.2. viiu	110111 (Commi), Dit 1	sdjha@ntpc.co.in
52.	S.K.Sharma	AGM(OS), ER-I	9471008359
•	1		

Sl. No.	Name	Designation	Contact Number
	S/Shri		e-mail id
52	G 't W	DCMC 1) D 1:	sksharma06@ntpc.co.in
53.	Sunit Kumar	DGM(Comml.), Ranchi	7091091020 sunitkumar@ntpc.co.in
54.	V.K.Jain	DGM(Comml.)	Vinodjain01@ntpc.co.in
55.	Faisal Ahmad	DGM(Comml.), ER-I	9470001120
	T WIGHT T TITLE		faisalahmad@ntpc.co.in
56.	Vijay Gulati	Advisor to BRBCL	9650990431
			vijaygulatintpc@gmail.com
POWERGRID	24.77.01.1	CM (F.G.C) FR. H	
57.	N.K.Ohdar	GM(ECC) ER-II	9434740031
58.	M.M. Baidya	General Manager (AM),ER-II	nkohdar@yahoo.co.in 9434742017
30.	Wi.Wi. Baidya	General Manager (MM),ER 11	mmbaidya@powergridindia.com
59.	S.V.P. Selvakumar	General Manager (AM)	9873549039
		, ,	victor@powergridindia.com
60.	A.K. Behera	DGM, Odisha	9437575638
(1	C.V. Cim1	DGM(AM), ER-I	akbehera@powergridindia.com 8544401030
61.	S.K. Singh	DGM(AM), ER-I	singhsk@powergridindia.com
62.	Ramchandra	DGM (CTU-Planning)	9910378128
02.	Tumonumu	Dom (ere raming)	ramachand@powergridindia.com
63.	Anjan Das	Chief Manager(AM)	9434740029
			anjandas@powergridindia.com
NHPC	T 1 01 11	T	1,005,001,0002
64.	Janardan Choudhary	Executive Director(O & M)	9958819003
65.	Parag Saxena	Chief Engg(Comml.)	janardan.choudhary@gmail.com 8527563777
03.	I alag Saxella	Chief Eligg(Commi.)	parags@nhpc.nic.in
66.			pungeomponio
VEDANTA			
67.	J.K. Mohanty	VP (Power)	9937251432
CLEDITE			jk.mohanty@vedanta.co.in
GMRKEL 68.	Arabinda Pani	Head (O & M)	7752020444
00.	Arabinda Pani	Head (O & M)	arabinda.pani@gmrgroup.in
69.	Pradeep Mohanty	GM(Electrical)	7894450332
	Tradep Fromunty		Pradeep.mohanty@gmrgroup.in
70.	Gyan Prakash Gupta	AGM(Powersale)	9711192639
			Gyanprakash.gupta@gmrgroup.in
Gati Infrastructure	Devajyoti Gogoi	Head- O & M	8170005692
PTC			Devajyoti.gogoi@gati.infra.com
71.	Harish Saran	Executive Director (Marketing)	9810394429
71.	Turish Suruh	Executive Director (Warketing)	harishsaran@ptcindia.com
TPTCL			
72.	Vikram Singh	Head Marketing	9810626743
73.	Rajendran M Nair	Head IR	8587900961
7.4	Dalanda Danian		mrajen@tatapower.com
74. Teesta Urja Ltd.	Rakesh Ranjan		Rakesh.ranjan@tatapower.com
75.	D.P. Bhargava	Sr. Consultant	9958833995
75.	D.I. Dimguvu	SI. Consultant	dpbhargava@teestaurja.com
76.	Jaideep Lakhtakia	General Manager	9810519283
APNRL			
77.	Sandeep Kumar Agarwal	Manager	9873644307
GE 4			sandeepkumaragarwal@adhunikgroup.co.in
CEA	D.C.M.,111. 1	Objection (AIDC)	0021777055
78.	B.C.Mallick	Chief Engineer (NPC)	9821766055 bikashmallik@yahoo.co.in
BHUTAN			UIKASIIIIAIIIKWYAIIOU.CU.III
79.	U.D. Dahal	GM(PSO), BPC	975-77101322
	1		•

Sl. No.	Name S/Shri	Designation	Contact Number e-mail id
			ujwaldahal@bpc.bt
80.	Tashi Wangchuk	Chief Technical Officer,RCO	975-17610606
		,	tashiwangchuk@bpc.bt
81.	Shamsher Pradhan	Associate Director	975-17925623
			shamsherpradhan@bpc.bt
DGPC			
82.	Rinzin Dorji	Head, EPD, O & M Department	975-17757627
	, and the second		r.dorji237@drukgreent.bt
DHPS			
83.	Passang	Executive Engineer	975-17592968
			Pyt.doc@gmail.com
84.	Ugyen Chopel	Engineer	975-17377018
			uchopel@mou.gov.bt
NLDC			
85.	G. Chakraborty	Dy. General Manager	9433041815
ERLDC			
86.	U.K. Verma	General Manager	8902496220
		_	ujwalkumar.verma@gmail.com
87.	P. Mukhopadhyay	General Manager	9836542777/9869438073
			pmukhopadhyay@posoco.in
88.	G. Mitra	DGM(MO)	9831297392
			gopalmitra@posoco.in
89.	S. Banerjee	DGM (SS&MIS)	9433041823
			surojit.banerjee@ posoco.in
90.	P.P.Chand	Dy. Mgr(GM)	9432351834
			purnprakash@gmail.com
91.	Biswajit Mondal	Engineer	9903329271
			biswajitmondal@gmail.com
ERPC			
92.	A.K. Bandyopadhyay	Member Secretary	9433068533
			mserpc-power@nic.in
93.	S.P. Datta	Addl. General Manager	9433067022
			dattasp@gmail.com
94.	D.K. Bauri	Executive Engineer	9883617236
			eeop.erpc@gov.in
95.	P.K. De	Executive Engineer	9433125844
			rpc.erpc@gov.in
96.	G. R. Jada	Executive Engineer	9547891353
			ereb_cea@yahoo.com
97.	P.P. Jena	AEE	8143673051
			ppjena.erpc@gov.in

# POWER SYSTEM DOVELOPMENT FUND (PSDF)

4/3/2017

### PSDF Generation of Fund

- ❖DSM Charges
- ❖Market Splitting (Power Exchange)
- Congestion Charges
- Reactive Energy Charges
- ❖Additional Transmission Charges from STOA advance bilateral transactions.
- ❖Such other charges notified by central commission

Amount deposited in PSDF is Rs. 14477 Crores as on 31.12.2016

4/3/2017 2

### **Eligible Entity**

- Regional Power Committees
- Generating companies
- Transmission Licensees
- ❖ Distribution Licensees
- ❖Load Dispatch Centers

4/3/2017

### **Eligible Schemes**

#### The following categories of projects are eligible for funding from PSDF:

- a) Creating necessary transmission systems of strategic importance.
- b) VAR management for improvement of voltage profile in the Grid.
- c) Installation of SPS, pilot and demonstrative projects, R & U of protection systems, communication, Phasor Measurement Units (PMUs) etc.
- d) Renovation and Modernization (R&M) of transmission and distribution systems for relieving congestion.
- e) Any other scheme/project in furtherance of the above objectives, such as, conducting technical studies and capacity buildings etc.
- Projects proposed by distribution utilities in the above areas which are incidental to interstate transmission system and have a bearing on grid safety and security.
- Any scheme sanctioned by the Central Government in the interest of development of power system which requires support from PSDF as part of the scheme shall be eligible for assistance from PSDF.
- ❖ Private sector projects would not be eligible for assistance from the Fund.

### **Funding Pattern**

Sr. No.	Eligible Schemes	Eligible Grant (% of the Accepted cost)
а	Creating necessary transmission systems of strategic importance.	75 %
b	VAR management for improvement of voltage profile in the Grid.	90 %
С	Installation of SPS, pilot and demonstrative projects, R & U of protection systems, communication, Phasor Measurement Units (PMUs) etc.	90 %
d	Renovation and Modernization (R&M) of transmission and distribution systems for relieving congestion.	75%
е	Any other scheme/project in furtherance of the above objectives, such as, conducting technical studies and capacity buildings etc.	100 %
Note	Schemes from Sikkim (as hilly state) shall be eligible for grant upto 100 %.	I

4/3/2017 5

# Process of Approval of the Schemes

- Scrutiny of DPR (techno-economic appraisal) and prioritization by Appraisal Committee
  - Techno Economic Sub Group: Chaired by Member (GO & D), CEA (At least one meeting per month)
  - Appraisal Committee : Chaired by Chairperson, CEA.
     (One meeting in two months)
- Concurrence of CERC
  - For ascertaining that the scheme falls within the scope of PSDF Regulations.
     ( 15 to 60 days for concurrence)
- Monitoring Committee: Chaired by Secretary (Power), MoP.
   ( One meeting in three months)

4/3/2017 6

# All India Schemes Approved

Sr. NO.	Regions	No. of Schemes	Grant Sanctioned (Amount in Rs. Crores)
1	Northern Region	14	1332.92
2	Western Region	9	246.62
3	Southern Region	13	596.83
4	Eastern Region	9	1103.14
5	North Eastern Region	9	604.17
6	All India Schemes (PGCIL,REC)	3	3368.27
Total		57	7251.95

4/3/2017

### Eastern Region

State/UT	No. of Schemes
Bihar	3
West Bengal	2
Odisha	1
DVC	1
ERPC	1
Powergrid	1
TOTAL	9

**Total Grant Sanctioned= Rs.1103.14 Cr.** 

# Approved Schemes of Bihar

#### All figures in crores

Sl. No.	Name of Scheme	Date of Submission of Scheme	Estimated Cost	Estimated Cost Accepted	Grant Approved	Grant Released	%age of Grant Released
1	Renovation and Upgradation of protection system of substations of BSPTCL	18-09-2014	74.13	71.35	64.22 on 11.05.2015	18.68	29.09
2	Installation of capacitor bank for Improvement of Voltage profile in BSPTCL, Bihar.	9-01-2016	24.94	20.98	18.88 On 05.09.2016	0	0
	Renovation and Upgradation of the protection and control system of 132/33kV Grid Sub Station of BSPTCL	9-01-2016	63.15	54.69	49.22 02.01.2017	0	0
Total Three	Schemes		162.22	147.02	132.32		

4/3/2017

9

# Approved Schemes of West Bengal

#### All figures in crores

SI. No.	Name of Scheme	Date of Submission of Scheme	Estimated Cost	Estimated Cost Accepted	Grant Approved	Grant Released	%age of Grant Released
1	Renovation and Upgradation of protection system of substations	30-07-2014	136.45	120.67	108.6 On 21.12.2014	11.0	10.1
2	The Renovation and Modernization of 220/ 132kV STPS switch yard and implementation of Substation Automation System.	23-12-2015	28.5	26.09	23.48 On 05.09.2016	0	0
Total (Two Schemes)			164.95	146.76	132.08		

4/3/2017

10

# Approved Scheme of Odisha

#### All figures in crores

SI. No.	Name of Scheme	Date of Submission of Scheme	Estimated Cost	Estimated Cost Accepted	Grant Approved	Grant Released	%age of Grant Released
1	Renovation and Upgradation of protection system of substations of OPTCL	17-07-2014	180.56	180.56	162.5 11.05.2015	19.53	12.01
	Total (One Scheme)		180.56	180.56	162.5	19.53	12.01

4/3/2017

# Approved Scheme of **ERPC**

#### All figures in crores

SI. No.	Name of Scheme	Date of Submission of Scheme	Estimated Cost	Estimated Cost Accepted	Grant Approved	Grant Released	%age of Grant Released
1	Creation and Maintanance of Web based Protection Database Management System and Desktop based Protection Setting Calculation Tool for Eastern Regional Grid. (067)	24-09-2015	20.00	20	20 on 17.03.2016	14.54	72.7
	Total (One Scheme)		20.00	20	20	14.54	72.7

# Approved Schemes of DVC

#### All figures in crores

SI. No.	Name of Scheme	Date of Submission of Scheme	Estimated Cost	Estimated Cost Accepted	Grant Approved	Grant Released	%age of Grant Released
1	Renovation and Upgradation of control and protection system and replacement of substation Equipment of 220KV/132KV/33KV Ramgarh S/S of DVC	30-03-2016	39.87	28.85	25.96 On 02.01.2017	0	0
	Total (One Schemes)		39.87	28.85	25.96		

4/3/2017

# Approved Scheme of Powergrid for ER

#### All figures in crores

SI. No.	Name of Scheme	Date of Submission of Scheme	Estimated Cost	Estimated Cost Accepted	Grant Approved	Grant Released	%age of Grant Released
1	Installation of STATCOMs in ER at Ranchi-New, Rourkela, Kishanganj and Jeypore substation of POWERGRID	05-06-2015	1059.49	700.31	630.28 On 05.01.2016	0	0
	Total (One Scheme)		1059.49	700.31	630.28	0	0

The entities may furnish information on the status of implementation of the schemes (physical as well as financial progress) in the prescribed format by first week of every month on regular basis to Member Convener, PSDF Project Monitoring Group (AGM, NLDC, POSOCO) with a copy to NPC Division.

il. No.	WBPDCL West Bengal DVC ERPC ERPC ERPC WBSETCL West Bengal WBSETCL	Name of the scheme	Estimate d cost (Rs crore)	Techno- Economic Subgroup Meeting	Remarks
		Implementation of islanding scheme at Bandel thermal power station	1.54	AC recommended	CERC concurrence awaited
2	DVC	R & U of the protection and control system	156.11	AC recommended	CERC concurrence awaited
	ERPC	Training Program for Power System Engineers of various constituents of Eastern Region	1.01	28 <sup>th</sup> -14.12.16	Input sought
	ERPC	Study programmes on power market trading at NORD POOL Academy for Power System Engineers of Eastern Regional Constituents	6.20	28 <sup>th</sup> -14.12.16	Input sought
	ERPC	Study programme on the Integration of Renewables Energy Resources into the Grid	5.20	28 <sup>th</sup> -14.12.16	kept in abeyance
		Scheme of WBSETCL for improving state transmission system by reactive power management	48.45	28 <sup>th</sup> -14.12.16	Input sought
	WBSETCL West Bengal	Improvement of State Transmission System by Renovation & Modernisation of Transmission System for relieving congestion in intra-state transmission system by capacity enhancement of existing network with an object to improve security, reliability and voltage profile in the State Grid.	72.65	22 <sup>nd</sup> -05.07.2016	Input sought
3	OHPCL Odhisá2017	Renovation and Upgradation of protection and control system of OHPC	38.93	26 <sup>th</sup> -28.09.16	Input sought


### **Observations**


- ❖No schemes from Jharkhand and Sikkim.
- ❖No Schemes for Reliable communication based on OPGW from ER.

The schemes are to be submitted to nodal agency as soon as possible.


4/3/2017


# Thank You




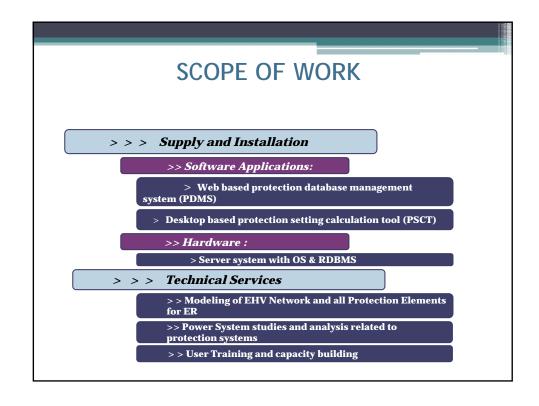





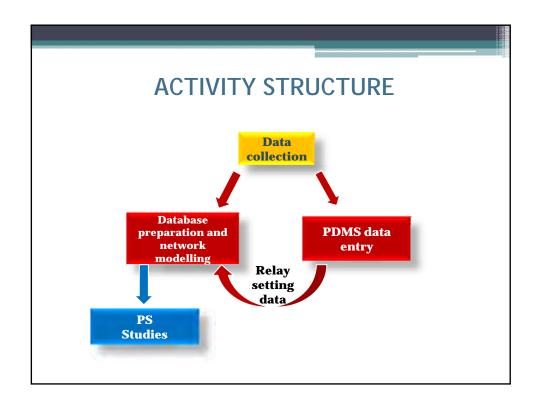

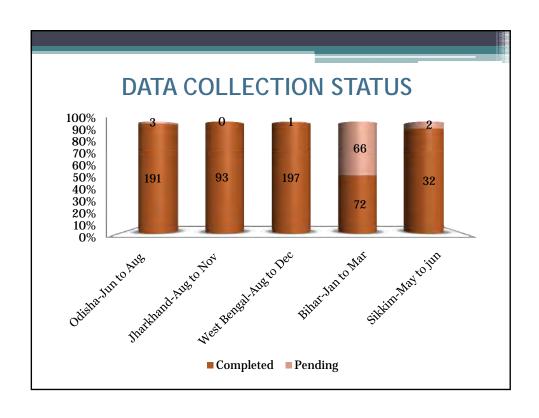

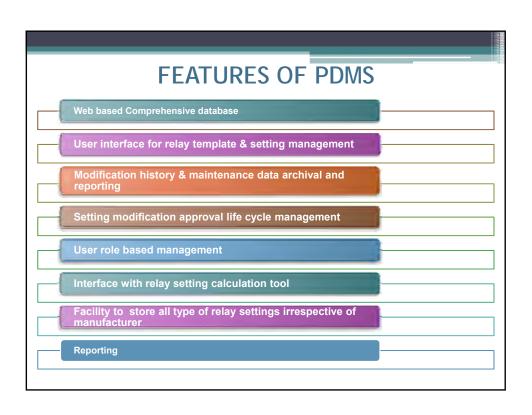

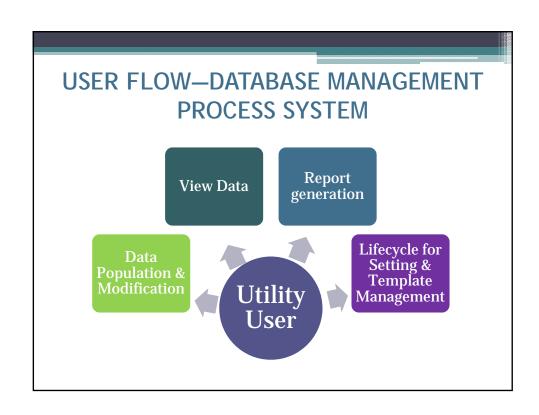



### Revised List of Sub-Stations to be connected with Fibre Optic in Bihar

Sr. No.	Name of Sub-station	IRV Level	Illink/Name	Integration with existing equipment	Length from nearest WB mode((in Kms))	Rematiks	S4.1	L4.1	L4.2	upto 150kms	Base Equipmen
11	Balmikinagar	132	Ramnagar-Balmikinagar	Ramnagar	778		0	0	1	0	
2	Ramnagar	1132/33			OPGW layiny considered under BSPTCL Package		0	I	1	0	1
33	Dhaka	1132/33	Motihari-Dhaka	Motihari	225		2	2	1	0	1+1
4	Sitamarhi	1132/33	Sítamarhi-Dhaka		52		0	2	1	0	
55	Ekma	1132/33	Siwan-Ekma	Siwan	11	Upto LILO of Chhapra-Siwan	1	0	0	0	
6	Dalsinghsarai	1132/33	Samastipur-Dalsingsarai	Samastipur	223		1	0	0	0	
77	Samastipur*	1132/33			OPGW layiny considered under BSPTCL Package		1	1	0	0	
88	Khagaria	1132/333	BTPS-Khagaria	BTPS	60		1	0	1	1	
99	BTPS*	220/132/33			OPGW layiny considered under HSPICL Package		0	0	1	11	
		1	khagaria-purnia		150		0	0	0	1	
10	Ekansarai	1132/33	Biharshariff-Ekansarai	Biharshariff	330		1	1	0	0	
111	Biharsharif*	2220/132/333			OPGW layiny considered under BSPTCL Package		3	12	0	0	11-61
112	Hulasganj	1132/333	Ekansarai-Hulasganj		115		1	0	0	0	
113	Sheikhpura	132/33	Blharshariff-Sheikhpura		220	station planned on new line under BGCL	1	1	1	0	
114	Jamui	132/333	Seikhpura-Jamui		55		0	2	1	0	
12.7	3411161	31221323	Jamui-Lakhisarai	Lakhisarai	35						
115	Lakhisarai	1132/333			OPGW layiny considered under BSPTCL Package		0	1	0	0	
16	Baripahadi	132/33	Biharshariff-Baripahadi				1	1	0	0	
117	Rajgir	1132/333	Nalanda-Rajgir	Nalanda	14		1	0	0	0	
118	Nalanda	1132/333			OPGW layiny considered under BSPTCL Package	M.	1	0	0	0	
119	Belagani	1132/33	Chandauti-Belaganj	Chandauti	220		1	0	0	0	
220	Chandauti	1132/333			OPGW layiny considered under BSPTCL Package		2	2	0	0	11+11
221	Rafiganj	1132/33	Chandauti-Rafigani		441		0	1	0	0	
22	Tekari	132/33	Chandauti-Tekari		29		1	1		0	
23	Goh	132/33	Tekari-Goh		222		1	0	0	0	
24	Vaishali	132/33//11	Muzaffarpur-Vaishali	Muzaffarpur	30		0	2	0	0	
225	Muzaffarpur	1132/333			OPGW layiny considered under BSPTCL Package		1	1	0	0	
26	Supaul	132/33	Madhepura-Supaul	Madhepura	330		0	4	0	0	1+1
227	Madhepura	2220 1132/33			OPGW layiny considered under BSPTCL Package		0		0	0	
28	Phulparas	1132/33	Supaul-Phulparas		32		1			0	1+1

29	Masrakh	132/33	Gopalganj-Masrakh	Gopalganj	40	Upto LILO of Gopalganj-Siwan	1	2	0	0	
30	Gopalgunj	220/132/ 33	153	P. delance	Already considered under BSPTCL Package		2	pane	1	0	1+1
31	Siwan	132/33			OPGW layiny considered under BSPTCL Package		1	2	1	0	1+1
			siwan-Chhapra		70					a line	
32	Mohania	132/33	Pusauli(BSEB)-Mohania	Pusauli(BSEB)	10		2	0	0	0	
33	Pusauli(BSEB)	220/132			OPGW llayiny considered under BSPTCL Package		2	2	1	0	1+1
34	Jainagar	132/33	Madhubani-Jainagar	Madhubani	40		0	2	2	0	
			Jainagar-Phulparas		55		0	0	0	0	
35	Madhubani	132/33			OPGW layiny considered under BSPTCL Package		0	2	0	0	
36	Dumraon	132/33	Ara(PG)-Dumraon	Ara(PG)	60		1	2	1	0	1+1
			Dumraon-Bikramganj		35		0	0	0	0	
37	Ara(PG)*	220/132	Ara(PG)-Khagaul		56		0	1	2	0	
38	Khagual	220/132/ 33			OPGW layiny considered under BSPTCL Package		2	0	1	0	
39	Buxar	132/33	Dumraon-Buxar		17		1	0	0	0	
40	Jagdishpur	132/11	Ara(PG)-Jagdishpur		27		0	1	0	0	
41	Digha	132/33	Khagaul-Digha	Khagaul	16		1	0	0	0	
42	Bikramganj	132/33	Dehri-Bikramganj	Dehri	45		0	2	1	0	
43	Dehri	220/132/33			OPGW layiny considered under BSPTCL Package		1	4	0	1	1+1
44	Banjari	132/33	Dehri-Banjari		38		0	1	0	0	
45	Sherghati	132/33	Bodhgaya-Sherghati	Bodhgaya	27		0	2	0	0	
46	Bodhgaya*	220/132/ 33			OPGW layiny considered under BSPTCL Package		0	2	0	1	
			Dehri-Gaya(PG)-Bodhgaya		95		0	0	0	0	
47	Wazirganj	132/33	Bodhgaya - Wazirganj		30		0	2	0	0	
48	Nawada	132/33	Wazirganj - Nawada		26		0	2	0	0	
			Nawada-Biharsharif		41		0	0	0	0	
49	Kishanganj	132/33	Forbisganj-Kishanganj	Forbisganj	70		1	1	2	0	1+1
			Katayia-Forbisganj		50		0	0	0	0	
50	Kataiya (Birpur)	132/33	Supaul- Kataiya		40		0	1	1	0	
51	Katihar	132/33	Purnea-Katihar	Pumea	29	- W W W	1	1	0	0	101
52	Purnea	132/33	2		OPGW layiny considered under BSPTCL Package		2	4	2	2	1+1+1
53	Forbishganj	132/33	Purnea-Forbishganj		85		1	1	3	0	1+1
54	Mithapur	132/33	Sipara-Mithapur	Sipara	16	station planned on new line under BGCL	2	0	0	0	
55	Sipara	220/132/ 33			OPGW layiny considered under BSPTCL Package		3	0	1	0	1+1
56	Jakkanpur		Jakkanpur-Sipara		10		1	0	0	0	
		122/22				station planned on new line under		17.			
57	Bihta	132/33	Khagaul-Bihta		15	BGCL	2	0	0	0	

58	Naugachia	132/33	Purnia-Naugachia		70	- 0	0	1	1	1	
			Naugachhia-BTPS	BTPS	136		0	0	0	0	
59	Karamnasa	132/33	Mohania-Karamnasa		11		1	0	1	0	
			Karamnasa-Pusauli(BH)	Pusauli(BH)	60	Trans.Line through Kudra TSS	0	0	0	0	
60	Harnaut	132/33	Baripahadi-Harnaut		26		0	1	0	0	
61	Karpi (Ataula)	132/33	Jehanabad - Ataula		28		0	1	0	0	
62	Jehanabad	132/33				considered under ULDC scheme	0	2	0	0	
63	Raxaul	132/33	Bettia - Raxaul		38		0	1	1	0	
64	Bettiah	132/33			OPGW layiny considered under BSPTCL Package		0	5	1	0	1+1
			Bettiah-Gopalganj		60		0	0	0	0	
65	Imamganj	132/33	Imamganj - Sherghati		30		0	1	0	0	
66	Tehta	132/ 33	132 KV Chandauti/ Jehanabad LILO- Tehta		6		2	0	0	0	
67	Udakishanganj	132/33	Saharsa - UdaKishanganj	Saharsa	51		0	0	1	0	
68	Saharasa	132/33			OPGW layiny considered under BSPTCL Package		0	1	2	0	
69	Karbigahiya	132/33	Karbigahia-Mithapur		3	Arial/UG fibre required as line is underground	1	0	0	0	
70	Kochas	132/33	Kudra - Kochas		35		1	2	0	0	
			Dumraon-Dehri LILO Kochas		29	Distance b/w LILO point to Kochas gss is 29km	0	0	0	0	
71	Kudra GSS	132/33	Kudra-Dehri		26		1	2	0	0	
			Kudra-Pusauli(PG)		10		0	0	0	0	
72	Pusauli(PG)*				OPGW layiny considered under BSPTCL Package		1	0	0	0	
73	Shekhpura	132/33	Hathidah - Shekhpura	Hathidah	28		0	1	0	0	
74	Hathidah	132/33			OPGW layiny considered under BSPTCL Package		0	1	0	0	
75	Jandaha	132/33	Samastipur/Hazipur LILO Jandaha		35		1	2	0	0	
76	Hajipur*	132/33			OPGW layiny considered under BSPTCL Package		0	1	0	0	
77	MTPS*	220/ 132/ 33			OPGW layiny considered under BSPTCL Package		0	0	0	0	
78	Sitalpur	132/33	Sitalpur-Vaishali		31		0	2	0	0	
79	Chhapra	132/33	Chhapra-Sitalpur		40	Parameter and the second	0	1	2	0	
80	Begusarai	220/ 132/ 33			OPGW layiny considered under BSPTCL Package		2	3	0	0	1+1
81	Kahalgaon(NTPC)*	Ŀ			OPGW layiny considered under BSPTCL Package		0	0	0	0	
82	Kahalgaon	132/33			Already considered under BSPTCL Package		0	1	0	0	
83	Sabour .	132/33			OPGW layiny considered under BSPTCL Package		1	1	0	0	
	1	1	Kahalgaon-sabour		25		0	0	0	0	
84	Fatua	220/132/33	ixanaigavii-saooui		OPGW layiny considered under BSPTCL Package		0	0	0		

	The second second second								
Ara(Bihar)	132/33			OPGW layiny considered					. ,
,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	102,00				0	0	0	0	
Sultanguni	132/33					1			
					1	1	0	0	
Jamalpur	132/33								
	1				0	1	0	10	1
Lakhisarai(PG)*	132/33					10	0	10	
	-			OPGW Inviny considered		10	0	10	-
Sonenagar	132/33				10	0	0	0	
Sasaram(BSEB)	132/33	Sasaram-Dehri	Dehri		2	0	0		-
305014111(2002)					0	0	0	0	
	100.00								
SKMCH	132/33				1	1	0	0	
		SKMCH-Muzaffarpur		15	0	0	0	0	
Runisaidpur	132	Runisaidpur-SKMCH	SKMCH	35	0	1	0	0	
Darbhanga	220/132/33			OPGW layiny considered					
Darbhanga	220/132/ 33			under BSPTCL Package	0	0	0	0	
Gangwara	132/33			OPGW layiny considered					
Gangwara	132/ 33				0	0	0	0	
Pandaul	132/33								
	132/33			under BSPTCL Package	0	0	0	0	
Purnea(PG)*		Purnea(PG)-Purnea(BH)	Purnea(BH)	2	1	0	0	0	
Motihari	132/33								
						0		0	
Barh	132/33	Barh-Biharsharif			1	0	0	0	
Barh(NTPC)*								0	1
					0	0	0	0	
Banka	132/33				0	2	0	0	
	-				U	12	- 0	10	
Banka(PG)*					0	0	0	0	
					10	10			+
				2/03	37	34	22	6	-
			on gss to be con			,			
Motihari new	400/132				1	1			
						0	_		
	100/00				· · · · · · · · · · · · · · · · · · ·	0		-	
	132/33			35	0	1		0	-
	220/122/22			1	1	0		0	-
Bihta new	220/132/33				1	-	_	-	-
101	220/122/22				0	0		10	-
					1	0		1	-
						0		0	-
						0			
Waisali Ganj	132/33				0	1	10	0	-
	Lakhisarai(PG)*  Sonenagar  Sasaram(BSEB)  SKMCH  Runisaidpur  Darbhanga  Gangwara  Pandaul  Purnea(PG)*  Motihari  Barh  Barh(NTPC)*  Banka	Sultangunj         132/33           Jamalpur         132/33           Lakhisarai(PG)*         132/33           Sonenagar         132/33           Sasaram(BSEB)         132/33           SKMCH         132/33           Runisaidpur         132           Darbhanga         220/132/33           Gangwara         132/33           Pandaul         132/33           Purnea(PG)*         132/33           Barh         132/33           Barh(NTPC)*         132/33           Banka         132/33           Banka(PG)*         220/132/33           Chagaria new         220/132/33           Sheohar         132/33           Waisali Ganj         132/33	Sultangunj	Sultanguni	Sultanguri	Sultangun	Marginari	Sultangung   132/33	Soltangunj   132/33

30

132/33

jamiu old- jamui new

Jamui new

	•		Jamui new- banka new	35	0	0	0	0
10	Banka new	132/33	Bamka old Banka new	30	0	1	0	0
			Chhapra old/ chhapra new lilo siwan		11 6		- 1	
11	Siwan new	132/33	new	5	0	1	1	0
12	Nathnagar	132/33	Sabour-Sultanganj LILO Nathnagar	10	1	1	0	0
13	Korha	132/33	Purnea-Naugachhia LILO Korha	20	0	1	1	0
14	Piro	132/33	Piro - Bikramganj	23	1	0	0	0
15	bhabua	132/33	Bhabuba-Pusauli new	33	0	1	0	0
16	Tarapur	132/33	Jamalpur/ Sultanganj lilo tarapur	16	1	1	0	0
17	Manihari	132/33	Purnia/ Katihar lilo Manihari	12	1	1	0	0
18	Barsoi	132/33	Barsoi- Kisanganj new	70	0	0	1	0
19	Dhamdaha	132/33	Purnia/Saharsa lilo Dhamdaha	1	1	1	0	0
20	Baisi	132/33	Kisanganj old-Baisi	1	1	0	0	0
21	Nirmali	132/33	Phulpras/Supaul lilo- Nirmali	15	1	1	0	0
22	Trivaniganj	132/33	Purnia/ Forbisganj lilo Trivaniganj	15	1	1	0	0
23	Shahpurpatori	132/33	Shahpurpatori- Samastipur new	31	0	1	0	0
24	Samastipur New	220/132/33			0	1	0	0
			D 100 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1					
25	Rosera	132/33	Begusarai/Kusheshwarasthan lilo Rosra	9	1	1	0	0
26	Kusheshwarsthan	132/33			0	1	0	0
27	Simri Bhatiyarpur	132/33	Simri Bhatiyarpur- Sonebarsa	16	1	0	0	0
28	Sonebarsa	132/33			1	0	0	0
29	Jhanjharpur	132/33	Jainagar/Phulparas lilo Jhanjharpur	35	0	2	0	0
30	Benipatti	132/33	Madhubani/Jainagar LILO Benipatti	12	2	1	0	0
31	Pupri	132/33	Pupri - Benipatti	32	0	1	0	0
32	Belsand	132/33	Dhaka/Sitamarhi LILO Belsand	9	0	2	0	0
33	Maharajganj	132/33	Maharajganj-Mashrakh	20	1	0	0	0
34	Hathua	132/33	Gopalganj/Siwan LILO Hathua	8	1	1	0	0
35	Pakridayal	132/33	Pakridayal-Dhaka	20	- 1	0	0	0
36	Areraj	132/33	Gopalganj/Bettia LILO Areraj	15 .	1	1	0	0
37	Chakia	132/33	Chakia-Motipur new	40	0	1	0	0
38	Motipur New	220/132			0	1	0	0
39	Narkatiyaganj	132/33	Bettia/Ramnagar LILO Narkatiyaganj	15	0	2	0	0
40	Banmankhi	132/33	purnia/Saharsa LILO Banmankhi	2	1	0	1	0
41	Mahanr	132/33	Mahnar-Jandaha	10	1	0	0	0
42	Bakhari	132/33	Bakhari-Begusarai	20	1	1	0	0
43	Balia	132/33	Begusarai/Bakhari LILO Balia	11	1	2	0	0
44	Manjhaul	132/33	Begusarai/Bakhari LILO Manjhaul	2	2	0	0	0
45	Teghra	132/33	Begusarai-Teghra	40	0	1	0	0
46	Araria	132/33	Kishanganj old/Forbisganj LILO Araria	1	0	2	0	0
10	Total	1000	L and	944		9 2	9	4 1
	Total		Total	2703+944=3647			,	<del>-</del> 1

List of sub-stations and Lines Deleted(already considered in Transmission/ULDC scheme of BSPTCL)

2	Masaudi	132/33	Jehanabad-Masaudi	30	considered under ULDC scheme	0	1	0	0
3	Sonebarsa		Madhepura-Sonebarsa	50	considered under ULDC scheme	0	0	1	0
4	Kusheshwarsthan	132/33	Sonebarsa - Kusheshwarsthan	75	considered under Tr. scheme	0	0	1	0
5	Hajipur 132kV	132/33	Hazipur (220KV)-Hazipur (132KV)	2	considered under ULDC scheme	1	0	0	0
_			Sipara-Masaurhi	24	considered under ULDC scheme	1			
-			Sipara-Khagaul	8	considered under ULDC scheme	1			
-			Banka-Banka(PG)-sabour	25	considered under ULDC scheme		1		
			Dehri-Sonenagar	30	considered under ULDC scheme		11		
			Muzaffarpur-Vaishali	30	already considered at sr no. 18		1		
				274					

274



ଓଡ଼ିଶା ओडिशा ODISHA

Jagyneswal of India
Notary Sovt. of India
Jaisha, BBSK, Dist-Khuris AA 975014
Regd No 9861006177

BEFORE THE NOTARY, BHUBANESWAR, ODISHA

#### **AFFIDAVIT**

I, Sri Jayakrushna Mohanty aged about 55 years, son of Sri Dambarudhar Mohanty, resident of S 3 Vedanta Meadows, Jharsuguda-768202, working as Vice President-Power at Vedanta Limited (formerly known as Sesa Sterlite Limited) at Jharsuguda unit having registered office at Sesa Ghor 20 EDC Complex, Patto, Panjim, Goa - 403001 do hereby affirm as under:

 That I am duly authorized to sign affidavits, agreements, letters, representations etc. vide power of attorney dated 16<sup>th</sup> July 2016 for and on behalf of the company.

That the ERPC board has discussed and reviewed the construction of dedicated WKVD/C transmission line to the PGCIL pooling station in the meeting held on



Bakak

25-11-16 21886 P.C. MOHANTY STAMP VENDER BHUBANESWAFTIOURT

Notary 30vt. of India
Notary 30vt. of India
Odisha, BBSK, Dist-Khurd
7791/2009
Regd No

19<sup>th</sup> November 2016 at Kolkata. Based on our prayer, LERPC board took the decision to allow for physical completion of the project by end of February 2017. The necessary statutory clearances for charging shall be obtained post completion of the physical activities. The status will be reviewed in March 2017 / next TCC meeting. Accordingly a fresh undertaking has to be submitted to CTU and ERPC in the form of affidavit.

- That I being the authorized signatory of the company do hereby inform that the above work is under execution and is being continuously monitored at our end on day to day basis.
- 4. That we are putting our best efforts for completion of the transmission line as per the revised schedule furnished before the ERPC board and would be able to physically complete the said work by 28<sup>th</sup> February 2017.
- 5. Hence this affidavit.

DEPONENT

#### **VERIFICATION:**

I, Jayakrushna Mohanty, the deponent named above do hereby verify that the contents of the above affidavit are true to the best of my knowledge and belief and are based on records.

Verified at Bhubaneswar on this the the day of December 2016.

DENTIFIED BY MA

NO 14 PO AGEORGIA DE LA CONTROL DE LA CONTR

Jagyneswar Acnarya
Netary Jovi of India
Netary Jovi of India
Jdisha, BB6R, Bist-Khuro
779112009
Regd No 779112009

Annexure- B9

## The detailed scope of work for conversion of 220 kV Tenughat-Biharsarif Line at 400 kV level

Site		Agreement Details	LOA details	Completion	Scope of Work	Reason for Delay
Tenughat	S/s	Date of Agreement:	M/s Sterling &	Scheduled	Original Scope: 5 Nos. Bays, (TB, BC,	Very irregular and delayed
(TVNL)		29.07.2010	Wilson, Kolkata	Completion:	ICT-1, ICt-2, Line & L/R).	payment from TVNL forcing
		Completion Time: 36	LOA Date:	30.06.2013		agency to demobilized/mobilized
ĺ	j	Months	25.04.2012		Additional Scope: Erection, Testing &	frequently . Still 4.07 Crore is
		(i.e. 28.07.2013)		Anticipated	Commissioning of OSM Equipments	pending (Other issues as per
		Estimated Cost: 24.20	LOA Value:	Completion:	(i.e. 2 x 250 MVA ICTs, 50 MVAR L/R).	annexure-B).
		Crore (incl. Consultancy	20.184 Crore.	30.06.2017	-	
		@ 15% + Service Tax)				
Biharsharif	S/s	Date of Agreement:	M/s Sterling &	Scheduled	Original Scope: 1 No. Bay & 0.81 km	Very irregular and delayed
(PG)	&	24.08.2008	Wilson, Kolkata	Completion:	400 kV T/L for Termination at	payment from JUSNL forcing
associated T	/L	Completion Time: 24		24.08.2010	Biharsharif S/s end.	agency to demobilized/mobilized
1		Months	LOA Value: 3.57		ļ <sub>i</sub>	frequently. The said job is on cost
		(i.e. 24.08.2010)	Crore.	Anticipated	į.	plus basis. The bay work is nearly
		7.13 Crore + Consultancy		Completion:		under completion stage and line
		@ 15% + Service Tax.		15.04.2017		diversion work is likely to be
 						completed by 15.04.2017 subject
						to release of balance payment of
	ļ				\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\	48.5 lakh.

## Tenughat end(TVNL)

## **TVNL Consultancy Project, TTPS**

Contractor

: M/s Sterling & Wilson, Kolkata

**LOA Date** 

: 25.04.2012

Sch Completion

30.06.2013

Ant Completion

31.06.2017

**LOA Value** 

: Rs. 20.184 Crores (Supply= Rs. 13.187 Crs; Services=7.006 Crs) as per last Amnd dtd 16/12/15 +

Consultancy fee(@15%) + Service Tax(@ 15%).

SCOPE

: 1) No of Bays : 05 (TB, BC, ICT-1, ICT-2, Line/LR) .

2) New scope: Erection, Testing, commissioning of OSM, i.e., 2x250 MVA ICTs and 50 MVAR Line

Reactor (OSM: ICT-1 .. OLD, ICT-2 .. NEW, LINE REACTOR .. OLD).

#### **MAJOR CONSTRAINTS:**

1. <u>FUND</u>: Delay in release of balance fund by TVNL for Rs 5.85 Crs (approx) against our Invoice dated 24.12.15. TVNL released 1.78 Crores only in the last week of Dec'16.

- 2. ERECTION OF ICT-2 (NEW): M/s S&W deputed erection engineer to site on 14.01.17 and erection gang is due to reach site by next week. BHEL engineer yet to be deputed to site by TVNL for supervision of erection & commissioning.
- ERECTION OF OLD OSMs (ICT-1 & LR): Test Report for Healthiness submitted to TVNL on 22/02/16. Clearance from TVNL still awaited. TVNL to take up the matter with BHEL and revert back.
- 4. <u>BALANCE SUPPLIES</u>: Balance supplies to site halted due to non-issuance of way bill & C-Form by TVNL despite repeated follow-up since last 2-years. <u>M/s S&W again started supplies with their own road permit since</u> 08/08/16. C-Forms for FY 2012 to 2016 not yet issued to M/s S&W.

#### PROGRESS OF WORK:

As on 14/01/17

SL	DESCRIPTION	TOTAL	FDN DONE	EQPT EREC	BALANCE EQPT ERECTION	REMARKS
1	BAY-1 (BUS TRANSFER)	40	40	37	CB=3 poles only	CB steps competed.
	BAY-2 (BUS COUPLER)	28	28	28	-	
	BAY-3 (ICT-1 OLD)	44	44	44		
	BAY-5 (ICT-2 NEW)	50	50	47	220 LA=3	220KV LA to be erected
	BAY-13 (LINE BAY, LR)	61	61	60	••	after erection of ICT-2.
2	CABLE TRENCH (Sec: 2-2, 3-3, 4-4)	100%	100%			Cable laying in progress.
3	STRINGING (MOOSE)	100%		98%		
	BUS BAR	100%		98%		
4	EARTHMAT	100%		100%	la and a	
	FLAT EARTHING	100%		93%		
5	ICT-2 (NEW)	1	100%			Erection gang to reach site by next week; deputation of BHEL engr at site not yet confirmed by TVNL.
	ICT-1 & LR (OLD)	1+1	100%			As per TVNL: BHEL engr at site to give advice on Test Report for Healthiness of the old eqpts.

## Eastern Regional Power Committee, Kolkata

# Minutes of Special Meeting on "High voltage issues in Eastern Region" held on 22<sup>nd</sup> December, 2016 at ERPC, Kolkata

List of participants is at **Annexure-A.** Member Secretary, ERPC welcomed all the participants to the special meeting and informed that this meeting was called on short notice to address the high voltage issues in Eastern Region particularly in West Bengal and Odisha. He expressed concern on the high voltage conditions being experienced at some pockets of E. Region, during off-peak hours, since onset of winter season.

It was informed that Subhasgram 400kV, Jeerat 400kV, Arambag 400kV, Kharagpur 400kV and Meramundali 400kV sub-stations are facing acute high voltage problem. The voltage profile of these and some other S/S recorded by ERLDC SCADA system for the month of November 2016, were presented before the house. It was felt in general that drastic reduction of off-peak demand in W. Bengal and Odisha had aggravated the high voltage problem.

Representative of OPTCL informed that voltage of Meramundali 400kV S/Stn mostly remains well above 412kV during off-peak period. Flow of huge reactive power from Meramundali S/Stn to Angul(PG) 400kV S/S over Meramundali-Angul D/C line is making GRIDCO liable for payment of huge charges in ER Reactive Pool account, every week. ERLDC observed that during most of the day, reactive power flows from 400kV N. Duburi to Meramundali S/Stn of OPTCL. Further, efforts should be made to export VAR from 400kV to 220kV system of Odisha by changing the tap of Meramundali 400/220kV ICT. However, OPTCL informed that high voltage condition is existing in their 220kV system also.

After further deliberations, it was decided that OPTCL would ensure absorption of maximum possible reactive power (as per capability curve) by the units of JSPL, Vedanta and GMR(Odisha). In addition, one circuit of 400kV Meramundali-N. Duburi line is to be switched off (from both ends) in night lean hours on trial basis, and the effect on Meramundali voltage is to be monitored by ERLDC. 50MVAR line reactor at Meramundali end of Vedanta-Meramundali-I 400kV circuit is presently under outage. OPTCL should therefore endeavor to restore this reactor at the earliest.

CESC and HEL representatives informed that one unit of 2X600MW HEL TPS was scheduled to be taken under shutdown from 24-12-16, for planned maintenance. The voltage of Subhasgram 400kV exceeded 430kV on regular basis even after absorption of around 80 MVAR by each of

the units. On 15-12-16, around 112-113 MVAR was absorbed by one unit on experimental basis, keeping the other unit at unity p.f. Since it is not possible to absorb further reactive power, they had proposed raising the setting of Stg-I over-voltage protection of HEL-Subhasgram D/C line at Subhasgram end as follows, to prevent tripping of the line on high voltage:

400kV HEL-Subhasgram-I 112% with 7 sec delay 400kV HEL-Subhasgram-II 111% with 3 sec delay

ERLDC suggested that to control Subhasgram and Jeerat 400kV voltages, apart from HEL units, reactive power should also be absorbed by Sagardighi, Kolaghat and Bakreswar units, as per their respective capabilities. Possibility of opening one or two lightly loaded 220kV lines connected to Subhasgram(PG) may also be explored.


WBSETCL informed that one circuit each of 220kV Jeerat-N. Town and Jeerat-Kasba lines are being switched off during night off-peak hours on regular basis. As such, it is not advisable to open any 220kV line from Subhasgram(PG). CESC apprised that 220kV Subhasgram(PG)-EMSS D/C line feeds essential and critical loads of Kolkata. On reliability considerations it is not advisable to open one circuit of this line. One no. 125MVAR shunt reactor is already planned to be installed at Subhasgram, but as the same would take around 18 months to be ready, the present problem would not be addressed. WBSETCL requested to switch off one circuit each of Chaibasa-Kharagpur and Sagardighi-Durgapur(PG) 400kV D/C lines, during off-peak hours, in order to control high voltages at Kharagpur and Aramabag.


ERLDC pointed out that it has already been observed in real time that opening 400kV Chaibasa-Kharagpur line has very little effect in reducing Arambag voltage. However, it would help in reducing voltage of Kharagpur. After further discussions it was decided that one circuit each of 400kV Kharagpur-Chaibasa and Sagardighi-Durgapur(PG) would be opened during night hours on experimental basis. However, at the same time, units at Kolaghat, Bakreswar, Sagardighi and Farakka should absorb reactive power upto their respective capability limits.

The meeting concluded with a vote of thanks to the chair.


\*\*\*\*\*

## **ICCP FLOW OF WEST BENGAL**

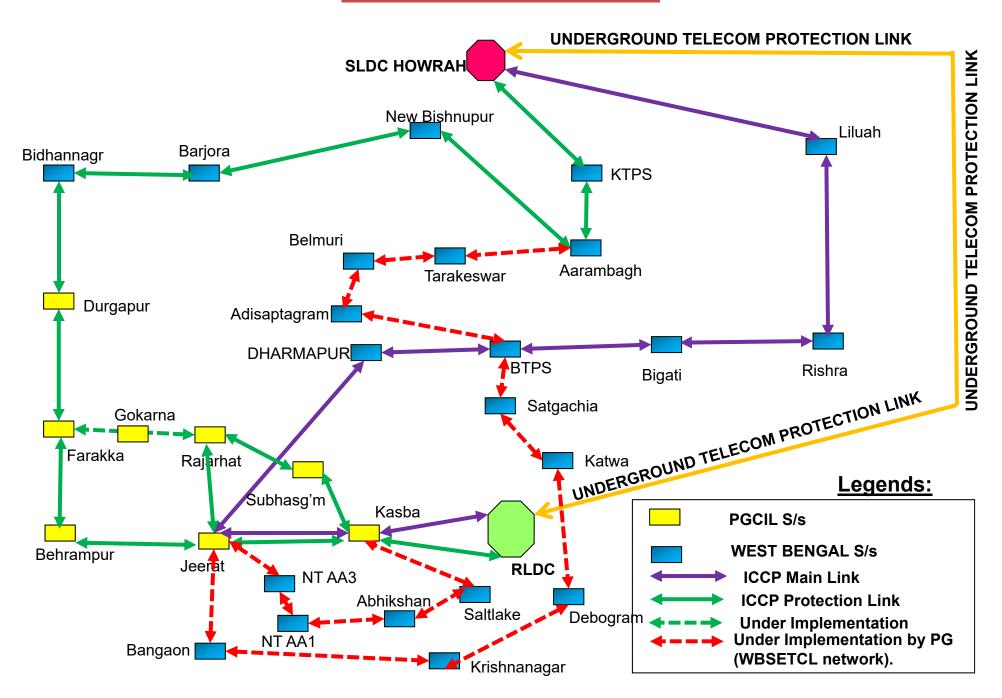

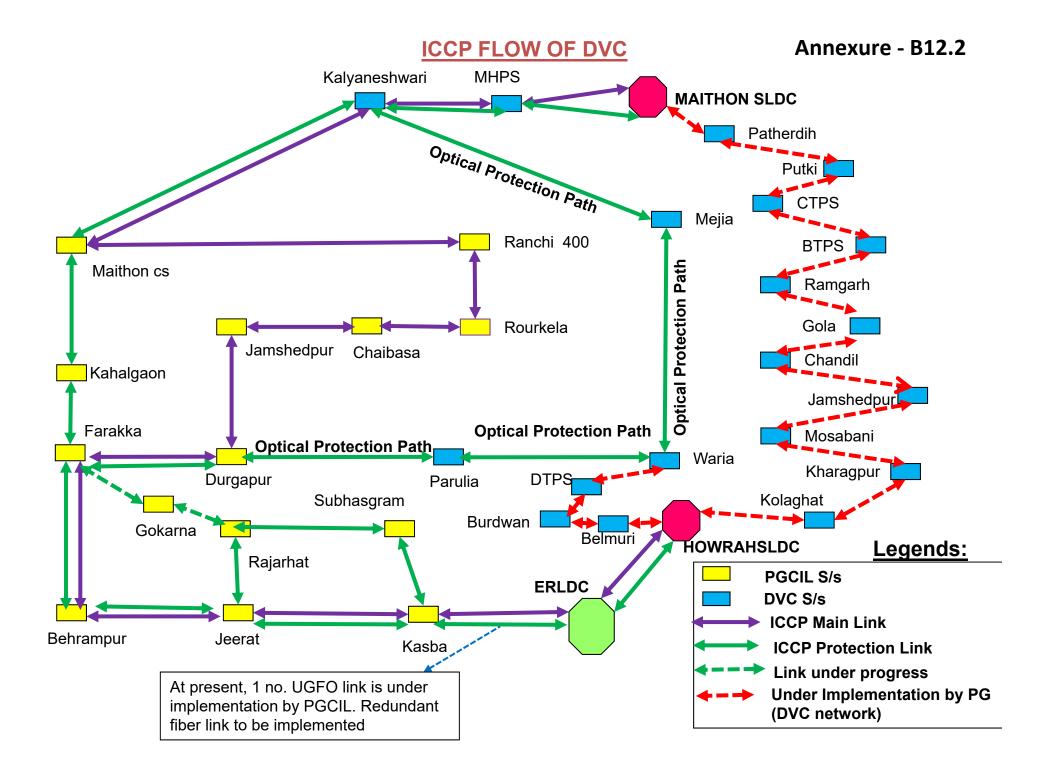


## **ICCP FLOW OF OPTCL**

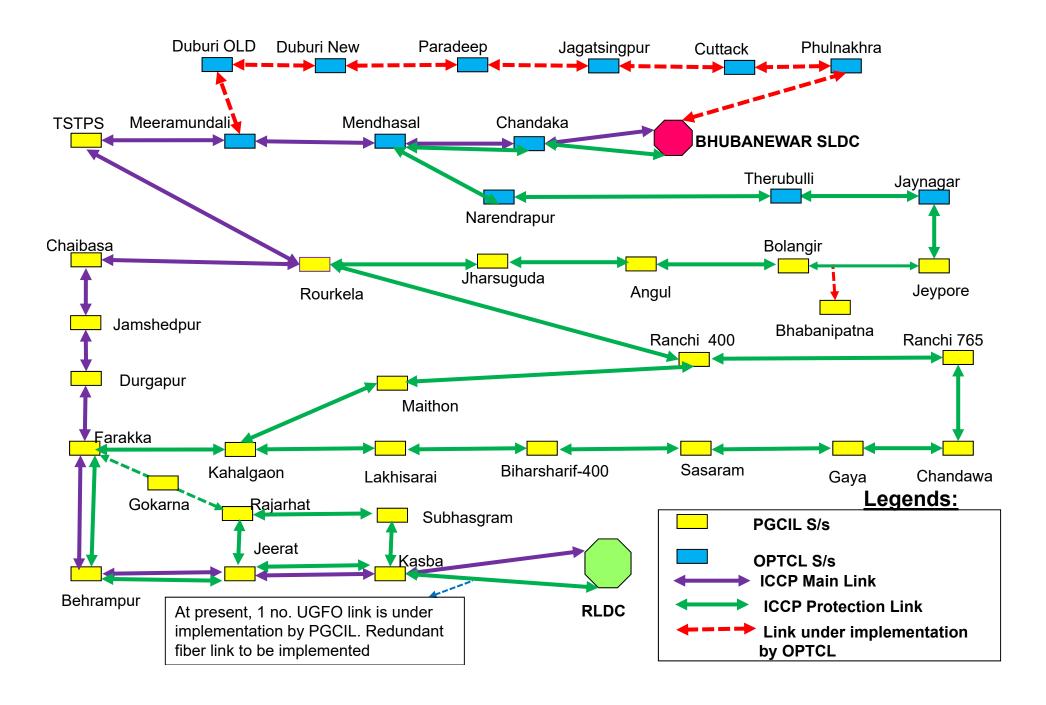


### Annexure - B12.2


## **ICCP FLOW OF BSPTCL**

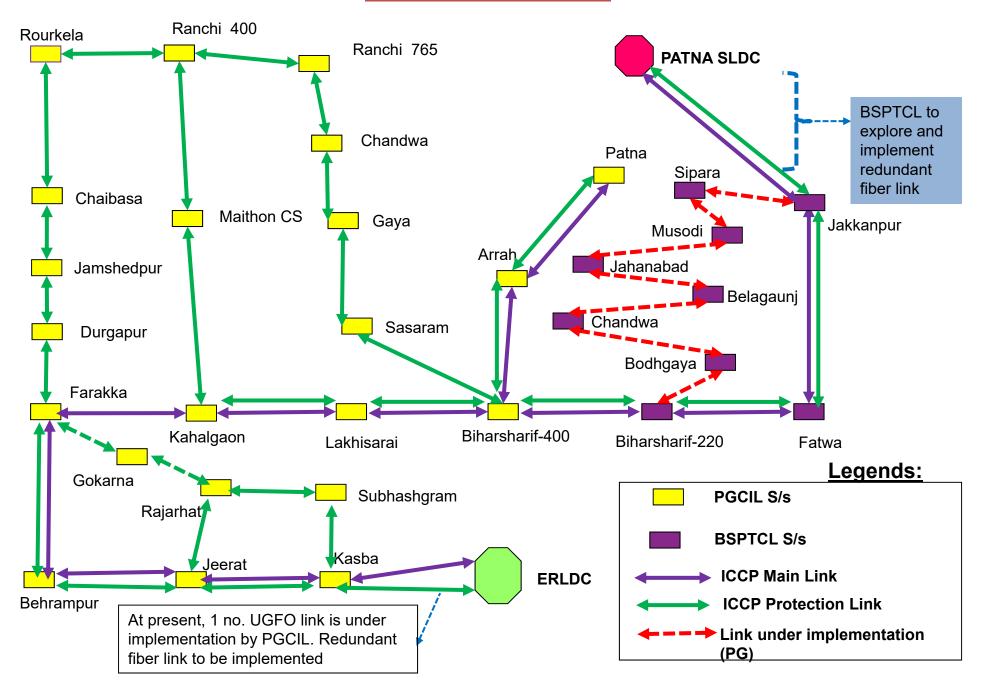

## ICCP FLOW OF JUSNL Annexure - B12.2

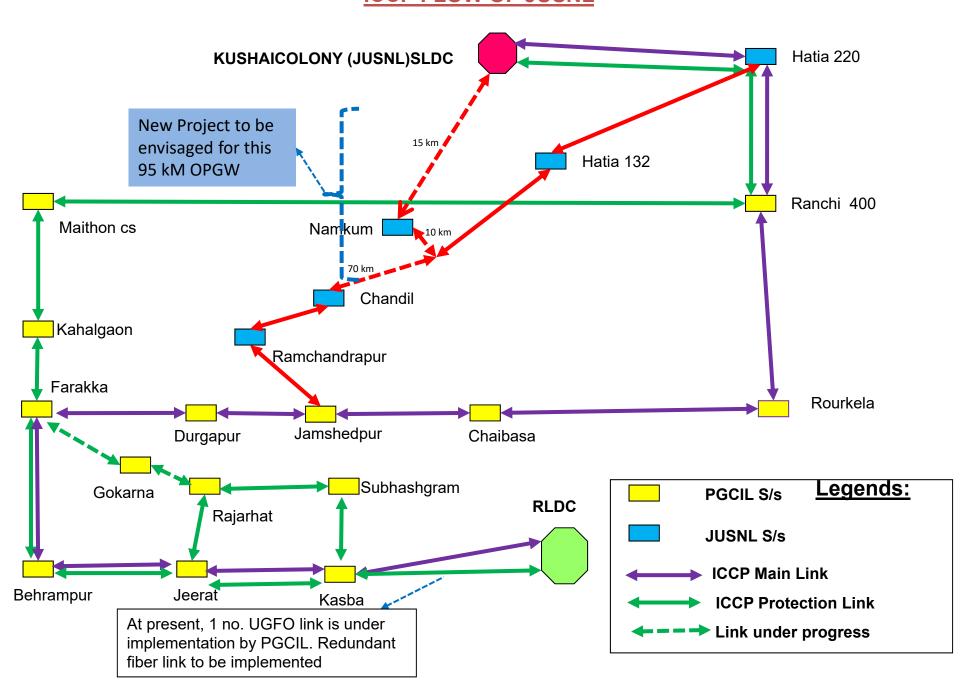

## Annexure - B12.2

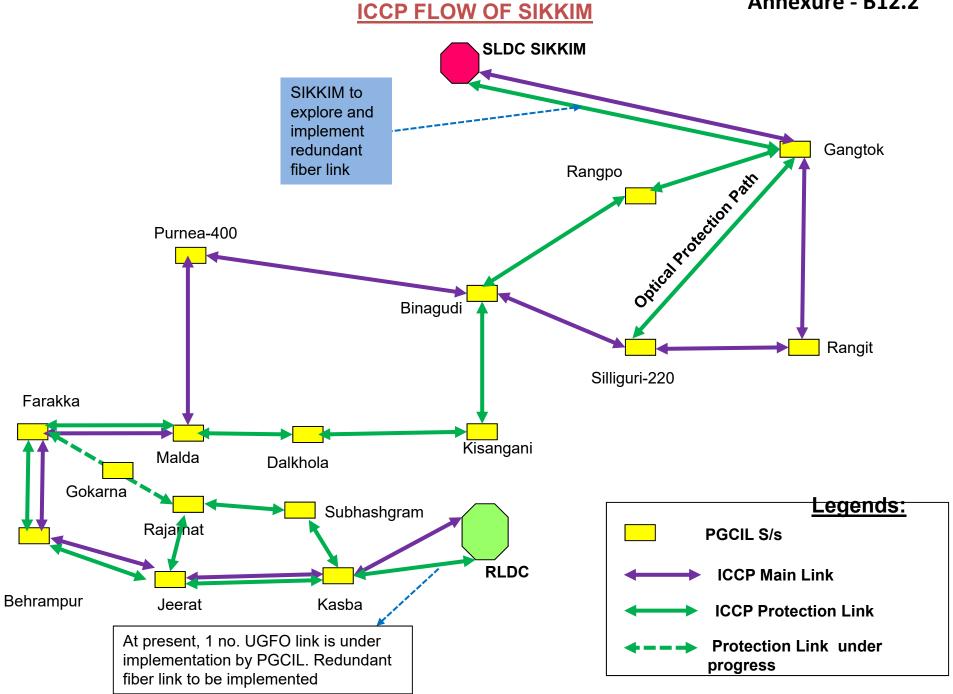

## **Annexure-B13**

## **Utilization of Transmission line**

## **WBSETCL lines**

SI	Name of Line	Percentage uti	lization to meet West	Bengal Demand			
		Quarter 1 2016-17	Quarter 2 2016-17	Quarter 3 2016-17			
1	132 kV Birpara(PG)-Birpara-I	99.2%	94.4%	99.3%			
2	132 kV Birpara(PG)-Birpara-II	99.2%	94.4%	99.3%			
3	132 kV NJP-NBU-I	98.6%	99.2%	98.1%			
4	132 kV NJP-NBU-II	98.6%	99.2%	98.1%			
5	132 kV Malda(PG)-Malda-I	99.9%	99.9%	99.9%			
6	132 kV Malda(PG)-Malda-II	99.9%	99.9%	99.9%			
7	400 kV Kharagpur-Baripada	Natural ISTS					
8	220 kV Santaldhi-Chandil	Natural ISTS					
9	220 kV Waria-Bidhannagar-I	Natural ISTS					
10	220 kV Waria-Bidhannagar-II	Natural ISTS					
11	132 kV Rangit-Rammam	75.0%	70.0%	72.7%			
12	220 kV Subhasgram(PG)-Subhasgram-I	98.6%	98.0%	97.6%			
13	220 kV Subhasgram(PG)-Subhasgram-II	98.6%	98.0%	97.6%			
14	400 kV Parulia-Bidhannagar-I	74.2%	67.8%	59.2%			
15	400 kV Parulia-Bidhannagar-II	74.2%	67.8%	59.2%			
16	220 kV Dalkhola(PG)-Dalkhola-I	99.7%	99.8%	99.8%			
17	220 kV Dalkhola(PG)-Dalkhola-II	99.7%	99.8%	99.8%			
18	132 kV Kurseong-Rangit		Part of ISTS				
19	132 kV Kurseong-Silliguri		Part of ISTS				
20	220 kV Subhasgram(PG)-Bantala	98.5%	98.3%	98.0%			
21	220 kV Subhasgram(PG)-New Town	96.8%	96.6%	96.0%			

## **DVC lines**

SI	Name of Line	Percentage utilization to meet DVC Demand					
		Quarter 1 2016-17	Quarter 2 2016-17	Quarter 3 2016-17			
1	Raghunathpur-DSTPS D/C	14.4%	20.4%	15.2%			
2	Raghunathpur-Ranchi (quad) D/C	14.2%	10.7%	20.5%			
3	LILO of Maithon(PG)-Ranchi(PG) line at RTPS	Part of ISTS					
4	Termination segment at DSTPS of Jamsedpur PG line		Part of ISTS				

## **Annexure-B13**

## **OPTCL lines**

SI	Name of Line	Percentage (	utilization to meet Od	isha Demand		
		Quarter 1 2016-17	Quarter 2 2016-17	Quarter 3 2016-17		
1	400 kV Indravati-Indravati(PG)	34.4%	31.4%	35.7%		
2	400 kV Regali-Keonjhar	15.2%	13.7%	18.2%		
3	400 kV Keonjhar-Baripada	15.2%	13.7%	18.2%		
4	400 kV Baripada-Khargpur		Natural ISTS			
5	220 kV Balimela-U.Sileru		Natural ISTS			
6	220 kV Jeypore-Jaynagar D/C	6.5%	5.3%	10.7%		
7	220 kV Budhipadar-Korba D/C	Natural ISTS				
8	220 kV Tarkera-Bisra D/C	75.7%	71.1%	80.7%		
9	220 kV Joda-Ramchandrapur	Natural ISTS				
10	220kV Joda-Jindal	0.2%	0.4%	0.5%		
11	220 kV Jindal-Jamsedpur		Natural ISTS			
12	220 kV Rengali-Rengali(PG)	46.4%	38.8%	44.7%		
13	220 kV Rengali PH- TSTPS	83.8%	79.9%	86.3%		
14	220 kV TTPS-TSTPS	53.2%	44.5%	52.2%		
15	220 kV TSTPS-Meramundali	42.2%	23.3%	33.1%		
16	220 kV Baripada-Balasore	92.8%	91.3%	93.7%		
17	132 kV Joda-Kendposi		Natural ISTS			
18	132 kV Baripada-Rairangpur	99.7%	99.8%	88.7%		
19	132 kV Baripada-Baripada(PG)	99.4%	99.7%	99.5%		

## Annexure - B14

## Current Status of Letter of Credit (LC) amount against UI charges for ER constituents


#### Figures in Lacs of Rupees


SI No	ER Constituents	No. of weeks in which Deviation Charge payable	No of times payment was delayed during 2015-16	Total Deviation charges payable to pool during 2015-16	Average weekly Deviation Charge liability	LC Amount	Due date of expiry	Remarks
		(A)	(B)	(C)	(D)	(E)	(F)	(G)
1	BSPHCL	42	42	9230.45609	177.50877	195.25965	Expired	Not Opened/Renewd (LC Expired of amount 529.52000 Lac on 03.01.17)
2	JUVNL	36	36	4060.64239	78.08928	85.89820	Not Opened	letter written
3	SIKKIM	5	5	75.76714	1.45706	1.60277	Expired	Not Opened/Renewd (LC Expired of amount 2.85136 Lac on 04.10.16)
4	MPL	7	2	34.59999	0.66538	0.73192	31.08.2017	Opened for 0.73192 Lacs
6	VEDANTA	48	15	7892.76469	151.78394	166.96233	31.05.2017	Opened for 166.96233 Lacs
7	APNRL	24	24	741.51734	14.25995	15.68594	20.04.2017	Opened for 15.63594 Lacs
8	CHUZACHEN	8	6	261.0675	5.02053	5.52258	Not Opened	Not Opened /Renewed
9	GMR	19	7	929.588	17.87669	19.66436	15.07.2017	Opened for 19.66436 Lacs
10	IND-BARATH	46	16	248.75964	4.78384	5.26222	Not Opened	Letter written


#### List of Time Drifted SEMs in El

	List of Time Drifted SEMs in ER										
SNO 1	BI-11	Sub Station ARA(BSPTCL)	METER S NO NP-6052-A	FEEDER NAME ARA END OF ARAH (PG)	23:53:55	00:04:11	TIME DIF(min) 11				
2	BI-58 BI-59	BANKA(BSPTCL) BANKA(BSPTCL)	NP-7833-A NP-7874-A	132 KV BANKA(PG) 132 KV BANKA LINE	22:38:06 18:41:05	22:51:58 18:52:12	13 11				
4	BH-22	BARH(NTPC)	NP-7482-A	400 KV BARH 200 MVA ICT 3	22:55:11	23:12:14	17				
5 6	EM-59 EM-58	BARIPADA(PG) BARIPADA(PG)	NP-5911-A NP-5913-A	HV SIDE OF 220/132 KV ICT-1 BARIPADA END OF BALASORE (GRIDCO) -2	09:02:45 09:01:52	09:13:24 09:15:33	11 14				
7	EM-89	BARIPADA(PG)	NP-5971-A	BARIPADA END OF MENDHASAL(GRIDCO)-2	09:09:05	09:22:55	13				
8	EM-87 EM-88	BARIPADA(PG) BARIPADA(PG)	NP-5974-A NP-5975-A	BARIPADA END OF JAMSHEDPUR BARIPADA END OF MENDHASAL(GRIDCO)-1	09:10:51 09:08:13	09:24:56 09:21:11	14 13				
10	ES-45	BARIPADA(PG)	NP-8074-A	400 KV SIDE OF 500 MVA ICT-3	09:11:44	09:23:48	12				
11 12	EP-88 EP-94	BERHAMPORE(PG) BERHAMPORE(PG)	NP-7989-A NP-7993-A	400 KV FARAKKA(NTPC) LINE(CHECK) 400 KV BHERMARA(BANGLDESH) LINE-1(CHECK)	09:00:48 09:03:49	09:18:34 09:20:14	18 17				
13 14	EP-95 EP-93	BERHAMPORE (PG) BHERAMARA (BANGADESH)	NP-7994-A NP-7612-A	400 KV BHERMARA(BANGLDESH) LINE-2(MAIN) 400 KV BHERMARA(BANGLDESH) LINE-1(MAIN)	09:04:39 09:03:04	09:18:45 09:22:02	14 19				
15	EP-96	BHERAMARA(BANGADESH)	NP-7613-A	400 KV BHERMARA(BANGLDESH) LINE-1(MAIN)  400 KV BHERMARA(BANGLDESH) LINE-2(CHECK)	09:05:26	09:18:20	13				
16 17	EM-07 FM-09	Binaguri(PG) Binaguri(PG)	NP-5086-A NP-5088-A	BINAGURI END OF TALA (THP)-1 BINAGURI END OF MALBASE(PG)	19:47:02 19:50:43	19:57:56 20:02:13	10 12				
18	EM-12	Binaguri(PG)	NP-5091-A	BINAGURI END OF PURNEA-2	19:56:15	20:08:26	12				
19 20	EM-13 ER-19	Binaguri(PG) Binaguri(PG)	NP-5092-A NP-5882-A	BINAGURI END OF PURNEA-3 BINAGURI END OF NEW JALPAIGURI (WBIHAR)-I	19:53:33 20:00:39	20:03:11	10 14				
21	ER-21	Binaguri(PG)	NP-5885-A	BINAGURI END OF BONGAIGAON (NER)-2	19:52:36	20:03:39	11				
22	EM-68 EM-10	Binaguri(PG) Binaguri(PG)	NP-5887-A NP-5888-A	BINAGURI END OF Rangpo-2 BINAGURI END OF TALA (THP)-4	19:58:06 19:49:46	20:12:21 20:02:38	14 13				
24 25	ER-87 EN-06	Binaguri(PG) Binaguri(PG)	NP-5890-A NP-7917-A	LV SIDE OF BINAGURI 315 MVA ICT-2 BINAGURI END ALIPURDUAR LINE - 1	20:03:27 19:59:51	20:13:02 20:16:21	10 17				
26	EN-07	Binaguri(PG)	NP-7918-A	BINAGURI END BONGAIGAON LINE - 2	19:59:03	20:14:03	15				
27 28	EP-49 ER-44	BIRPARA(PG) BIRPARA(PG)	NP-5891-A NP-5892-A	HV SIDE OF 220 ICT-2 BIRPARA END OF BIRPARA (WB)-1	23:28:02	23:55:00	27 35				
29	ER-40	BIRPARA(PG)	NP-6464-A	BIRPARA END OF CHUKHA (CHPC) -2	23:19:06	23:08:00	-11				
30 31	ER-41 WB-02	BIRPARA(PG) BIRPARA(WBSETCL)	NP-6490-A NP-5893-A	BIRPARA END OF MALBASE BIRPARA END OF BIRPARA (PG)-2	23:22:43 23:12:50	23:12:46 23:34:26	-10 22				
32 33	EP-33 EP-31	BOLANGIR(PG) BOLANGIR(PG)	NP-7536-A NP-7537-A	400 KV SIDE BOLANGIR KV 315 MVA ICT-II BOLANGIR END OF JEYPORE-1	09:01:48 09:00:02	09:19:00 09:13:50	18 13				
34	EP-32	BOLANGIR(PG)	NP-7538-A	BOLANGIR END OF JINDAL(JDL)	09:02:22	09:17:30	15				
35 36	EP-99 JS-05	BOLANGIR(PG) CHANDIL(JUVNL)	NP-7560-A NP-7434-A	400 KV BOLANGIR 315 MVA ICT 1 CHANDIL END OF RANCHI (PG)	09:00:48 22:20:07	09:18:37 22:36:46	18 16				
37	JS-08	CHANDIL(JUVNL)	NP-7435-A	CHANDIL END OF HATIA(JSEB)	22:17:43	22:32:35	15				
38 39	JS-57 JS-56	CHANDIL(JUVNL) CHANDIL(JUVNL)	NP-7436-A NP-7461-A	CHANDIL END OF SANTALDIH (WBIHAR) CHANDIL END OF MANIQUE (DVC)	22:19:19 22:18:31	22:35:21 22:29:53	16 11				
40	ER-60 ER-61	DALKHOLA(PG)  DALKHOLA(PG)	NP-6477-A NP-6479-A	220 KV DALKHOLA FDR1 220 KV DALKHOLA FDR2	09:05:12 09:04:08	08:51:04 08:47:14	-14 -17				
41	EM-96	DALKHOLA(PG)  DALKHOLA(PG)	NP-6479-A NP-7969-A	220 RV DALKHOLA FDR2 220 DALKHOLA(WBSETCL) LINE-1	09:04:08	09:16:10	-17 16				
43	EP-55 BI-62	Dalkhola(WB) DEHRI(BSPTCL)	NP-5068-A NP-6097-A	220 KV DALKHOLA (WB) LINE-2 220 KV DEHRI (BSPHCL) - PUSAULII (PG)	09:00:55 09:00:02	09:23:05 09:10:16	23 10				
45	BI-18	DEHRI(BSPTCL)	NP-7397-A	220 KV DEHRI (BSPHCL)-GAYA(PG) LINE-II	09:01:47	09:16:18	15				
46 47	BI-17 BI-12	DEHRI(BSPTCL) DUMRAON(BSPTCL)	NP-7449-A NP-6067-A	220 KV DEHRI (BSPHCL)-GAYA(PG) LINE-I 132 KV DUMRAON (BSPHCL) - ARAH (PG)	09:01:00 23:10:26	09:15:30 23:20:21	14 10				
48	ER-68	DURGAPUR(PG)	NP-5831-A	400 KV B NAGAR-1 LINE MAIN	09:16:51	09:29:10	13				
49 50	EM-20	DURGAPUR(PG) DURGAPUR(PG)	NP-6024-B NP-7557-A	RF 1KT-2 LINE 400 KV SDG LINE 2	09:31:11 09:11:20	09:47:28 09:29:02	16 18				
51 52	EP-79 EP-80	DURGAPUR(PG) DURGAPUR(PG)	NP-7954-A NP-7975-A	400 KV FARAKKA LINE 1 400 KV FARAKKA 2	09:05:48 09:08:34	09:20:09 09:24:31	15 16				
53	FK-05	FARAKKA(NTPC)	NP-7553-A	FARAKKA GT5	09:02:40	09:18:09	16				
54 55	EP-87 FK-03	FARAKKA(NTPC) FARAKKA(NTPC)	NP-7609-A NP-7928-A	400 KV FARAKKA(NTPC) LINE(MAIN) FARAKKA GT-3	09:00:02 09:13:42	09:18:30 09:28:38	18 15				
56	FK-01	FARAKKA(NTPC)	NP-7960-A	FARAKKA (GT1)	09:14:29	09:29:23	15				
57 58	FK-02 BI-23	FARAKKA(NTPC) FATUA(BSPTCL)	NP-7986-A NP-7850-A	FARAKKA GT-2 220 KV PATNA (PG)	09:15:18 23:52:11	09:30:45 00:03:30	15 11				
59 60	EM-06 EM-02	GANGTOK(PG) GANGTOK(PG)	NP-6025-A NP-6027-A	66 KV SIDE OF GANGTOK 132/66 KV ICT-2 132 KV GANGTOK(PG) - RANGIT (NHPC)	19:57:28 19:53:46	20:17:08 20:04:40	20 11				
61	EM-05	GANGTOK(PG)	NP-6028-A	132 KV SIDE OF GANGTOK 132/66 KV ICT-2	19:55:37	20:11:32	16				
62	EM-03 EM-04	GANGTOK(PG) GANGTOK(PG)	NP-6029-A NP-6030-A	132 KV SIDE OF GANGTOK 132/66 KV ICT-1 66 KV SIDE OF GANGTOK 132/66 KV ICT-1	19:54:43 19:56:31	20:04:05 20:06:07	10 10				
64	EP-16	GAYA(PG)	NP-6098-A	220 KV GAYA (PG)-DEHRI(BSPHCL) LINE-II	09:35:45	09:49:18	14 10				
65 66	EP-28 EP-12	GAYA(PG) GAYA(PG)	NP-7428-A NP-7453-A	765 KV SIDE OF 765/400 KV GAYA ICT-1 400 KV SIDE GAYA 400/220 315 MVA ICT-2	21:43:26 09:21:49	21:53:21 09:32:36	11				
67 68	EN-70 ES-62	GAYA(PG) GAYA(PG)	NP-7473-A NP-7827-A	GAYA- KODERMA LINE-1 220 KV GAYA (PG)-SONAGAR(BSPHCL) LINE-I	09:13:36 09:41:23	09:23:32 09:51:00	10 10				
69	BI-52	HAJIPUR(BSPTCL)	NP-7851-A	220KV MUZAFFARPUR -1 (PG)	09:00:02	09:16:29	16				
70 71	BI-53 JS-06	HAJIPUR(BSPTCL) HATIA(JUVNL)	NP-7852-A NP-6121-A	220KV MUZAFARPUR -2(PG) HATIA END OF CHANDIL (JSEB)	09:00:49 09:00:54	09:14:46 09:22:27	14 22				
72 73	JS-07 DV-57	HATIA(JUVNL) JAMSHEDPUR(DVC)	NP-6122-A NP-6010-B	HATIA END OF RANCHI (PG)  JAMSHEDPUR END OF JODA(GRIDCO)	09:00:02 23:54:36	09:13:37 00:25:47	13 31				
74	EP-89	JEERAT(WBSETCL)	NP-7610-A	400 KV JEERAT(WBSETCL) LINE(MAIN)	09:01:34	09:22:31	21				
75 76	EP-90 ER-75	JEERAT(WBSETCL) JEYPORE(PG)	NP-7611-A NP-5955-A	400 KV JEERAT(WBSETCL) LINE(CHECK) HV SIDE OF JEYPORE 315 MVA ICT -1	09:02:19 21:24:58	09:17:48 22:13:48	15 49				
77	ER-77	JEYPORE(PG)	NP-5956-A	HV SIDE OF JEYPORE 315 MVA ICT -2	21:25:58	22:18:59	53				
78 79	ER-34 ER-35	JEYPORE(PG) JEYPORE(PG)	NP-5957-A NP-5958-A	JEYPORE END OF JEYNAGAR (GRIDCO) -1 JEYPORE END OF JEYNAGAR (GRIDCO) -2	21:26:51 21:27:44	22:18:39 22:22:53	52 55				
80 81	ER-36 ER-38	JEYPORE(PG) JEYPORE(PG)	NP-5959-A NP-5960-A	JEYPORE END OF INDRAVATI (PG)  JEYPORE END OF M MUNDALI (GRIDCO)	21:28:37 21:29:33	22:15:05 22:19:08	47 50				
82	ER-84	JEYPORE(PG)	NP-5961-A	JEYPORE END OF GAJUWAKA (PG) -1	06:21:08	07:07:11	46				
83 84	ER-85 JD-02	JEYPORE(PG) JITPL	NP-5962-A NP-7947-A	JEYPORE END OF GAJUWAKA (PG) -2 400 KV SIDE OF JINDAL GT-2	21:30:48 23:53:47	22:19:44 00:09:32	49 16				
85	JD-01	JITPL	NP-7948-A	400 KV SIDE OF JINDAL GT-1	23:53:02	00:09:00	16				
86 87	BI-09 BI-10	KAHALGAON(BSPTCL) KAHALGAON(BSPTCL)	NP-6071-A NP-6076-A	KAHALGAON END OF LALMATIA LINE-I KAHALGAON END OF KAHALGAON (NTPC)	22:05:39 22:06:39	22:22:46 22:19:52	17 13				
88 89	WB-59 JS-52	KALIMPONG(WBSETCL) KENDIPOSI(JUVNL)	NP-5994-A NP-6117-A	Melli Bazar 1 KENDIPOSI END OF JODA (GRIDCO)	23:40:47 22:09:56	00:10:31 22:23:47	30 14				
90	EP-64	KEONJHAR(PG)	NP-7546-A	HV SIDE OF 400/220 KV JEONJHAR ICT-1	09:05:33	09:20:24	15				
91 92	EP-62 EP-63	KEONJHAR(PG) KEONJHAR(PG)	NP-7547-A NP-7548-A	KEONJHAR END OF 400 KV BARIPADA(PG) KEONJHAR END OF 400 KV RENGALI(PG)	09:08:19 09:02:48	09:25:21 09:17:25	17 15				
93	EP-65	KEONJHAR(PG)	NP-7549-A	HV SIDE OF 400/220 KV JEONJHAR ICT-2	09:00:02	09:12:42	12				
94 95	BI-22 WB-17	KHAGAUL(BSPTCL) KHARAGPUR(WBSETCL)	NP-5833-A NP-7563-A	KHAGAUL END OF PATNA 400 KV BARIPADA(PG)	22:25:18 23:40:21	22:38:27 23:57:33	13 17				
96 97	BI-21 DV-61	Kishanganj(BSPTCL) KOLAGHAT(DVC)	NP-6085-A NP-6558-B	KISHANGANJ END OF DALKHOLA (WBIHAR) KOLAGHAT END OF KOLAGHAT (WBIHAR)	23:41:05 22:00:51	23:52:10 21:50:07	11 -10				
98	WB-57	KURSEONG(WBSETCL)	NP-7541-A	132 KV RANGIT(NHPC)	23:42:17	23:55:27	13				
99 100	JS-03 JS-04	LALMATIA(JUVNL) LALMATIA(JUVNL)	NP-6108-A NP-6109-A	132 KV LALMATIA (JSEB) - KAHALGAON (NTPC) 220 KV LALMATIA (JSEB) - FARAKKA (NTPC)	09:01:00 09:01:53	09:14:46 09:13:54	13 12				
101	JS-63	LALMTIA(JUVNL)	NP-6107-A	32 KV LALMATIA (JSEB) - KAHALGAON (BSPHCL)	09:00:02	09:14:29	14				
102 103	EM-97 EM-98	MAITHON(PG) MAITHON(PG)	NP-5206-A NP-5225-A	MAITHON END OF MEJIA LINE-1 MAITHON END OF MEJIA LINE-2	21:10:23 21:03:50	21:40:54 21:34:47	30 31				
104 105	ER-12 ER-69	MAITHON(PG) MAITHON(PG)	NP-6451-A NP-6453-A	MAITHON END OF KALYANESWARI (DVC) -2 HV SIDE OF MAITHON 315 MVA ICT -1	21:00:02 09:04:31	20:49:16 08:51:40	-11 -13				
106	EM-82	MAITHON(PG)	NP-6509-A	MAITHON END OF KALYANESHWARI LINE-3	21:01:59	20:51:28	-10				
107 108	EM-84 EM-81	MAITHON(PG) MAITHON(PG)	NP-6519-A NP-6529-A	MAITHON END OF MAITHON RB (MPL)-1 MAITHON END OF KALYANESWARI (DVC) -1	21:09:29 21:01:02	20:58:35 20:51:46	-11 -10				
100	LIVI OI	(1 0)	UUL 7-M		21.01.02	20.01.40	10				

109	EP-06	MAITHON(PG)	NP-7492-A	MAITHON END OF DURGAPUR(PG)-II	21:13:44	21:31:25	18
110	EP-05	MAITHON(PG)	NP-7534-A	MAITHON END OF DURGAPUR(PG)-I	21:12:56	21:28:42	16
111	EP-22 EP-50	MAITHON(PG) MAITHON(PG)	NP-7535-A NP-7550-A	MAITHON END OF RTPS -2  MAITHON END OF KODERMA LINE-I	21:15:20 21:16:08	21:32:44 21:32:29	17 16
113	EP-51	MAITHON(PG)	NP-7551-A	MAITHON END OF KODERMA LINE-II	21:16:56	21:32:26	16
114	EP-78	MAITHON(PG)	NP-7902-A	MAITHON END OF RANCHI LINE	21:14:32	21:29:03	15
115 116	EP-76 EP-77	MAITHON(PG) MAITHON(PG)	NP-7903-A NP-7904-A	MAITHON END OF KAHALGAON LINE-1 MAITHON END OF KAHALGAON LINE-2	21:12:08	21:27:42 21:26:49	15 15
117	ER-59	MALDA(PG)	NP-6478-A	132 KV MALDA WBSETCL2	09:00:02	08:44:37	-16
118	ER-58	MALDA(PG)	NP-7555-A	132 KV MALDA WBSETCL1	09:01:47	09:19:24	18
119 120	EP-91 EN-04	MALDA(PG) MALDA(PG)	NP-7925-A NP-7926-A	220 KV ICT3 220 KV ICT-5	09:06:04 09:03:21	09:21:52 09:19:12	15 16
121	ER-88	MALDA(PG)	NP-7927-A	400 KV PURNIA2	09:07:38	09:23:13	16
122	EP-92	MALDA(PG)	NP-7976-A	400 KV PURNIA1	09:06:51	09:21:47	15
123 124	EP-98 EP-97	MALDA(PG) MALDA(PG)	NP-7977-A NP-7978-A	132 KV ICT-1 132 KV ICT-2	09:01:01 09:02:34	09:14:28 09:17:40	13 15
125	DV-24	MEJIA(DVC)	NP-5226-A	MEJIA END OF MAITHON(PG)-1	09:01:42	09:23:30	22
126	DV-25	MEJIA(DVC)	NP-5227-A	MEJIA END OF MAITHON(PG)-2	09:03:28	09:20:51	17
127	DV-05	MEJIA(DVC)	NP-6508-A	MEJIA END OF JAMSHEDPUR (PG)	09:09:45	08:59:28	-10 -11
128 129	DV-13 DV-12	MEJIA(DVC) MEJIA(DVC)	NP-6532-A NP-6534-A	HV SIDE OF MEJIA GT-2 HV SIDE OF MEJIA GT-1	09:04:21 09:06:05	08:53:42 08:55:15	-11
130	DV-04	MEJIA(DVC)	NP-6557-A	MEJIA END OF DSTPS (DVC)	09:08:07	08:56:20	-12
131	DV-16	MEJIA(DVC)	NP-6776-A	MEJIA END OF DSTPP (DVC)	09:07:12	08:53:23	-14
132	DV-17 DV-26	MEJIA(DVC) MEJIA(DVC)	NP-7493-A NP-7494-A	MEJIA END OF JAMSHEDPUR (PG)  MEJIA END OF MAITHON(PG)-1	09:08:59 09:00:55	09:23:37 09:15:33	15 15
134	DV-27	MEJIA(DVC)	NP-7495-A	MEJIA END OF MAITHON(PG)-2	09:02:41	09:23:33	21
135	DV-14	MEJIA(DVC)	NP-7943-A	HV SIDE OF MEJIA STN TRANSF-1	09:00:02	09:16:13	16
136 137	SM-51 SM-04	MELLI(SIKKIM) MELLI(SIKKIM)	NP-5849-A NP-5997-A	66 KV Kalimpong 132 KV Rangit	11:56:16 09:00:02	12:07:52 09:12:34	11 12
138	MR-05	MPL	NP-7568-A	HV SIDE OF MAITHON RB GT-1	21:59:56	22:12:50	13
139	MR-08	MPL	NP-7897-A	HV SIDE OF MAITHON	22:31:43	22:41:40	10
140	MR-06 EP-56	MPL MUZAFFARPUR(PG)	NP-7972-A NP-5233-A	HV SIDE OF MAITHON RB GT-2 MUZAFFARPUR(PG)-HAJIPUR(BSPHCL) LINE-1	23:44:34 09:07:16	00:00:08 09:22:33	16 15
142	EP-57	MUZAFFARPUR(PG)	NP-5234-A	MUZAFFARPUR(PG)-HAJIPUR(BSPHCL) LINE-2	09:08:09	09:20:37	12
143	WB-04	NBU(WBSETCL)	NP-5953-A	NBU END OF SILIGURI(PG)-1	09:00:02	09:16:17	16
144 145	ES-34 EM-56	PANDIABIL(PG) PATNA(PG)	NP-7554-A NP-5271-A	400 KV PANDIABIL(PG)-MENDHASAL(GRIDCO)-2 220 KV SIDE OF PATNA ICT-1	07:02:35 23:38:17	07:19:05 23:49:19	17 11
146	EM-53	PATNA(PG)	NP-5273-A	400 KV PATNA (ER) - BALIA (NR)-2	09:31:35	09:42:34	11
147	EM-65	PATNA(PG)	NP-5832-A	220 KV PATNA(PG) - KHAGAUL(BSPHCL)	23:49:49	00:00:26	11
148 149	EM-62 EM-64	PATNA(PG) PATNA(PG)	NP-5839-A NP-5865-A	400 KV SIDE OF PATNA ICT-2 220 KV PATNA - FATUA	09:17:10 23:32:29	09:27:43 23:44:36	10 12
150	EP-47	PATNA(PG)	NP-7838-A	220 KV PATNA(PG)-SIPARA(BSPHCL) LINE-II	09:14:25	09:26:48	12
151	EP-46	PATNA(PG)	NP-7864-A	220 KV PATNA(PG)-SIPARA(BSPHCL) LINE-I	23:55:20	00:09:44	14
152 153	JS-55 JS-54	PATRATU(JUVNL) PATRATU(JUVNL)	NP-6003-B NP-6004-B	PATRATU END OF PATRATU (DVC) TRANSFER BUS  PATRATU END OF PATRATU (DVC) -1	09:01:50 09:00:55	09:16:51 09:22:02	15 22
154	JS-40	PATRATU(JUVNL)	NP-6005-B	PATRATU END OF PATRATU (DVC) -2	09:00:02	09:19:40	19
155	BI-20	Purnea(BSPTCL)	NP-5236-A	PURNEA END OF PURNEA (PG)-3	23:40:11	23:55:06	15
156 157	BI-03 BI-51	Purnea(BSPTCL)	NP-6088-A NP-6090-A	PURNEA END OF PURNEA (PG) -1 PURNEA END OF PURNEA (PG) -3	23:37:32 23:38:26	23:47:23 23:49:16	10 11
158	ER-62	Purnea(BSPTCL) Purnea(PG)	NP-6081-A	PURNEA END OF PURNEA (BIHAR) -1	09:00:02	09:12:33	12
159	ER-48	Purnea(PG)	NP-6083-A	PURNEA END OF PURNEA (BIHAR) -3	09:01:59	09:16:00	15
160 161	ER-65 ER-64	Purnea(PG) Purnea(PG)	NP-7419-A NP-7420-A	PURNEA END OF DALKHOLA (PG) -2 PURNEA END OF DALKHOLA (PG) -1	09:04:37 09:03:50	09:22:24 09:21:12	18 18
162	EM-51	Purnea(PG)	NP-7421-A	PURNEA END OF MUZAFFARPUR -1	09:05:50	09:21:38	16
163	EM-52	Purnea(PG)	NP-7422-A	PURNEA END OF MUZAFFARPUR LINE-2	09:05:03	09:22:52	17
164 165	ER-32 ER-33	Purnea(PG) Purnea(PG)	NP-7423-A NP-7424-A	PURNEA END OF BINAGURI (PG)-2 PURNEA END OF BINAGURI (PG)-1	09:02:28 09:01:41	09:20:58 09:18:13	18 17
166	EP-83	Purnea(PG)	NP-7828-A	PURNEA END OF MADHEPURA(BSPHCL) LINE-1	09:00:55	09:12:19	12
167	EP-84	Purnea(PG)	NP-7829-A	PURNEA END OF MADHEPURA(BSPHCL) LINE-2	09:00:02	09:16:03	16
168 169	EP-86 EM-41	Purnea(PG) RANCHI(PG)	NP-7835-A NP-5871-A	PURNEA END OF BIHARSHARIFF LINE-2 400 KV RANCHI(PG)-RTPS(DVC)	09:07:35	09:21:09	14 12
170	EM-42	RANCHI(PG)	NP-5871-A NP-5873-A	400 KV SIDE OF RANCHI ICT-2	09:07:03	09:17:20	10
171	EM-46	RANCHI(PG)	NP-5877-A	400 KV RANCHI-MAITHON	09:06:07	09:17:20	11
172	EN-08 EN-05	RANCHI(PG) RANCHI(PG)	NP-7402-A	400 KV RANCHI (PG) - RANCHI NEW(PG) LINE-3	09:17:33	09:36:25	19 14
173 174	EN-05	RANCHI(PG)	NP-7837-A NP-7873-A	400 KV RANCHI(PG)- RANCHI NEW(PG) LINE-1 400 KV RANCHI(PG)- RANCHI NEW(PG) LINE-4	09:16:00 09:18:17	09:30:43 09:33:30	15
175	EM-49	RANCHI(PG)	NP-7880-A	220 KV HATIA LINE 2	09:03:34	09:16:14	13
176	EN-96	RANCHI(PG)	NP-7881-A	220 KV HATIA LINE 1	09:02:47	09:16:52	14
177 178	EP-81 ER-72	RENGALI(PG) ROURKELA(PG)	NP-7952-A NP-5930-A	RENGALI END OF 400 KV TSTPP LINE-1 HV SIDE OF ROURKELA 315 MVA ICT -2	22:13:44 22:22:38	22:23:29 22:39:29	10 17
179	ER-26	ROURKELA(PG)	NP-5931-A	ROURKELA END OF JAMSHEDPUR (PG)-2	22:29:05	22:50:05	21
180	ER-24	ROURKELA(PG) ROURKELA(PG)	NP-5933-A	ROURKELA END OF TARKERA (GRIDCO)-2 ROURKELA END OF RAIGARH - I	22:24:36	22:38:38	14
181 182	ER-80 EM-92	ROURKELA(PG) ROURKELA(PG)	NP-5943-A NP-7965-A	ROURKELA END OF RAIGARH - I ROURKELA END OF RAIGARH (WR)-2	22:21:39 22:25:34	22:31:07 22:38:30	10 13
183	WB-53	SANTALDIH(WBSETCL)	NP-7942-A	SANTALDIH END OF CHANDIL (JSEB)	23:53:41	00:10:15	17
184	EP-23	SASARAM(PG)	NP-7412-A	400 KV SASARAM(PG)-NABI NAGAR(BSPHCL)-II 400 KV SASARAM (PG) EAST BUS-III	09:07:55	09:23:52	16
185 186	EP-01 EP-02	SASARAM(PG) SASARAM(PG)	NP-7414-A NP-7468-A	400 KV SASARAM (PG) EAST BUS-III 400 KV SASARAM (PG) NORTH BUS-3 BALIA	09:10:27 08:57:39	09:20:14 09:14:08	10 17
187	BI-25	SIPARA(BSPTCL)	NP-7870-A	220 KV PATNÁ (PG) LINE-2	23:33:17	23:45:17	12
188	BI-24	SIPARA(BSPTCL)	NP-7872-A	220 KV PATNA (PG) LINE-1	23:31:15	23:46:27	15
189 190	BI-66 BI-60	SONNAGAR(BSPTCL) SONNAGAR(BSPTCL)	NP-6013-B NP-6015-B	SONNAGAR END OF RIHAND(UPSEB)  132 KV SONENAGAR (BSPHCL)- JAPLA (JSEB)	22:17:13 22:16:13	22:37:00 22:36:50	20 20
191	EM-19	SUBHASHGRAM(PG)	NP-5847-A	SUBHASGRAM END OF SUBHASGRAM-2 (WB)	09:03:41	09:14:18	11
192	EN-18	SUBHASHGRAM(PG)	NP-7566-A	315 MVA ICT 4 - 220 KV	09:10:10	09:26:31	16
193 194	EP-72 EN-16	SUBHASHGRAM(PG) SUBHASHGRAM(PG)	NP-7935-A NP-7938-A	SUBHASGRAM END OF EMBYPASS(WB) LINE-1 400 KV HALDIA LINE 1	09:06:16 09:08:36	09:16:50 09:20:14	10 12
195	EP-58	SUBHASHGRAM(PG)	NP-7939-A	HV SIDE OF SUBHASGRAM ICT-4	09:07:50	09:17:37	10
196	EN-28	SUBHASHGRAM(PG)	NP-7996-A	315 MVA ICT 3 - 220 KV	09:10:57	09:23:04	13
197 198	EP-68 EP-69	SUNDERGARH(PG) SUNDERGARH(PG)	NP-7896-A NP-7898-A	400 KV RAIGARH(WR) LINE-1 400 KV ROURKELA(PG) LINE-1	23:38:00 23:38:48	23:50:25 23:55:05	12 17
199	EP-67	SUNDERGARH(PG)	NP-7912-A	400 KV ROURKELA(FG) LINE-1 400 KV ROURKELA(PG) LINE-2	23:37:12	23:51:05	14
200	EP-66	SUNDERGARH(PG)	NP-7913-A	400 KV RAIGARH(WR) LINE-2	23:36:24	23:49:18	13
201	JS-62 DV-35	TENUGHAT(JUVNL) TISCO(DVC)	NP-6115-A NP-7406-A	TENUGHAT END OF BIHARSARIFF(BIHAR) 400 KV BARIPADA (PG)	22:37:18 21:07:27	22:50:40 21:23:25	13 16
202	DV-35 DV-34	TISCO(DVC)	NP-7406-A NP-7408-A	400 KV BARIPADA (PG) 400 KV JAMSHEDPUR (PG)	21:07:27	21:23:25	16
204	ST-06	VEDANTA(GRDICO)	NP-6527-A	ST-2	23:36:37	23:58:38	22
205	ST-02	VEDANTA(GRDICO)	NP-6528-A	GT-2	23:34:50	23:59:50	25
206	ST-01 ST-05	VEDANTA(GRDICO) VEDANTA(GRDICO)	NP-6540-A NP-6543-A	GT-1 ST-1	00:34:32 23:35:43	00:59:21 23:57:58	25 22
				STERLITE END OF RAIGARH (WR)-2	22:26:23	22:15:13	-11
208	EM-93	VEDANTA(GRDICO)	NP-6545-A				
208	EM-93 ST-03 ST-04	VEDANTA(GRDICO)  VEDANTA(GRDICO)  VEDANTA(GRDICO)	NP-6555-A NP-6556-A	GT-3 GT-4	23:37:30 23:38:23	00:02:54 23:58:40	25 20

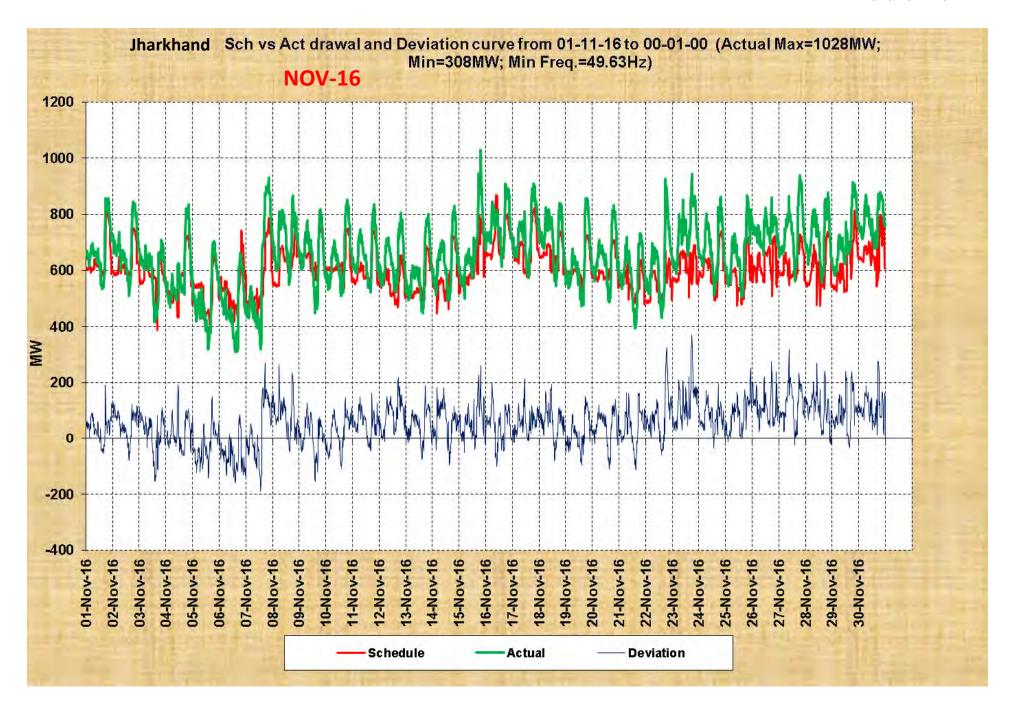

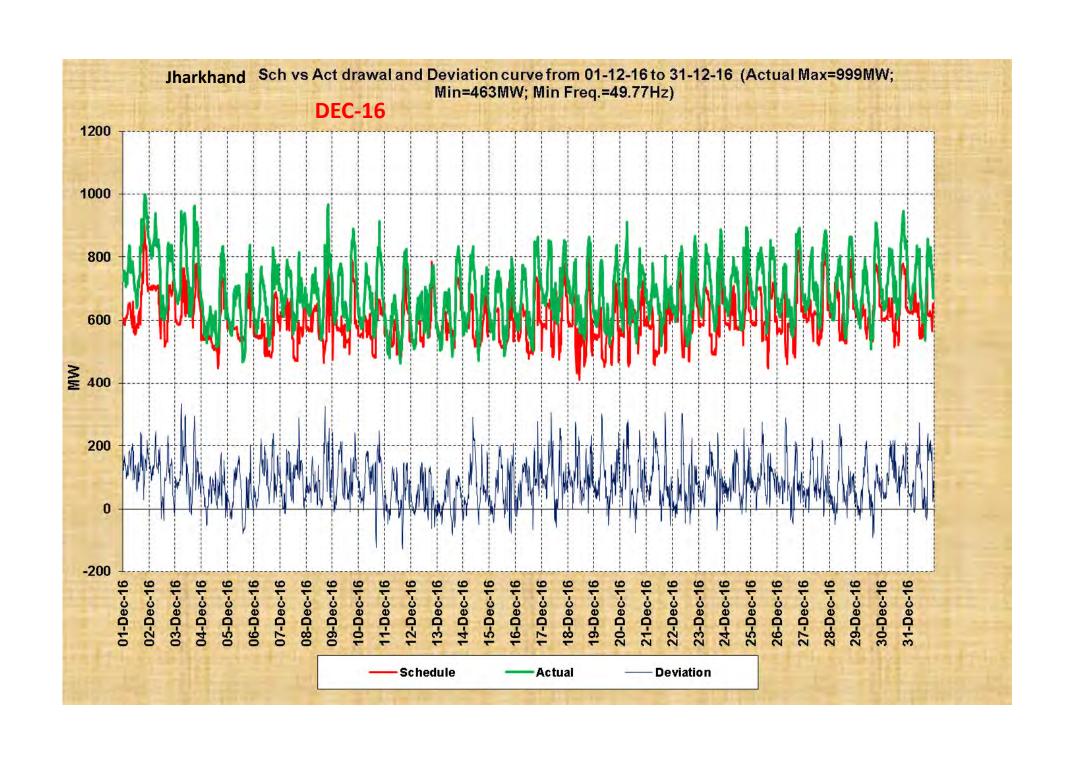

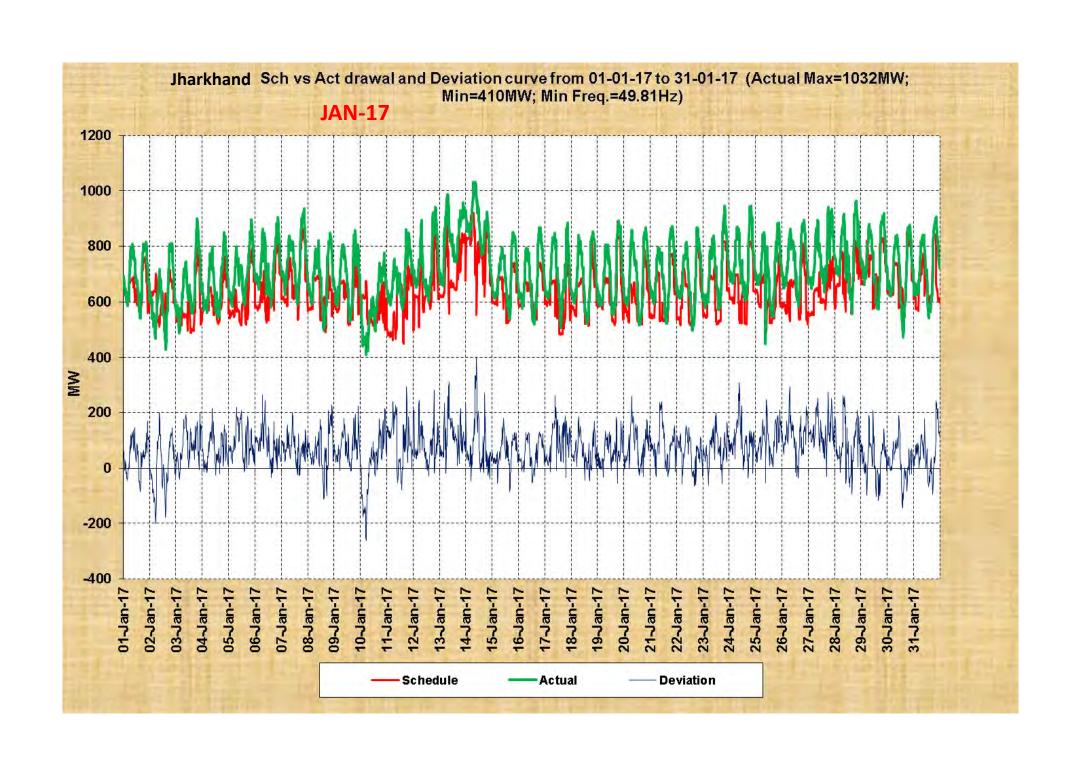

# Annexure-C1 Annexure-II


	Reporting Format to the PSDF Project Monito	ring Group
Name of the Scheme		
1.1 Name of the substation and its Location		
1.2 Executing Agency		
1.3 State/Region		
Date of Sanction order		
2.1 Date of Agreement of Entity with State (	Jovt/NLDC	
2.2 Total Approved Cost of the Scheme		
2.3 Approved Grant by Monitoring Committ	ee ( Rs. In Lakhs)	
2.4 Date of Requisition by the Entity		
2.4.a) date and Reference of LOA		
2.4.b) Amount of LOA		
2.5 Date of Disbursement and amount		
2.5.1 : Ist Installment		
2.5.2: IInd installment		
2.5.3: Illrd installment		
2.6 Date of Scheduled completion of Work		
2.7 Date of handing over of Site to entity (in	f. I i i	

No.	Supply Description	Qty. AS PER LOA	Quantity Received during Month	CUMMULATIVE PROGRESS Till date		BALANCE	Remarks
				Sch.	Act.	6000000	
1	item Details						
.1			-				
.2							
2	work details	LOA	During Month	TROOK	ESS Till date		
4.							
2.1						-	
2.2							
2.2	Others						

## Chronic issue with real time data availability in eastern region:-

> Frequent Failure of Purnea New real time data.

Percentage Non-Availability of real time data from Purnea 400 kV to ERLDC.



- > Another 31 days gone but JITPL and Lalmatia data yet be restored by JITPL and NTPC respectively.
- No redundant Communication channel in eastern region for real time telemetry over IEC 101, IEC 104 as well as over ICCP protocol

## No VOICE over VOIP

- **▶ IPP** : JITPL, GMR, IBEUL, TEESTA #3.
- ➤ POWERGRID: Bolangir, Indravati, Jeypore, Keonjhar, Purnea 400 kV, Purnea 220, Baharampur 400kV, Rourkella, Lakhisarai, Rengali, Keonjhor, Jeypore, Dalkhola (PG), Birpara, Kishanganj,Indravati (PG), Bolangir, Pandiabili.
- ►NTPC : Nabinagar.

# Building more confidence of Grid operator on SCADA data.

## Meeramundali MVAr data:

	Duburi New 1	Duburi New 2	Mendhasal	Angul 1	Angul 2	GMR	Talcher STPS	ICT 2	JSPL 1	JSPL 2	Sterlite 1	Sterlite 2	Residue
Site	-96	-98	19	100	126	14	18	85	-23	-25	-52	-52	16
OPTCL	-96	-92	57	182	126	25	20	85	-25	-30	5	-2	255
ERLDC	-96	-92	57	182	126	25	20	85	-25	-30	5	-2	255

➤ Data validation is required to be done on periodic basi.

## Non availability of Unit side data

- ▶ IBEUL (Unit 1, Unit 2)
- > Farakka Unit #6, Unit #5 (erroneous data).
- > Sagardighi Unit #3.
- > Teesta V HPS unit data.
- > Rangit HPS Unit Data.

## **OLTC**

- 1. NEW SASARAM @ 1500 MVA 765/400 kV ICT 1
- 2. ANGUL @ 1500 MVA 765/400 kV ICT 1
- 3. ANGUL @ 1500 MVA 765/400 kV ICT 3
- 4. ANGUL @ 1500 MVA 765/400 kV ICT 4
- 5. JHARSUGUDA @ 1500 MVA 765/400 kV ICT 1
- 6. JHARSUGUDA @ 1500 MVA 765/400 kV ICT 2
- 7. BOLANGIR @ 315 MVA 400/220 kV ICT 1
- 8. BIHARSHARIF @ 315 MVA 400/220 kV ICT 1
- BIHARSHARIF @ 315 MVA 400/220 kV ICT 3
- 10. INDRAVATI (2ND ICT) @ 315 MVA 400/220 kV ICT 1
- 11. INDRAVATI (2ND ICT) @ 315 MVA 400/220 kV ICT 2
- 12. KEONJHAR @ 315 MVA 400/220 kV ICT 1
- 13. KEONJHAR @ 315 MVA 400/220 kV ICT 2
- 14. MALDA @ 315 MVA 400/220 kV ICT 1
- 15. MUZAFFARPUR @ 315 MVA 400/220 kV ICT 3
- 16. RANCHI @ 315 MVA 400/220 kV ICT 1

## **OLTC**

- 19. RANCHI @ 315 MVA 400/220 kV ICT 2
- 20. RENGALI @ 315 MVA 400/220 kV ICT 2
- 21. ROURKELA @ 315 MVA 400/220 kV ICT 3
- 22. CHAIBASA @ 315 MVA 400/220 kV ICT 1
- 23. CHAIBASA @ 315 MVA 400/220 kV ICT 2
- 24. CHAIBASA @ 315 MVA 400/220 kV ICT 3
- 25. SUBHASGRAM (ICT I, II & V) @ 315 MVA 400/220 kV ICT3
- 26. KISHANGUNJ @ 500 MVA 400/220 kV ICT 2
- 27. KISHANGUNI @ 500 MVA 400/220 kV ICT 3
- 28. BARH @ 200 MVA 400/132 kV ICT 1
- 29. BARH @ 200 MVA 400/132 kV ICT 2
- 30. LAKHISARAI @ 200 MVA 400/132 kV ICT 3
- 31. ARRAH @ 100 MVA 220/132 kV ICT 1
- 32. ARRAH @ 100 MVA 220/132 kV ICT 2
- 33. PURNEA @ 160 MVA 220/132 kV ICT 1
- 34. PURNEA @ 160 MVA 220/132 kV ICT 2

## NTPC

- Lalmatia: ( No data since Jan 2016).
- Farakka NTPC:
  - ➤ Unit #5 MW and MVAr data not matching with site data (As per inputs from NTPC, This will be done during overhauling of Unit#5)
  - ➤Unit # 6 LV side not available.
- ▶ Nabinagar NTPC :
  - > Alternet Data channel not provided.
  - ►Unit HV side data.
  - ≻No VOIP.

## **POWERGRID**

- > Data Intermittent / not available:
  - Purnea 400kV (Frequent Failure of RTU)
  - Ranchi 400kV, Baripada, Gaya, Angul, Chaibasa
- > VOIP for following station not yet provided:
  - ➤ Bolangir , Indravati , Jeypore , Keonjhar

## **WBSETCL**

- Following station data not available:
  - >TLDP 4.
  - ➤ Gokarna 400kV (400/220 kV ICT was first charged on 15th Sept'16),
  - ➤ Dharampur 220,
  - ≻Krishnanagar 220,
  - ► Hura 220,
  - Foundry Park 220.
  - ▶ Dalkhola
  - **≻**Bantala
  - Lakshmikantapur
  - ➤ New Town
- Sagardighi :
  - ➤ Unit 3 LV side (Unit) data not available.
- Kolaghat TPS: Kharagpur #1 MW/MVAR flow not available.

## **BSPHCL**

- ➤ Data Intermittent / not available:
  - Dumraon, Sonenagar, Khagaul ,Darbhanga, Dehri, sultangaunj, Lakhisarai, Karmanasa, Kahalgaon, Jamaui, Banka, Gopalganj, Kisanganj, Arrah, Rajgir, Sipara, Hajipur (New), Pusauli, Valmikinagar, Koshi

## **JSUNL**

- Data Intermittent / not available:
  - Hatia New 220,
  - > Dumka 220.
  - Patratu(Intermittent)
  - DEOGHAR
  - > DUMKA
  - ▶ GARHW
  - GOELKERA
  - > JAMTARA
  - > JAPLA
  - KENDOPOSI

## DVC

- ▶ Data Not provided:
  - ►Giridhi 220,
- Durgapur TPS (DSTPS): Highly intermittent.

#### **SUMMARY OF DEVIATION CHARGE RECEIPT AND PAYMENT STATUS**

#### BILL from 28.03.16 to 15.01.17 (upto Week - 42 of 2016 - 17) Last Payment Disbursement Date -06.02.17

Figures in Rs. Lakhs

CONSTITUENTS	Receivable	Received	Payable	Paid	Outstanding
WR	18945.83570	15811.18729	19599.07787	18811.73327	2347.30381
SR	1945.76835	2007.72646	23225.74713	21150.55211	-2137.15314
NER	63096.40148	65502.27270	8914.27578	4893.70576	-6426.44124
NR	5857.93007	1034.56935	55033.92138	53647.63389	3437.07323
BSPHCL	7561.70870	5169.10465	985.21941	0.00000	1407.38464
JSEB	8010.47974	3396.15457	452.33933	0.00000	4161.98584
DVC	1154.07523	1178.91245	2024.12651	2025.94398	-23.01975
GRIDCO	1875.01522	1879.33318	1756.60024	1707.72168	-53.19652
WBSETCL	7637.54908	7509.02958	293.29540	562.41588	397.63998
SIKKIM	43.59053	0.00000	1181.43602	1127.85538	-9.99011
NTPC	9187.65294	9131.16590	0.00000	3.67096	60.15800
NHPC	0.00000	0.00000	1744.87050	1731.78504	-13.08546
MPL	44.45104	44.45104	776.45449	761.95433	-14.50016
STERLITE	5050.74588	5050.74578	0.16892	0.16882	0.00000
APNRL	417.02909	219.63563	239.15938	0.00000	-41.76592
CHUZACHEN (GATI)	24.03633	24.03633	496.40362	495.88149	-0.52213
NVVN (IND-BNG)	360.13993	357.99741	94.81568	95.81574	3.14258
JITPL	1089.74945	1090.24160	1068.93820	1038.44005	-30.99030
GMR	333.01621	321.59716	1202.70596	1202.70596	11.41905
IND BARATH	89.32950	76.47458	443.91325	432.14046	1.08213
TPTCL(DAGACHU)	1217.59576	1203.83791	69.71771	78.03065	22.07079
JLHEP (DANS ENERGY)	331.01994	306.08875	151.80440	133.30605	6.43284
BRBCL(NABINAGAR)	194.44901	218.24747	1000.92121	610.76237	-413.95730
NVVN (IND-NEPAL)	404.60514	410.16777	59.23818	79.55593	14.75512
HVDC SASARAM	1.60348	1.60348	20.72042	19.65339	-1.06703
KBUNL	29.18928	25.15868	0.00000	0.00000	4.03060
TEESTA-III(TUL)	0.00000	0.00000	0.00000	0.00000	0.00000
Pool Balance	0.00000	0.00000	-190.83260	0.00000	190.83260
Addl Deviation charge	9261.11594	14611.28008	0.00000	0.00000	-5350.16414
IRE	0.00000	0.00000	441.60109	0.00000	-441.60109
VAE	0.00000	0.00000	4554.93355	0.00000	-4554.93355
TOTAL	134902.96708	121969.73972	125641.57303	110611.43319	

% Realization
Receivable by ER POOL
Received by ER POOL

90.41 Payable

Paid

As on

**07.02.17**Payable by ER POOL
Paid by ER POOL

Receivable:

Received

<sup>&</sup>quot;- ve" Payable by ER pool

<sup>&</sup>quot;+ ve" Receivable by ER pool

## STATUS OF REACTIVE CHARGES

## RECEIVABLE IN ER POOL AS PER PUBLISHED A/C UPTO 15.01.17 (2016 -17) AS ON 07.02.2017

CONSTITUENT	AMOUNT RECEIVABLE	AMOUNT RECEIVED	OUTSTANDING
	IN THE POOL (Rs.)	IN THE POOL (Rs.)	(Rs.)
BSPHCL	93587	0	93587
JSEB	0	0	0
DVC	0	0	0
GRIDCO	39469035	35786551	3682484
WBSETCL	195794216	163498985	32295231
SIKKIM	0	0	0
TOTAL	235356838	199285536	36071302

Note: (+ve) means payable by utility & (-ve) means receivable by utility

#### SUMMARY OF RRAS CHARGE RECEIPT AND PAYMENT STATUS

## BILL from 18.04.16 to 15.01.17 (upto Week - 42 of 2016 - 17) Last Payment Disbursement Date -07.02.17

Figures in Rs. Lakhs

CONSTITUENTS	Receivable	Received	Payable	Paid	Outstanding
FSTPP STG-I	220.51369	220.51369	3446.68584	3446.09651	-0.58933
FSTPP STG-II	45.46118	44.71118	599.64887	599.64887	0.75000
KhSTPP STG-I	173.72258	171.01295	1604.50088	1604.41716	2.62591
KhSTPP STG-II	77.11902	77.11902	5204.16558	5203.76097	-0.40460
TSTPP STG-I	121.13318	121.13318	377.24070	375.87592	-1.36478
BARH STG-I	0.00000	0.00000	0.00000	0.00000	0.00000
BARH STG-II	270.57348	270.39444	3263.68011	3263.23386	0.73279
NTPC TOTAL	908.52312	905.63444	14495.92197	14493.03325	-0.00004
RANGIT	0.00000	0.00000	0.00000	0.00000	0.00000
TEESTA-V	0.00000	0.00000	0.00000	0.00000	0.00000
NHPC TOTAL	0.00000	0.00000	0.00000	0.00000	0.00000
TOTAL	908.52312	905.63444	14495.92197	14493.03325	-0.00004

#### SUMMARY OF CONGESTION CHARGE RECEIPT AND PAYMENT STATUS

## Bill upto 07.01.2013 Last Payment Disbursement Date - 13.05.2013

Figures in Rs. Lakhs

CONSTITUENTS	Receivable	Received	Payable	Paid	Outstanding
BSEB	0.67823	0.67823	0.39118	0.39118	0.00000
JSEB	16.37889	16.37889	2.61323	2.61323	0.00000
DVC	0.00000	0.00000	6.24040	6.24040	0.00000
GRIDCO	5.34488	5.34488	0.00000	0.00000	0.00000
WBSETCL	0.00000	7.42249	4.32834	11.75083	0.00000
SIKKIM	0.65609	6.20909	0.00000	5.55300	0.00000
NTPC	6.93152	6.93152	7.42249	7.42249	0.00000
NHPC	0.70445	0.70445	0.05875	0.05875	0.00000
MPL	4.81694	4.81694	0.85169	0.85169	0.00000
STERLITE	7.70504	7.70504	0.00000	0.00000	0.00000
Pool Balance	0.00000	0.00000	21.30996	21.30996	0.00000
TOTAL	43.21604	56.19153	43.21604	56.19153	0.00000

% Realization As on 31.05.2015

Receivable: Receivable by ER POOL Payable Payable by ER POOL Paid Paid by ER POOL

#### **ANNEXURE-C10.5**

### DETAILS OF DISBURSEMENT TO POWER SYSTEM DEVELOPMENT FUND

		Amount transferred	Date of		
SI No	Nature of Amount	to PSDF (Rs in Lac)	Disbursement	Cheque No	Remarks
1	Opening Balance (upto 31.12.15)	83873.87922			
2	Addl. Dev	18.40442	01.01.16		Addl Dev Charge 15-16
3	Addl. Dev	16.46976	05.01.16		Addl Dev Charge 15-16
4	Addl. Dev	33.27577	07.01.16		Addl Dev Charge 15-16
5	Addl. Dev	19.11532	11.01.16		Addl Dev Charge 15-16
6	Addl. Dev	90.94357	14.01.16		Addl Dev Charge 15-16
7	Addl. Dev	19.04467	18.01.16		Addl Dev Charge 15-16
8	Addl. Dev	50.72543	20.01.16		Addl Dev Charge 15-16
9	Addl. Dev	11.10228	22.01.16		Addl Dev Charge 15-16
10	Addl. Dev	45.43206	27.01.16		Addl Dev Charge 15-16
11	Addl. Dev	96.62204	29.01.16		Addl Dev Charge 15-16
12	Reactive Charge	450.00000	02.02.16		Reactive Energy Charge_15-16
13	Addl. Dev	69.01901	04.02.16		Addl Dev Charge 15-16
14	Addl. Dev	45.99429	11.02.16		Addl Dev Charge 15-16
15	Addl. Dev	50.44878	15.02.16		Addl Dev Charge 15-16
16	Addl. Dev	371.30972	17.02.16		Addl Dev Charge 15-16
17	Addl. Dev	91.04585	22.02.16		Addl Dev Charge 15-16
18	Addl. Dev	121.28575	24.02.16		Addl Dev Charge 15-16
19	Addl. Dev	40.83267	29.02.16		Addl Dev Charge 15-16
20	Addl. Dev	61.45400	02.03.16		Addl Dev Charge 15-16
21	Addl. Dev	16.51444	04.03.16		Addl Dev Charge 15-16
22	Addl. Dev	142.93695	09.03.16		Addl Dev Charge 15-16
23	Addl. Dev	55.54777	15.03.16		Addl Dev Charge 15-16
24	Addl. Dev	85.71223	17.03.16		Addl Dev Charge 15-16
25	Addl. Dev	58.13810	21.03.16		Addl Dev Charge 15-16
26	Addl. Dev	253.40681	23.03.16		Addl Dev Charge 15-16
27	Addl. Dev	25.92020	28.03.16		Addl Dev Charge 15-16
28	Reactive Charges	250.00000	28.03.16		Reactive Charges_15-16
29	Addl. Dev	83.33978	01.04.16		Addl Dev Charge 15-16
30	Addl. Dev	43.77416	05.04.16		Addl Dev Charge 15-16
31	Addl. Dev	31.83984	07.04.16		Addl Dev Charge 15-16
32	Addl. Dev	52.08622	11.04.16		Addl Dev Charge 15-16
33	Addl. Dev	107.23773	13.04.16		Addl Dev Charge 15-16
34	Addl. Dev	220.15330	19.04.16		Addl Dev Charge 15-16
35	Addl. Dev	76.84824	21.04.16		Addl Dev Charge 15-16
36	Addl. Dev	20.84026			DSM Interest 2014-15(Paid by APNRL)
37	Addl. Dev	10.01920	26.04.16		Addl Dev Charge 16-17
43	Addl. Dev	432.25696			Addl Dev Charge 16-17
44	Addl. Dev	117.08707	02.05.16		Addl Dev Charge 16-17
45	Addl. Dev	41.65418	04.05.16		Addl Dev Charge 16-17
46	Addl. Dev	114.33049			Addl Dev Charge 15-16 & 16-17
47	Deviation Interest	38.50018			Deviation Interest
48	Addl. Dev	35.54178			Addl Dev Charge 16-17
49	Addl. Dev	448.87953	31.05.16		Addl Dev Charge 16-17
50	Addl. Dev	170.51274	29.06.16		Addl Dev Charge 16-17
51	Reactive Charges	530.57497	28.09.16		Reactive Charges_15-16
274	Reactive Charges	1000.00000	26.12.16		Reactive Charges_16-17
	Total	90040.05774			

**Annexure-C11.1** 

## **Status of Reconciliation of Deviation Pool Account**

		2015	5-16	2016-17			
			_				
Name of The Utility	Q1 (01.07.15)	Q2(05.10.15)	Q3(05.01.16)	Q4(05.04.16)	Q1 (04.07.16)	Q2 (03.10.16)	Q3 (04.01.17)
Inter Regional							
WR	YES	NO	YES	YES	YES	YES	YES
SR	YES	YES	YES	YES	YES	YES	NO
NER	NO	NO	YES	YES	YES	YES	YES
NR	NO	NO	NO	NO	NO	NO	NO
	Intra R	egional					
BSPHCL	YES	YES	YES	YES	YES	YES	YES
JUVNL	NO	NO	NO	NO	NO	NO	NO
DVC	YES	YES	YES	YES	YES	YES	NO
GRIDCO	YES	YES	YES	YES	YES	YES	YES
WBSETCL	YES	YES	YES	YES	YES	YES	YES
SIKKIM	YES	YES	YES	YES	NO	NO	NO
NTPC	YES	YES	YES	YES	YES	YES	YES
NHPC	YES	YES	YES	YES	YES	YES	YES
MPL	YES	YES	YES	YES	YES	YES	YES
VEDANTA	YES	YES	YES	YES	NO	NO	NO
APNRL	YES	YES	YES	YES	YES	YES	NO
CHUZACHEN(GATI)	YES	YES	YES	YES	NO	NO	NO
NVVN(Ind-Bng)	YES	YES	YES	YES	YES	YES	YES
NVVN(Ind-Nep)	N/A	N/A	N/A	N/A	YES	YES	YES
GMR	YES	YES	YES	YES	YES	YES	NO
JITPL	YES	YES	YES	YES	YES	YES	YES
INBEUL	NO	NO	NO	NO	NO	NO	NO
TPTCL (DAGACHU)	YES	YES	YES	YES	YES	YES	YES
JLHEP(DANS ENERGY)	N/A	N/A	YES	YES	NO	NO	NO
POWERGRID	N/A	N/A	N/A	N/A	N/A	N/A	YES

Note:

<sup>(1)</sup>The dates in the bracket indicates the date of sending the Reconciliation statements by ERLDC to utilities.

<sup>(2)</sup> YES Indicates that signed reconciliation statement received by ERLDC

<sup>(3)</sup> NO Indicates that signed reconciliation statement is not received by ERLDC

## Annexure- C11.4

	Reconciliation Between Open Access department of ERLDC and SLDCs, STUs										
Sl. No.	STUs / SLDCs Name	Apr-16	May-16	Jun-16	Jul-16	Aug-16	Sep-16	Oct-16	Nov-16	Dec-16	
	Date of Issuance	13-May-16	14-Jun-16	13-Jul-16	17-Aug-16	16-Sep-16	14-Oct-16	16-Nov-16	15-Dec-16	12-Jan-17	
1	West Bengal - SLDC and STU	YES	YES	YES	YES	YES	YES	YES	YES	NO	
2	DVC - SLDC	Not Applicable	YES	Not Applicable							
3	OPTCL-SLDC and STU	YES	YES	YES	YES	YES	YES	YES	YES	NO	

SI. No.	Applicants Name	Quarter-I (Apr-16-	Quarter-II	Quarter-III
31. 140.	Applicants Name	June-16)	(Jul-16-Sep-16)	(Oct-16-Dec-16
	Date of Issuance	14-07-2016	18-10-2016	13.01.17
1	Calcutta Electric Supply Company	YES	YES	NO
2	Damodar Valley Corporation	YES	NA	NA
3	GMR Kamalanga Energy Limited	YES	YES	NO
4	Jindal India Thermal Power Limited	YES	YES	NO
5	Jharkhand State Electricity Board	NO	NO	NO
6	SAIL Rourkela Steel Plant	YES	NO	NO
7	TATA Steel - Discom	NA	NO	YES
8	TATA Steel Ferro Alloy Plant Bamnipal	YES	YES	YES
9	TATA Steel Ferro Alloy Plant Joda	NA	NA	YES
10	Tata Steel Limited Kalinganagar	NA	YES	YES
11	West Bengal State Distribution Company Ltd.	YES	NA	NA

Reconcil	Reconciliation Between Open Access department of ERLDC and CTU									
SI. No.	STUs / SLDCs Name	Apr-16	May-16	Jun-16	Jul-16	Aug-16	Sep-16	Oct-16	Nov-16	Dec-16
	Date of Issuance	13-May-16	14-Jun-16	13-Jul-16	17-Aug-16	16-Sep-16	14-Oct-16	16-Nov-16	15-Dec-16	12-Jan-17
1	CTU(POWERGRID)	YES								



## Assam Power Distribution Company Limited Bijulee Bhawan ::: Paltanbazar ::: Guwahati-781001

Annexure- C14
Fax no. 0361 - 2739501
F-mailacccomtageba rediffmail.com

BY SPEED POST

No. APDCL/ CGM (COM)/ ACC-0/ PT-9/ 2007/ 9

Dated 07.10.2016.

To.

The Chief Engineer (Commercial),
Bihar State Electricity Board, (Holding Company)
Vidyut Bhawan, Baily Road, Patna-800021.

Sub: Outstanding Dues Payable by BSEB on account of drawl of NER Power during July' 1993 to April' 1994.

Ref: This Office Earlier Letter No. ACE (COM)/ACC-0/PT-8/2003/133 dated 09.08.2012.

Sir.

I am to intimate you that under the period of bilateral transaction of power, between erstwhile ASEB (now APDCL) and erstwhile EREB (now ERPC) for above mentioned period, BSEB drew power from ASEB from time to time. Billing was accordingly done by then ASEB on the basis of monthly Regional Energy Accounting prepared by then EREB. Accordingly payments were being made by BSEB at initial period. But during later stage BSEB had failed in timely payment and thus there remains an outstanding arrear unpaid. The details thereof with accumulated surcharge are shown below:

TOTAL	₹ 6.74.93.833.00
Surcharge as on 31.08.2016	₹ 5,66,93,230.00
Principal outstanding	₹ 1,08,00,603.00

Details of calculations are furnished as **Annexure A.** It may kindly be noted that the above outstanding is of pre-reforms period and long pending. We are sending our reminders from time to time but there is no response from your side. The power which BSEB had consumed, was from the ASEB's share out of its allocations from central sector generating agencies of NER and as such it created liabilities for ASEB. You would also appreciate that being APDCL a successor agency, the burden has come to APDCL as a pass through items.

Under the circumstances you are once again requested kindly to liquidate the bill amount within the due date of payment without any further delay.

Your early response is awaited.

Yours faithfully,

Chief General Manager (Commercial) APDCL, Bijulee Bhawan, Guwahati-1.

Memo No. APDCL/ CGM (COM)/ACC-0/PT-9/ 2007/ (A)

Dated 07.10.2016.

Copy for information and necessary action to:

- The Chairman, Bihar State Electricity Board, Vidyut Bhavan, Baily Road, Patna-800021.-He is requested kindly to look into the matter and take necessary steps to liquidate the outstanding amount.
- 2. The Member Secretary, Eastern Regional Power Committee, 14, Golf Club Road, Tollygunge, Kolkata-700033.

3. The Chief General Manager (F&A), APDCL.

Chief General Manager (Commercial) APDCL, Bijulee Bhawan, Guwahati-1.



Assam Power Distribution Company Limited Bijulee Bhawan ::: Paltanbazar ::: Guwahati-781001

Fax no. 0361 - 2739501 E-mailacecomt.aseb@rediffmail.com

## INVOICE

To

The Chief Engineer (Commercial) Bihar State Electricity Board, Vidyut Bhawan, Baily Road, Patna-800021.

Bill No. ACE (COM)/ACC-0/BSEB/BILL-21

Dated 07.10.2016.

1. Amount of Principal Outstanding

= Rs.1,08,00,603.00.

Rate of Late Payment Surcharge

= 2 % per month.

3. Surcharge already claimed up to March' 2012

= Rs. 4,52,38,081.00.

4. Period of Surcharge from April'2012 to August' 2016

= 1613 Days.

5. Surcharge for 1613 days up to August' 2016

=Rs.1,14,55,149.00.

6. Total Surcharge up to 31st August' 2016

= Rs. 5,66,93,230.00.

7. Total Outstanding with Principal up to March'10

= Rs. 6,74,93,833.00.

(Rupees Six Crore seventy four Lakh Ninety three Thousand Eight Hundred and Thirty Three only)

Due Date of Payment:

06.11.2016.

75

Chief General Manager (Commercial), APDCL, Bijulee Bhawan, Paltanbazar, Guwahati-1.



PTC/MTFG/ERLDC/ 11428

To,
Member Secretary,
ERPC, 14 Golf Club, Road,
Kolkata – 700 033
(Fax No. 033 – 24221802).
E-mail: mserpc-power@nic.in

Subject: Billing on account of Re-import of Kurichhu Energy by Royal Govt. of Bhutan through Assam Grid for the period from December 2014 onwards - APDCL letter regarding.

Dear Sir,

PTC is in receipt of letter from Assam Power Distribution Company Limited (APDCL) vide letter no. APDCL/CGM (Com)/ CERC-RGoB/2015 /13 dated 23<sup>rd</sup> September 2016 regarding the said subject wherein APDCL has requested to arrange a joint meeting of all the concerned stakeholders to find out an amicable billing methodology so that APDCL does not suffer any financial loss for supply of power to Bhutan from December 2014 onwards. The copy of the same has been marked to you also.

We request you to kindly arrange for a joint meeting as requested by APDCL.

Thanking you,

Yours faithfully,

Harish Saran Executive Director (Marketing)

CC:

Chief General Manager (Commercial)
Assam Power Distribution Company Limited,
5<sup>th</sup> Floor, Bijulee Bhawan, Paltan Bazar,
Guwahati, Assam – 781 001
Fax: 0361 – 2739543



## Assam Power Distribution Company Limited Bijulee Bhawan ::: Paltanbazar ::: Guwahati-781001

Fax no. 0361 - 273950] E-mailacecoust, aseb@rediffmail.com

No. APDCL/ CGM (COM)/ CERC-RGOB/ 2015/ 13

dated 23.09.2016.

To,

- The Member Secretary,
   Eastern Regional Power Committee,
   Golf Club Road, Tollygunge, Kolkata-700033.
- Executive Director (Marketing),
   PTC India Limited, 2<sup>ND</sup> Floor, NBCC Tower,
   Bhikaji Cama Place, New Delhi 110066.

Sub: Billing on account of Re-import of Kurichhu Energy by Royal Govt.

Bhutan through Assam Grid for the period from December' 2014 onwards.

Ref: Letter No. APDCL/ CGM (COM)/ CERC-RGOB/ 2015/ 11 Dated 01.07.2016.

Sir,

On the basis of the CERC order dated 13.06.2016 in APDCL Petition No. 150 MP/2015, APDCL has submitted the Energy Bill of \$\frac{7}{2}\$,13,84,866.00 on account of r import of Kurichhu energy by Bhutan for the period from April' 2003 November'2014 for favour of necessary payment from your end. However, though the bill enclosed in our Petition was up to November' 2014, but APDCL has been continuing supply of energy to Bhutan on the basis of existing PPA signed with PTC the interest of all concerned. But the CERC order is silent in the methodology of billing for subsequent period from December' 2014 onwards. Meanwhile, the DSM rate alcomes down drastically with the improvement of average frequency within the range 50 Hz; as a result there is little chance of recovery of cost of energy.

Being ERPC is the accounting authority and nodal agency, this issue for the earlier period from April' 2003 to November' 2014 is settled under your guidance at with the active participation of all stakeholders like NERPC, NERLDC, ERLDC, PT etc.

Likewise, you are again requested kindly to arrange another joint meeting of a concerned stakeholders in this case to find out an amicable billing methodology that APDCL does not suffer any financial loss in this regard.

Yours faithfu

1

Chief General Manager (Commercia

hase : 33	Locations		S.No	ERLDC ID	OLD MTR NEW MTR	LOCATION	S.No	ERLDC ID	OLD MTR	NEW MTR	LOCATION
1	BALIMELA(BLM)	GRIDCO	1	AP-03	NP-7438-A NP-8642-A	APNRL	109	EN-51	-	NP-7887-A	LAKHISARAI(PG)
2	BANGRIPOSHI(BGR)	GRIDCO	2	AP-02	NP-7462-A NP-8643-A	APNRL	110	EN-52		NP-7430-A	LAKHISARAI(PG)
3	BANKA(BNK)	PG	3	EN-93	NP-8742-A	ARA(PG)	111	EN-89		NP-7887-A	LAKHISARAI(PG)
4	CHAIBASA(CHB)	PG	4	EN-94	NP-8743-A	ARA(PG)	112	EN-90		NP-7430-A	LAKHISARAI(PG)
5	CHAIBASA(CHA)	JUVNL	5	ES-02	NP-8860-A	ARA(PG)	113	EN-51		NP-7888-A	LAKHISARAI(PG)
6	DUMKA(DUM)	JUVNL	6	ES-22	NP-8790-A	BOLANGIR(PG)	114	EN-52		NP-7431-A	LAKHISARAI(PG)
7	DARBHANGA(DBG)	DMTCL	7	ES-23	NP-8789-A	BOLANGIR(PG)	115	OR-23		NP-7915-A	DUBURI(GRIDCO)
8	GYALSHING(GSH)	SIKKIM	8	EP-99	NP-7560-A	BOLANGIR(PG)	116	JS-09		NP-8695-A	DUMKA(JUVNL)
9	HALDIA(HAL)	WBSETCL	9	ES-27	NP-8775-A	MALDA(PG)	117	JS-09 JS-10		NP-8774-A	DUMKA(JUVNL)
10	IND-BARATH (IBR)	IPPR	10	ES-28	NP-8776-A	MALDA(PG)	118	SM-07		NP-8730-A	GYALSHING(SIKKIN
11	JAMUI(JMU)	BIHAR	11	EN-87	NP-8727-A	MAITHON(PG)	119	WB-60		LT-0307-A	
12	( /	IPPR			NP-8739-A	- ( - /	120	WB-61		LT-0307-A LT-0311-A	HALDIA CESC(WB)
	JLHEP(DANS ENERGY)	PG	12	EN-88 ES-42		MAITHON(PG) MAITHON(PG)	121				HALDIA CESC(WB
13 14	KISANGANJ (KSN)  KATAPALLI(KTP)	GRIDCO	13 14	ES-42 ES-01	NP-7401-A NP-8874-A	MUZAFFARPUR(PG)	122	OR-15 OR-16		NP-7991-A NP-7992-A	BALIMELA(GRIDCO BALIMELA(GRIDCO
15	KUDRA(KUD)	BIHAR		ES-07	NP-8871-A	. ,	123	OR-16 OR-62		NP-7992-A NP-5907-A	BANGRIPOSHI(GRIDO
	` ′		15			MUZAFFARPUR(PG)					
16	KISANGANJ (KIS)	BSPTCL	16	ES-08	NP-8873-A	MUZAFFARPUR(PG)	124	NB-01		NP-8700-A	NABINAGAR
17	LAKHISARAI(LKS)	PG	17	ES-09	NP-8872-A	MUZAFFARPUR(PG)	125	NB-02		NP-8701-A	NABINAGAR
18	LAKHISARAI(LKK)	BIHAR	18	ES-43	NP-6077-A	MUZAFFARPUR(PG)	126	NB-05		NP-8662-A	NABINAGAR
19	NABINAGAR(NBN)	NTPC	19	ES-44	NP-6078-A	MUZAFFARPUR(PG)	127	NB-07		NP-8892-A	NABINAGAR
20	NEW DUBRI (DBR)	GRIDCO	20	OR-20	NP-5983-A NP-7498-A	MENDHASAL(GRIDCO)	128	NB-11		NP-8891-A	NABINAGAR
21	NEW PUSAULI (NPS)	BIHAR	21	BI-72	NP-8748-A	BANKA(BSPTCL)	129	BI-56		NP-7690-A	NALANDA(BSPTCL
22	NALANDA(NLN)	BIHAR	22	ES-40	NP-8692-A	PUSAULI(PG)	130	OR-22		NP-7916-A	NEW DUBURI(GRIDO
23	NEW MELLI (NML)	PG	23	ES-41	NP-8693-A	PUSAULI(PG)	131	EN-85		NP-8647-A	NEW MELLI(PG)
24	PANDIABILPNB)	PG	24	EN-83	NP-8673-A	BANKA(PG)	132	EN-86		NP-8640-A	NEW MELLI(PG)
25	RANCHI NEW(RNC)	PG	25	EN-84	NP-8675-A	BANKA(PG)	133	ES-51		NR-4621-A	NEW MELLI(PG)
26	SADIEPALI(SDP)	GRIDCO	26	ES-03	NP-8694-A	BANKA(PG)	134	ES-52		NR-4620-A	NEW MELLI(PG)
27	RANGPO(RGP)	PG	27	ES-04	NP-8696-A	BANKA(PG)	135	BI-27		NP-8698-A	JAMUI(BSPHCL)
28	SAGBARI(SGB)	SIKKIM	28	BH-22	NP-7482-A	BARH(NTPC)	136	BI-26		NP-8669-A	JAMUI(BSPHCL)
29	TEEST-III(TST)	TUL	29	ES-45	NP-8074-A	BARIPADA(PG)	137	BI-27		NP-8668-A	JAMUI(BSPHCL)
30	TALCHER SOLAR (TLS)	NTPC	30	EN-68	NP-8721-A	BERHAMPORE(PG)	138	JL-01		NP-8737-A	JORETHANG(JLHE
31	DIKCHU(DIC)	DICKCHU	31	EN-69	NP-8726-A	BERHAMPORE(PG)	139	JL-02		NP-8766-A	JORETHANG(JLHE
32	SONNAGAR NEW(SONN)	BSPTCL	32	ES-10	NP-8655-A	PATNA(PG)	140	JL-03		NP-8762-A	JORETHANG(JLHE
33	ALIPURDUAR	PG	33	RG-12	NP-8734-A	RANGIT(NHPC)	141	JL-04		NP-8763-A	JORETHANG(JLHEI
34	MTPS KANTI(NTPC)	NTPC	34	RG-13	NP-8733-A	RANGIT(NHPC)	142	JL-05		NP-8764-A	JORETHANG(JLHE
35	KEONJHAR(KEO)	GRIDCO	35	RG-14	NP-8732-A	RANGIT(NHPC)	143	JL-06		NP-8765-A	JORETHANG(JLHE
36	ATRI(ATR)	GRIDCO	36	RG-15	NP-8736-A	RANGIT(NHPC)	144	OR-17		NP-7561-A	KATAPALI(GRIDCO
37	PURI(PUR)	GRIDCO	37	RG-16	NP-8735-A	RANGIT(NHPC)	145	BI-32		NP-8664-A	PUSAULI NEW(BSPH
			38	OR-55	NP-0624-B NP-5938-A	JODA(GRIDCO)	146	BI-33		NP-8665-A	PUSAULI NEW(BSPH
			39	EN-29	NP-7950-A	ANGUL(PG)	147	EN-10		NP-7847-A	RANCHI NEW(PG)
			40	EN-30	NP-7558-A	ANGUL(PG)	148	EN-11		NP-7876-A	RANCHI NEW(PG)
			41	EN-31	NP-7987-A	ANGUL(PG)	149	EN-12		NP-7849-A	RANCHI NEW(PG)
			42	EN-32	NP-7988-A	ANGUL(PG)	150	EN-13		NP-7866-A	RANCHI NEW(PG)
			43	EN-43	NP-7629-A	ANGUL(PG)	151	EN-14		NP-7865-A	RANCHI NEW(PG)
			44	EN-44	NP-7949-A	ANGUL(PG)	152	EN-19		NP-7875-A	RANCHI NEW(PG)
			45	EN-32	NP-7988-A NP-7908-A	ANGUL(PG)	153	EN-91		NP-8755-A	RANCHI NEW(PG
			46	EN-63	NP-8780-A	ANGUL(PG)	154	EN-92		NP-8754-A	RANCHI NEW(PG
			47	EN-64	NP-8781-A	ANGUL(PG)	155	EN-99		NP-8753-A	RANCHI NEW(PG
			48	EN-65	NP-8785-A	ANGUL(PG)	156	ES-46		NP-7013-A	KISHANAGNJ(PG
			49	EN-66	NP-8786-A	ANGUL(PG)	157	ES-47		NR-4614-A	KISHANAGNJ(PG
			50	EN-77	NP-8778-A	ANGUL(PG)	158	ES-48		NR-4444-A	KISHANAGNJ(PG
			51	EN-77	ND 0770 A	ANGUL (DO)	150	E0.40		ND 4400 A	I COLUMNIA ON LICE
			52	EN-76	NP-8779-A NP-8777-A	ANGUL(PG) ANGUL(PG)	160	ES-49 ES-50		NR-4436-A NR-4440-A	KISHANAGNJ(PG KISHANAGNJ(PG
			53		NP-8788-A	ANGUL(PG) ANGUL(PG)		-		NP-8887-A	KISHANGANJ(PG
				ES-06		ANGUL(PG) ANGUL(PG)	161	ES-11			
			54	ES-05	NP-8787-A NP-7995-A		162	ES-12		NP-8885-A	KISHANGANJ(PG
			55	ES-58	NP-8077-A	ANGUL(PG)	163	ES-13		NP-8856-A	KISHANGANJ(PG
			56	ES-59	NP-8076-A	ANGUL(PG)	164	ES-14		NP-8886-A	KISHANGANJ(PG
			57	EM-49	NP-7880-A NP-7471-A NP-8660-A	CHANDIL(JUVNL)	165	ES-15		NP-8858-A	KISHANGAN (PG
			58 59	EP-18 ES-26	NP-7471-A NP-8660-A NP-8659-A	GAYA(PG) GAYA(PG)	166 167	ES-16 ES-17		NP-8889-A NP-8859-A	KISHANGANJ(PG KISHANGANJ(PG
			1 59	E3-20	INC-0009-A	GATA(FG)	107	E3-17		HNC-0009-A	NIOTANGANJ(PG

61	WB-30		NP-7403-A	KHARAGPUR(WB)	169	ES-19	1	NP-8880-A	KISHANGANJ(PG)
62	BS-38		NR-4442-A	KISHANAGNJ(BSPTCL)	170	ES-20		NP-8888-A	KISHANGANJ(PG)
63	BS-39		NR-4445-A	KISHANAGNJ(BSPTCL)	171	ES-21		NP-8857-A	KISHANGANJ(PG)
64	BI-28		NP-8653-A	SULTANGANJ(BSPHCL)	172	EN-22		NP-7933-A	RANGPO(PG)
65	BI-29		NP-8672-A	SULTANGANJ(BSPHCL)	173	EN-23		NP-7955-A	RANGPO(PG)
66	BI-61	NP-6019-B	NP-7400-A	SULTANGANJ(BSPHCL)	174	EN-24		NP-7956-A	RANGPO(PG)
67	EN-40	N1 -0013-B	NP-7906-A	SUNDERGARH(PG)	175	EN-25		NP-7957-A	RANGPO(PG)
68	EN-41		NP-7634-A	SUNDERGARH(PG)	176	EN-33		NP-7922-A	RANGPO(PG)
69	EN-42		NP-7638-A	SUNDERGARH(PG)	177	EN-34		NP-7923-A	RANGPO(PG)
70	EN-57		NP-7907-A	SUNDERGARH(PG)	178	EN-35		NP-7924-A	RANGPO(PG)
71	EN-79		NP-7636-A	SUNDERGARH(PG)	179	EN-36		NP-7623-A	RANGPO(PG)
72	EN-95		NP-7635-A	SUNDERGARH(PG)	180	EN-39		NP-7622-A	RANGPO(PG)
73	WB-23		LT-0194-A	SAGARDIGHI(WBSETCL)	181	EN-38		NP-7621-A	RANGPO(PG)
74	WB-24		LT-0191-A	SAGARDIGHI(WBSETCL)	182	EN-54		NP-7619-A	RANGPO(PG)
75	WB-25		NP-8724-A	SAGARDIGHI(WBSETCL)	183	EN-55		NP-7620-A	RANGPO(PG)
76	WB-26		NP-8725-A	SAGARDIGHI(WBSETCL)	184	EN-59		NP-8710-A	RANGPO(PG)
77	WB-27		NP-8723-A	SAGARDIGHI(WBSETCL)	185	EN-60		NP-8711-A	RANGPO(PG)
78	WB-28		NP-8722-A	SAGARDIGHI(WBSETCL)	186	EN-80		NP-8714-A	RANGPO(PG)
79	BI-07	NP-6074-A	NP-7825-A	SABOUR(BSPHCL)	187	EN-81		NP-8715-A	RANGPO(PG)
80	BI-73		NP-8749-A	SABOUR(BSPHCL)	188	2.101		NP-7940-A	RANGPO(PG)
81	ES-31		NP-7442-A	PANDIABILI(PG)	189			NP-7941-A	RANGPO(PG)
82	ES-32		NP-7427-A	PANDIABILI(PG)	190	ES-24		NP-8712-A	RANGPO(PG)
83	ES-33		NP-7454-A	PANDIABILI(PG)	191	ES-25		NP-8713-A	RANGPO(PG)
84	ES-34		NP-7554-A	PANDIABILI(PG)	192	OR-18		NP-7944-A	SADEIPALI(GRIDCO)
85	ES-35		NP-7438-A	PANDIABILI(PG)	193	JS-11		NP-8865-A	CHAIBASA(JUVNL)
86	ES-36		NP-7407-A	PANDIABILI(PG)	194	JS-12		NP-8866-A	CHAIBASA(JUVNL)
87	ES-37		NP-7462-A	PANDIABILI(PG)	195	JS-13		NP-8867-A	CHAIBASA(JUVNL)
88	JS-50		NP-8644-A	KENDIPOSI(JUVNL)	196	SM-05		NP-8797-A	SAGBARI(SIKKIM)
89	WB-29		NP-7381-A	KHARAGPUR(WB)	197	SM-06		NP-8798-A	SAGBARI(SIKKIM)
90	BI-50		NP-7869-A	KUDRA(BSPHCL)	198	BI-42		NP-7380-A	SONNAGAR NEW(BSPTCL)
91	BI-26		NP-8697-A	LAKHISARAI(BSPHCL)	199	BI-42		NP-7450-A	SONNAGAR NEW(BSPTCL)
92	BI-30		NP-8670-A	LAKHISARAI(BSPTCL)	200	IB-01		NP-8792-A	IBEUL
93	BI-31		NP-8671-A	LAKHISARAI(BSPTCL)	201	IB-01		NP-8793-A	IBEUL
94	EN-46		NP-7432-A	LAKHISARAI(PG)	202	IB-02		NP-8795-A	IBEUL
95	EN-27		NP-7433-A	LAKHISARAI(PG)	203	IB-03		NP-8794-A	IBEUL
96	EN-37		NP-7889-A	LAKHISARAI(PG)	204	IB-05		NP-8783-A	IBEUL
97	EN-26		NP-7885-A	LAKHISARAI(PG)	205	IB-05		NP-8782-A	IBEUL
98	EN-47		NP-7886-A	LAKHISARAI(PG)	206	IB-07		NP-8784-A	IBEUL
99	EN-50		NP-7429-A	LAKHISARAI(PG)	207	IB-08		NP-8796-A	IBEUL
100	EN-51		NP-7888-A	LAKHISARAI(PG)	208	TL-32		NP-7961-A	TALCHER SOLAR(NTPC)
101	EN-58		NP-8678-A	CHAIBASA(PG)	209	TL-32		NP-7626-A	TALCHER SOLAR(NTPC)
102	EN-67		NP-8637-A	CHAIBASA(PG)	210	TL-34		NP-7962-A	TALCHER SOLAR(NTPC)
103	EN-97		NP-8868-A	CHAIBASA(PG)	211	TL-35		NP-7628-A	TALCHER SOLAR(NTPC)
104	EN-98		NP-8869-A	CHAIBASA(PG)	212	TL-37		NP-7627-A	TALCHER SOLAR(NTPC)
105	ES-29		NP-7471-A	CHAIBASA(PG)	213	TL-38		NP-5968-A	TALCHER SOLAR(NTPC)
106	ES-30		NP-7467-A	CHAIBASA(PG)	214	TL-30		NP-7909-A	TALCHER SOLAR(NTPC)
107	DM-01	<del>                                     </del>	NP-8656-A	DARBHANGA(DMTCL)	215	TL-31		NP-5979-A	TALCHER SOLAR(NTPC)
108	DM-01	<del> </del>	NP-8719-A	DARBHANGA(DMTCL)	216	TL-37	NP-7627-A	NP-7946-A	TALCHER SOLAR(NTPC)
.00	5 02	l.	07.1071	27 (1.12.17 (1.10.1 (2.11.1 0.2)	217	TL-40	NP-7618-A	NP-7945-A	TALCHER SOLAR(NTPC)
				<b>├</b>	218	TL-39	NP-7614-A	NP-7631-A	TALCHER SOLAR(NTPC)
				<b>├</b>	219	TL-41	NP-7615-A	NP-7633-A	TALCHER SOLAR(NTPC)
				+	220	TL-36	NP-7632-A	NP-7630-A	TALCHER SOLAR(NTPC)
				· ·	221	12 00	111 700271	LT-0135-A	MTPS KANTI(NTPC)
				· ·	222			LT-0192-A	MTPS KANTI(NTPC)
				<del> </del>	223			LT-0132-A	MTPS KANTI(NTPC)
				· ·	224			LT-0133-A	MTPS KANTI(NTPC)
				<b>├</b>	225			LT-0093-A	MTPS KANTI(NTPC)
				<b>├</b>	226			LT-0127-A	MTPS KANTI(NTPC)
				ļ-	227			LT-0126-A	MTPS KANTI(NTPC)
				<del> </del>	228			TP-0006-A	MTPS KANTI(NTPC)
				<del> </del>	229			LT-0132-A	MTPS KANTI(NTPC)
				<del> </del>	230			LT-0130-A	MTPS KANTI(NTPC)
				<del> </del>	231			LT-0130-A	MTPS KANTI(NTPC)
				<del> </del>	232			LT-0032-A	MTPS KANTI(NTPC)
				<b>├</b>	233			LT-0125-A	MTPS KANTI(NTPC)
				H	234			LT-0140-A	MTPS KANTI(NTPC)
				L L			<b></b>	0071	3

235

236

LT-0131-A

TP-0008-A

MTPS KANTI(NTPC)

MTPS KANTI(NTPC)

237		LT-0246-A	MTPS KANTI(NTPC)
238		LT-0219-A	MTPS KANTI(NTPC)
239		LT-0214-A	MTPS KANTI(NTPC)
240		LT-0242-A	MTPS KANTI(NTPC)
241		LT-0187-A	MTPS KANTI(NTPC)
242		LT-0215-A	MTPS KANTI(NTPC)
243	ES-54	NR-4451-A	ALIPURDUAR(PG)
244	ES-55	NR-4452-A	ALIPURDUAR(PG)
245	ES-56	NR-4457-A	ALIPURDUAR(PG)
246	ES-57	NR-4458-A	ALIPURDUAR(PG)



# List of all Energy Meters installed at various Sub Stations which has defective RS-485 communication port

Date: 19-Jan-2017

SL No	Utility	Sub Station	Meter SL No.	
1.	BSEB	Biharsharif	NP-5842-A	
2.	JSEB	Ramchandrapur	NP-5119-A	
3.	NTPC	Kahalgaon	NP-5855-A	
4.	NTPC	Talcher	NP-5081-A	
5.	PG	Rourkela	NP-5932-A	
6.	IPPR	MPL	NP-6549-A	
7.	GRIDCO	Mendhasal	NP-5980-A	
8. WBS	WBSEB	Sagardihi	NP-5072-A	
			NP-6119-A	
9.	PG	Jeypore	NP-5961-A	
10.	PG	Gaya	NP-7469-A	
			NP-7428-A	
11.	WBSEB	Kharagpur	NP-7381-A	
			NP-7403-A	
12.	DVC	DSTPP	NP-6525-A	

## Annexure- C21

#### Date of Commercial Operation(DOCO) of the Asstes

Date of Commercial Operation(DOCO) of the Assies						
Eastern Region Strengthening Scheme-XII.	DOCO	Approved Cost	Standing Committee Reference	RPC Meeting Reference	Sharing of Charges	
4 nos of 220kV GIS line bays at Kishanganj (GIS) Sub-station 20/10/16		Rs.522.29 Cr.( including IDC	2nd 2013 SCM meeting of ER		As per New Sharing	
Modification of 132kV Bus arrangement at 220/132kV Siliguri Substation with GIS bays	30/11/16	of Rs.33.24 Cr.).	on 27.08.13.	25th ERPC Meeting on 21.09.13	methodology of PoC	
Eastern Region Strengthening Scheme IX	DOCO	Approved Cost	Standing Committee Reference	RPC Meeting Reference	Sharing of Charges	
I no of 1x125 MVAR Bus Reactor(1st) and associated bay equipment at 400kV Durgapur S/S	23/10/16	Rs.196.58 Cr.( including IDC of Rs.10.65 Cr.).	SCM meeting of ER on 05.01.13.	22nd ERPC Meeting on 25.08.12 & 24th ERPC meeting on 27.04.13	As per New Sharing methodology of PoC	
1 no of 1x125 MVAR Bus Reactor(2nd) and associated bay equipment at 400kV Durgapur S/S	30/12/16					
Transmisison system for transfer of Power from generation projects in Sikkim to NR/WR(Part A)	DOCO	Approved Cost	Standing Committee Reference	RPC Meeting Reference	Sharing of Charges	
400kV 125 MVAR Bus Reactor - II with associated bays at Kishanganj (GIS) substation	09/12/16	Rs.250.03 Cr.( including IDC of Rs.19.03 Cr.).	10.09.09 & SCM of ER on 20.09.10.	15th & 16th ERPC Meeting on 28.09.10 & 18.12.10 respectively	As per New Sharing methodology of PoC	
Eastern Region Strengthening Scheme-VII	росо	Approved Cost	Standing Committee Reference	RPC Meeting Reference	Sharing of Charges	
2nos of 400kV line bays along-with 2x50 MVAR (Fixed) line reactors at 765/400kV Ranchi Substation under substation extension	17/10/16		SCM meeting of ER on 08.02.12	21st ERPC Meeting at Kolkata on 21.04.14	As per New Sharing methodology of PoC	
1x63 MVAR (Fixed) line reactor at Chaibasa under substation extension	27/10/16	Rs.71.35 Cr.( including IDC of Rs.3.96 Cr.).				
2 nos 400kV line bays at Kharagpur of West Bengal	14/11/16					
Transmisison system for transfer of Power from generation projects in Sikkim to NR/WR(Part B)	DOCO	Approved Cost	Standing Committee Reference	RPC Meeting Reference	Sharing of Charges	
LILO of one ckt of 400kV D/C Teesta III-Kishanganj line(LILO-I) at Rangpo and associated bays at Rangpo	26/11/16	Rs.1585.12 Cr.( including IDC of Rs.101.83 Cr.).	27th SCM meeting of NR on 30.05.09 & 29th SCM of WR on 16.09.09.	16th ERPC Meeting on 18.12.10	As per New Sharing methodology of PoC	
Eastern Region Strengthening Schemo₌V	DOCO	Approved Cost	Standing Committee Reference	RPC Meeting Reference	Sharing of Charges	
2 nos of 400kV line bays for termination of LILO of 2nd circuit of Jamshedpur-Rourkela 400kV line at Chaibasa Substation	22/11/16	Rs.71.35 Cr.( including IDC of Rs.3.96 Cr.).	SCM meeting of ER on 08.02.12	21st ERPC Meeting at Kolkata on 21.04.14	As per New Sharing methodology of PoC	
Eastern Region Strengthening Scheme-III	DOCO	Approved Cost	Standing Committee Reference	RPC Meeting Reference	Sharing of Charges	
LILO of 400kV D/C Baripada-Mendhasal line and associated bays at Pandiabili GIS	31/07/16					
1 no 500 MVA, 3 phase 400/220kV , Transformer and associated bays at Pandiabili GIS	31/07/16	Rs. 1512.08 Cr. (including IDC of Rs. 96.92 Cr.).	08/11/2008 at Bhubaneswar	Special(9th.) ERPC meeting on 30/12/2008 & 10th ERPC meeting on 11/04/2009 at Port Blair	As per New Sharing methodology of PoC	
1 no 80 MVAR , 400kV Bus Reactor and associated bays at Pandiabili GIS	31/07/16					
02 nos 63 MVAR, 400kV Switchable Line Reactor both shifted from Mendhasal(as Fixed Line Reactor) with associated bays at Pandiabili GIS	31/07/16					
6 nos 220kV line bays at Pandiabili GIS	31/07/16					
	4 nos of 220kV GIS line bays at Kishanganj (GIS) Sub-station  Modification of 132kV Bus arrangement at 220/132kV Siliguri Substation with GIS bays  Eastern Region Strengthening Scheme-IX  1 no of 1x125 MVAR Bus Reactor(1st) and associated bay equipment at 400kV Durgapur S/S  T no of 1x125 MVAR Bus Reactor(2nd) and associated bay equipment at 400kV Durgapur S/S  Transmisison system for transfer of Power from generation projects in Sikkim to NR/WR(Part A)  400kV 125 MVAR Bus Reactor - II with associated bays at Kishanganj (GIS) substation  Eastern Region Strengthening Scheme-VII  2nos of 400kV line bays along-with 2x50 MVAR (Fixed) line reactors at 765/400kV Ranchi Substation under substation extension  1x63 MVAR (Fixed) line reactor at Chaibasa under substation extension  2 nos 400kV line bays at Kharagpur of West Bengal  Transmission system for transfer of Power from generation projects in Sikkim to NR/WR(Part B)  LILO of one ckt of 400kV D/C Teesta III-Kishanganj line(LILO-I) at Rangpo and associated bays at Rangpo  Eastern Region Strengthening Scheme-VII  2 nos of 400kV line bays for termination of LILO of 2nd circuit of Jamshedpur-Rourkela 400kV line at Chaibasa Substation  Eastern Region Strengthening Scheme-III  LILO of 400kV D/C Baripada-Mendhasal line and associated bays at Pandiabili GIS  1 no 500 MVA, 3 phase 400/220kV , Transformer and associated bays at Pandiabili GIS  1 no 80 MVAR , 400kV Bus Reactor and associated bays at Pandiabili GIS  20 nos 63 MVAR , 400kV Bus Reactor and associated bays at Pandiabili GIS	4 nos of 220kV GIS line bays at Kishanganj (GIS) Sub-station  20/10/16  Modification of 132kV Bus arrangement at 220/132kV Siliguri Substation with GIS bays  Eastern Region Strengthening Scheme-IX  DOCO  1 no of 1x125 MVAR Bus Reactor(1st) and associated bay equipment at 400kV Durgapur S/S  1 no of 1x125 MVAR Bus Reactor(2nd) and associated bay equipment at 400kV Durgapur S/S  Transmisison system for transfer of Power from generation projects in Silkkim to NR/WRPart A)  400kV 125 MVAR Bus Reactor - II with associated bays at Kishanganj (GIS)  ubstation  Eastern Region Strengthening Scheme-VII  DOCO  2nos of 400kV line bays along-with 2x50 MVAR (Fixed) line reactors at 765/400kV Ranchi Substation under substation extension  17/10/16  1x63 MVAR (Fixed) line reactor at Chaibasa under substation extension  27/10/16  Transmisison system for transfer of Power from generation projects in Silkkim to NR/WRPart B)  DOCO  LILO of one ckt of 400kV D/C Teesta III-Kishanganj line(LILO-I) at Rangpo and associated bays at Rangpo  Eastern Region Strengthening Scheme-V  DOCO  2 nos of 400kV line bays for termination of LILO of 2nd circuit of Jamshedpur-Rourkela 400kV line at Chaibasa Substation  Eastern Region Strengthening Scheme-V  DOCO  2 nos of 400kV D/C Baripada-Mendhasal line and associated bays at Pandiabili GIS  1 no 500 MVAR, 400kV Bus Reactor and associated bays at Pandiabili GIS  1 no 80 MVAR, 400kV Switchable Line Reactor both shifted from Mendhasal(as Fixed Line Reactor) with associated bays at Pandiabili GIS	4 nos of 220kV GIS line bays at Kishanganj (GIS) Sub-station  Modification of 132kV Bus arrangement at 220/132kV Siligari Substation with GIS bays  Fastern Region Strengthening Scheme-IX  DOCO  Approved Cost  In on of 1x125 MVAR Bus Reactor(1st) and associated bay equipment at 400kV Durgapur SIS  In on of 1x125 MVAR Bus Reactor(2nd) and associated bay equipment at 400kV Durgapur SIS  Transmision system for transfer of Power from generation projects in Sikkin to NR/WR/Part A)  400kV 125 MVAR Bus Reactor - II with associated bays at Kishanganj (GIS)  substitution  Bastern Region Strengthening Scheme-VII  DOCO  Approved Cost  Res. 25.0.03 Cr. (including IDC of Rs. 19.03 Cr.).  Eastern Region Strengthening Scheme-VII  DOCO  Approved Cost  17/10/16  Res. 71.35 Cr. (including IDC of Rs. 19.03 Cr.).  Lik 3 MVAR (Fixed) line reactor at Chaibasa under substation extension  27/10/16  Transmision system for transfer of Power from generation projects in Sikkin to NR/WR/Part B)  Lik 3 MVAR (Fixed) line reactor at Chaibasa under substation extension  27/10/16  Transmision system for transfer of Power from generation projects in Sikkin to NR/WR/Part B)  Lik 0 of one ckt of 400kV Dr. Teesta Ill-Kishanganj line(LILO4) at Rangpo and associated bays at Rangpo  Res. 71.35 Cr. (including IDC of Rs. 10.83 Cr.).  Eastern Region Strengthening Scheme-V  DOCO  Approved Cost  Res. 71.35 Cr. (including IDC of Rs. 10.83 Cr.).  Eastern Region Strengthening Scheme-V  DOCO  Approved Cost  Res. 71.35 Cr. (including IDC of Rs. 10.83 Cr.)  Eastern Region Strengthening Scheme-VIII  DOCO  Approved Cost  Res. 71.35 Cr. (including IDC of Rs. 3.96 Cr.).  Eastern Region Strengthening Scheme-III  DOCO  Approved Cost  III. On 400kV Dr. Baripada-Mendhasal line and associated bays at Pandiabili GIS  Res. 1512.08 Cr. (including IDC of Rs. 3.96 Cr.).  Res. 1512.08 Cr. (including IDC of Rs. 96.92 Cr.).	A nos of 220kV GIS line boys at Kishanganj (GIS) Sub-station  201016  Res 522.29 Cr. (nichding IDC GIS Sub-station)  201016  Res 522.29 Cr. (nichding IDC GIS Sub-station)  201116  Res 1228 MVAR Bus Reactor(1st) and associated bay equipment at 400kV Drappur SS  1 mo of 11228 MVAR Bus Reactor(2nd) and associated bay equipment at 400kV Drappur SS  Transmission system for transfer of Power from generation projects in Station in NEW REPart 3, 100 CO  Approved Cost  Standing Committee Reference  825.003 Cr. (nichding IDC GIS SUb-station)  201216  Res 250.03 Cr.	# now of 220kk V GR line beys at Kishangan (GRS) Substation    # now of 220kV GR line beys at Kishangan (GRS) Substation    # now of 220kV GR line beys at Kishangan (GRS) Substation    ## Note of 132kV Bas arrangement at 200132kV Siligari Substation with    ## Substation (Committee Medicates of 132kV Bas arrangement at 200132kV Siligari Substation with    ## DOCO	
